


# Cathedral Commons



## Preliminary Draft Site Use and Sequence Plan

Updated on:  
08/15/2012

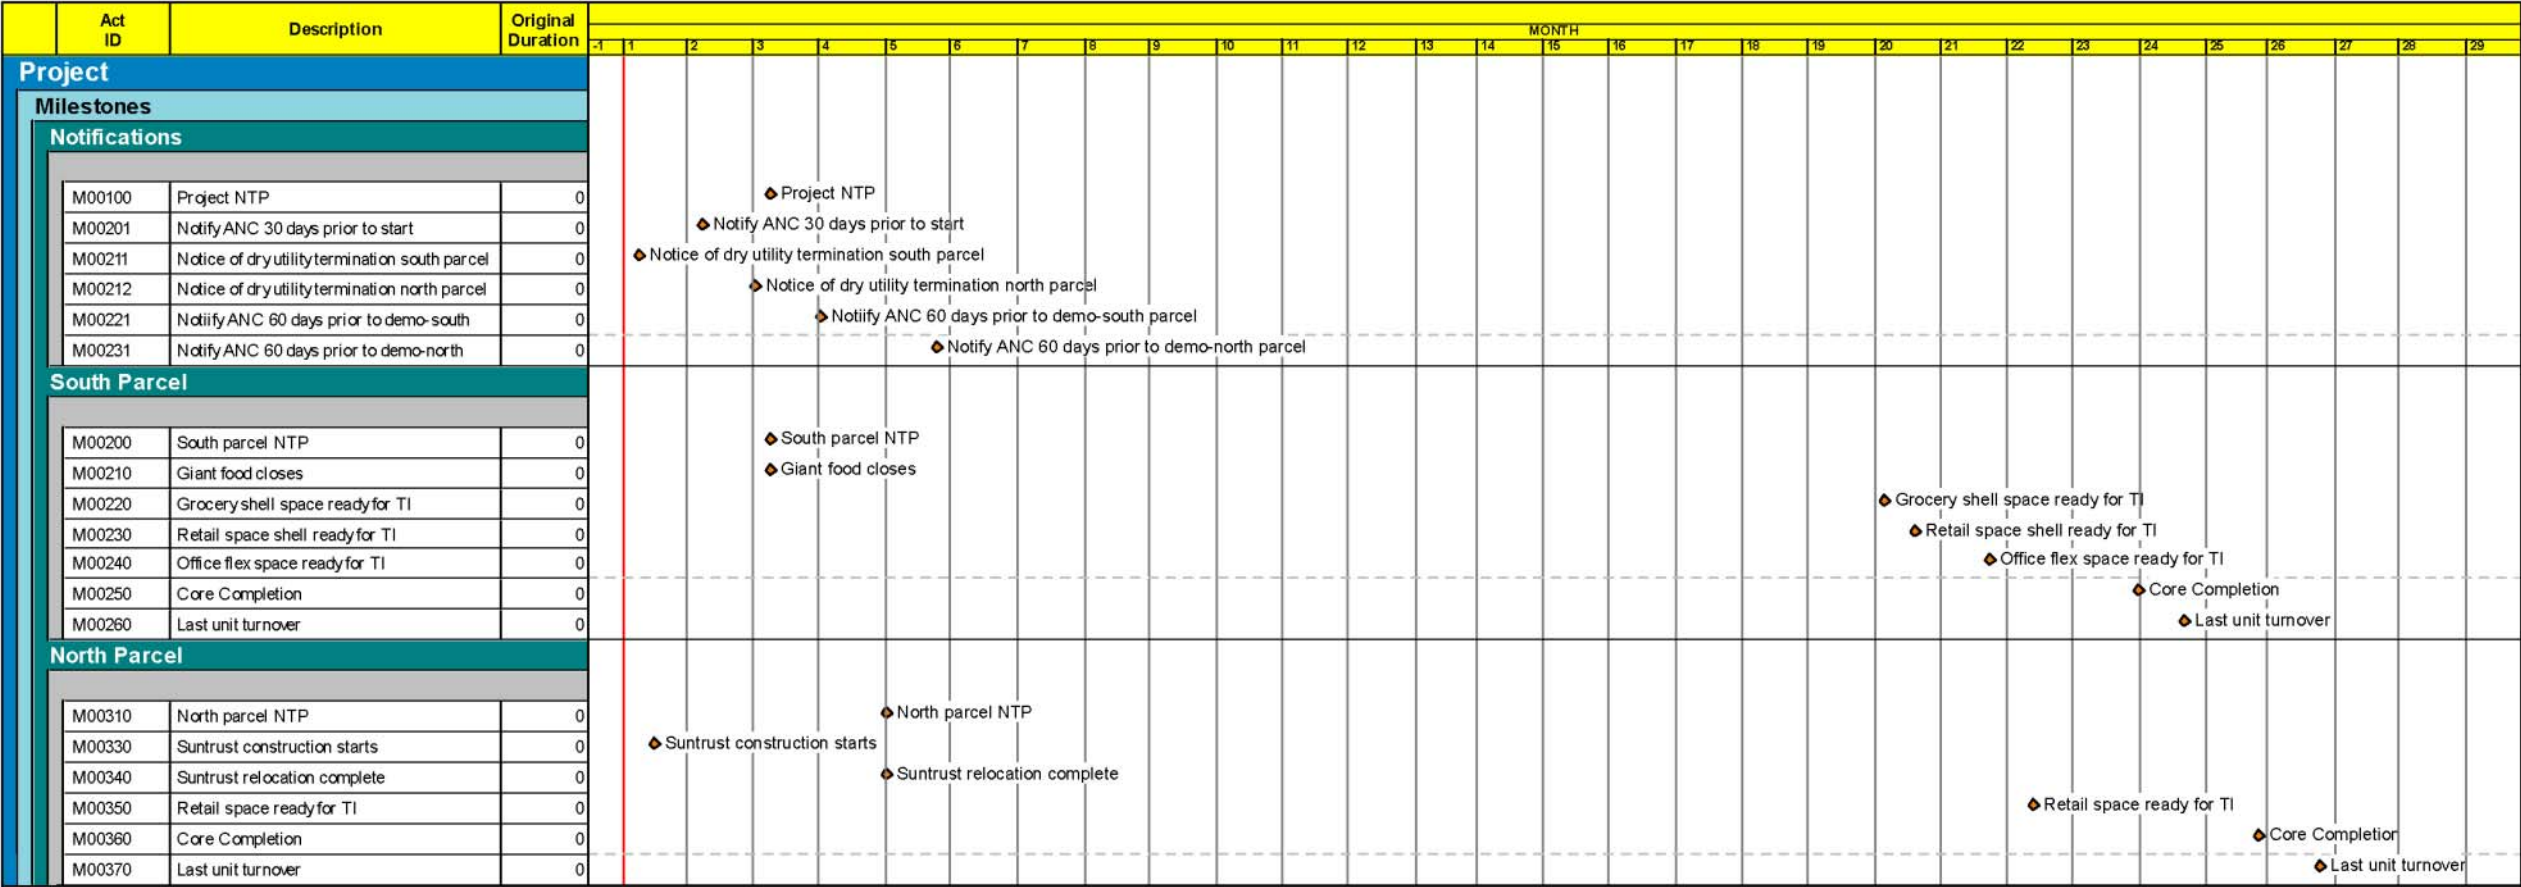

Start date	01FEB12
Finish date	24MAR14
Data date	01FEB12
Run date	20MAR12
Page number	1A
© Primavera Systems, Inc.	

Bozzuto Construction Company  
Cathedral Commons - Draft  
Preliminary Construction Schedule

- Early bar
- Progress bar
- Critical bar
- Summary bar
- Start milestone point
- Finish milestone point






Start date	01FEB12
Finish date	24MAR14
Data date	01FEB12
Run date	20MAR12
Page number	2A
© Primavera Systems, Inc.	

Bozzuto Construction Company  
Cathedral Commons - Draft  
Preliminary Construction Schedule


- Early bar
- Progress bar
- Critical bar
- Summary bar
- Start milestone point
- Finish milestone point

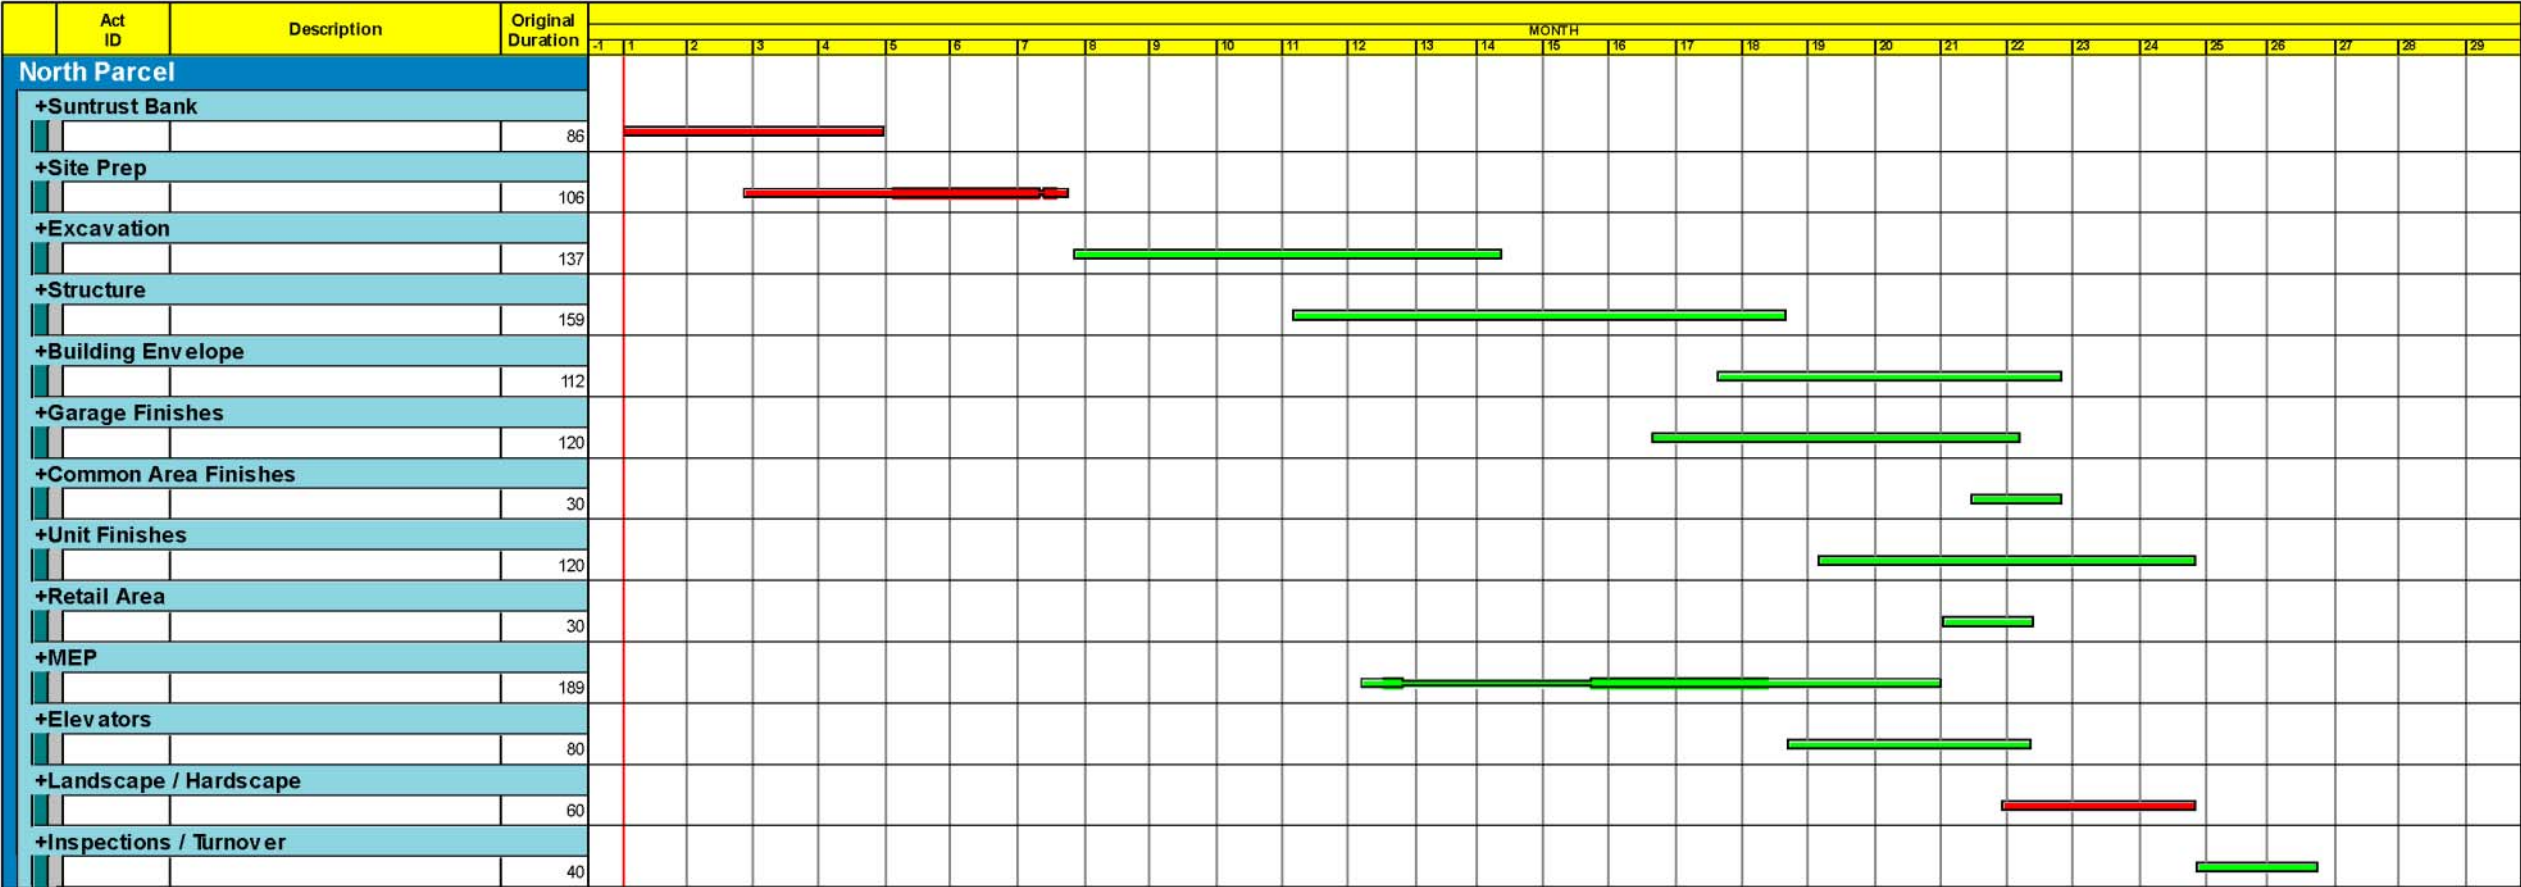

Start date	01FEB12
Finish date	24MAR14
Data date	01FEB12
Run date	20MAR12
Page number	3A
© Primavera Systems, Inc.	

Bozzuto Construction Company  
Cathedral Commons - Draft  
Preliminary Construction Schedule

- Early bar
- Progress bar
- Critical bar
- Summary bar
- Start milestone point
- Finish milestone point

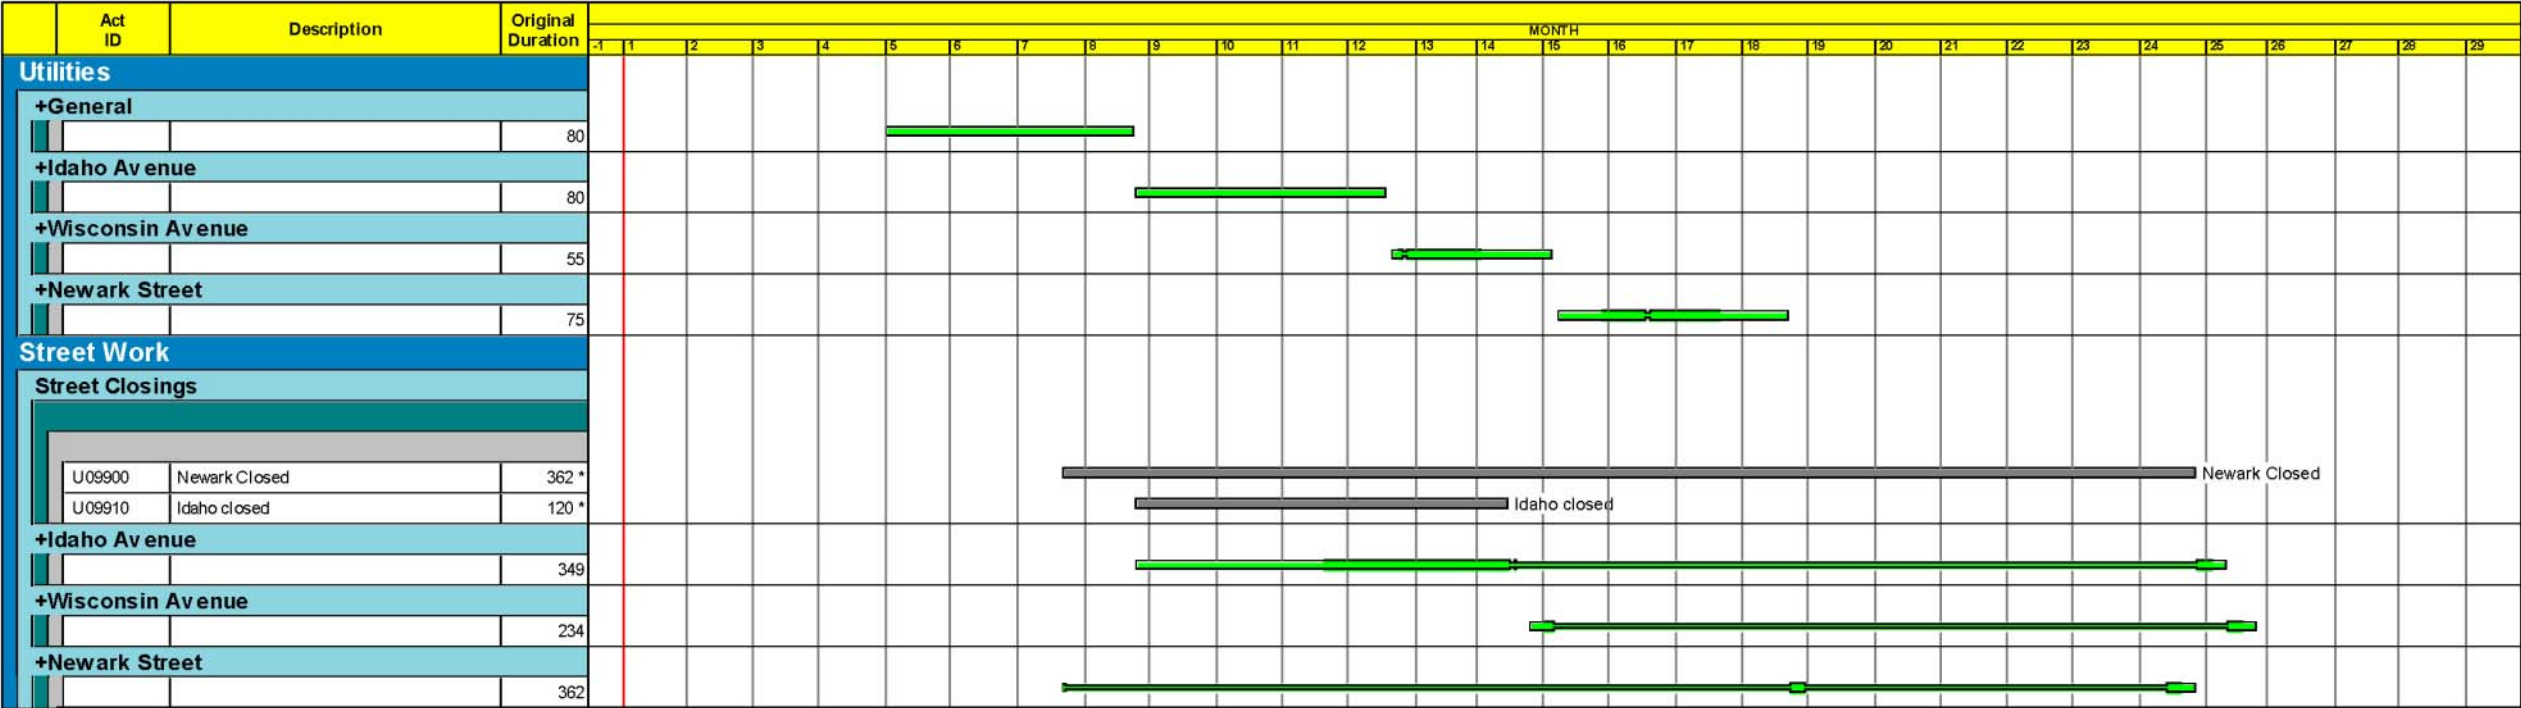

Start date	01FEB12
Finish date	24MAR14
Data date	01FEB12
Run date	20MAR12
Page number	4A
© Primavera Systems, Inc.	

Bozzuto Construction Company  
Cathedral Commons - Draft  
Preliminary Construction Schedule


- Early bar
- Progress bar
- Critical bar
- Summary bar
- Start milestone point
- Finish milestone point

# Cathedral Commons Draft - Site Utilization

Project Mobilization

Demolition

Month 1 to 5

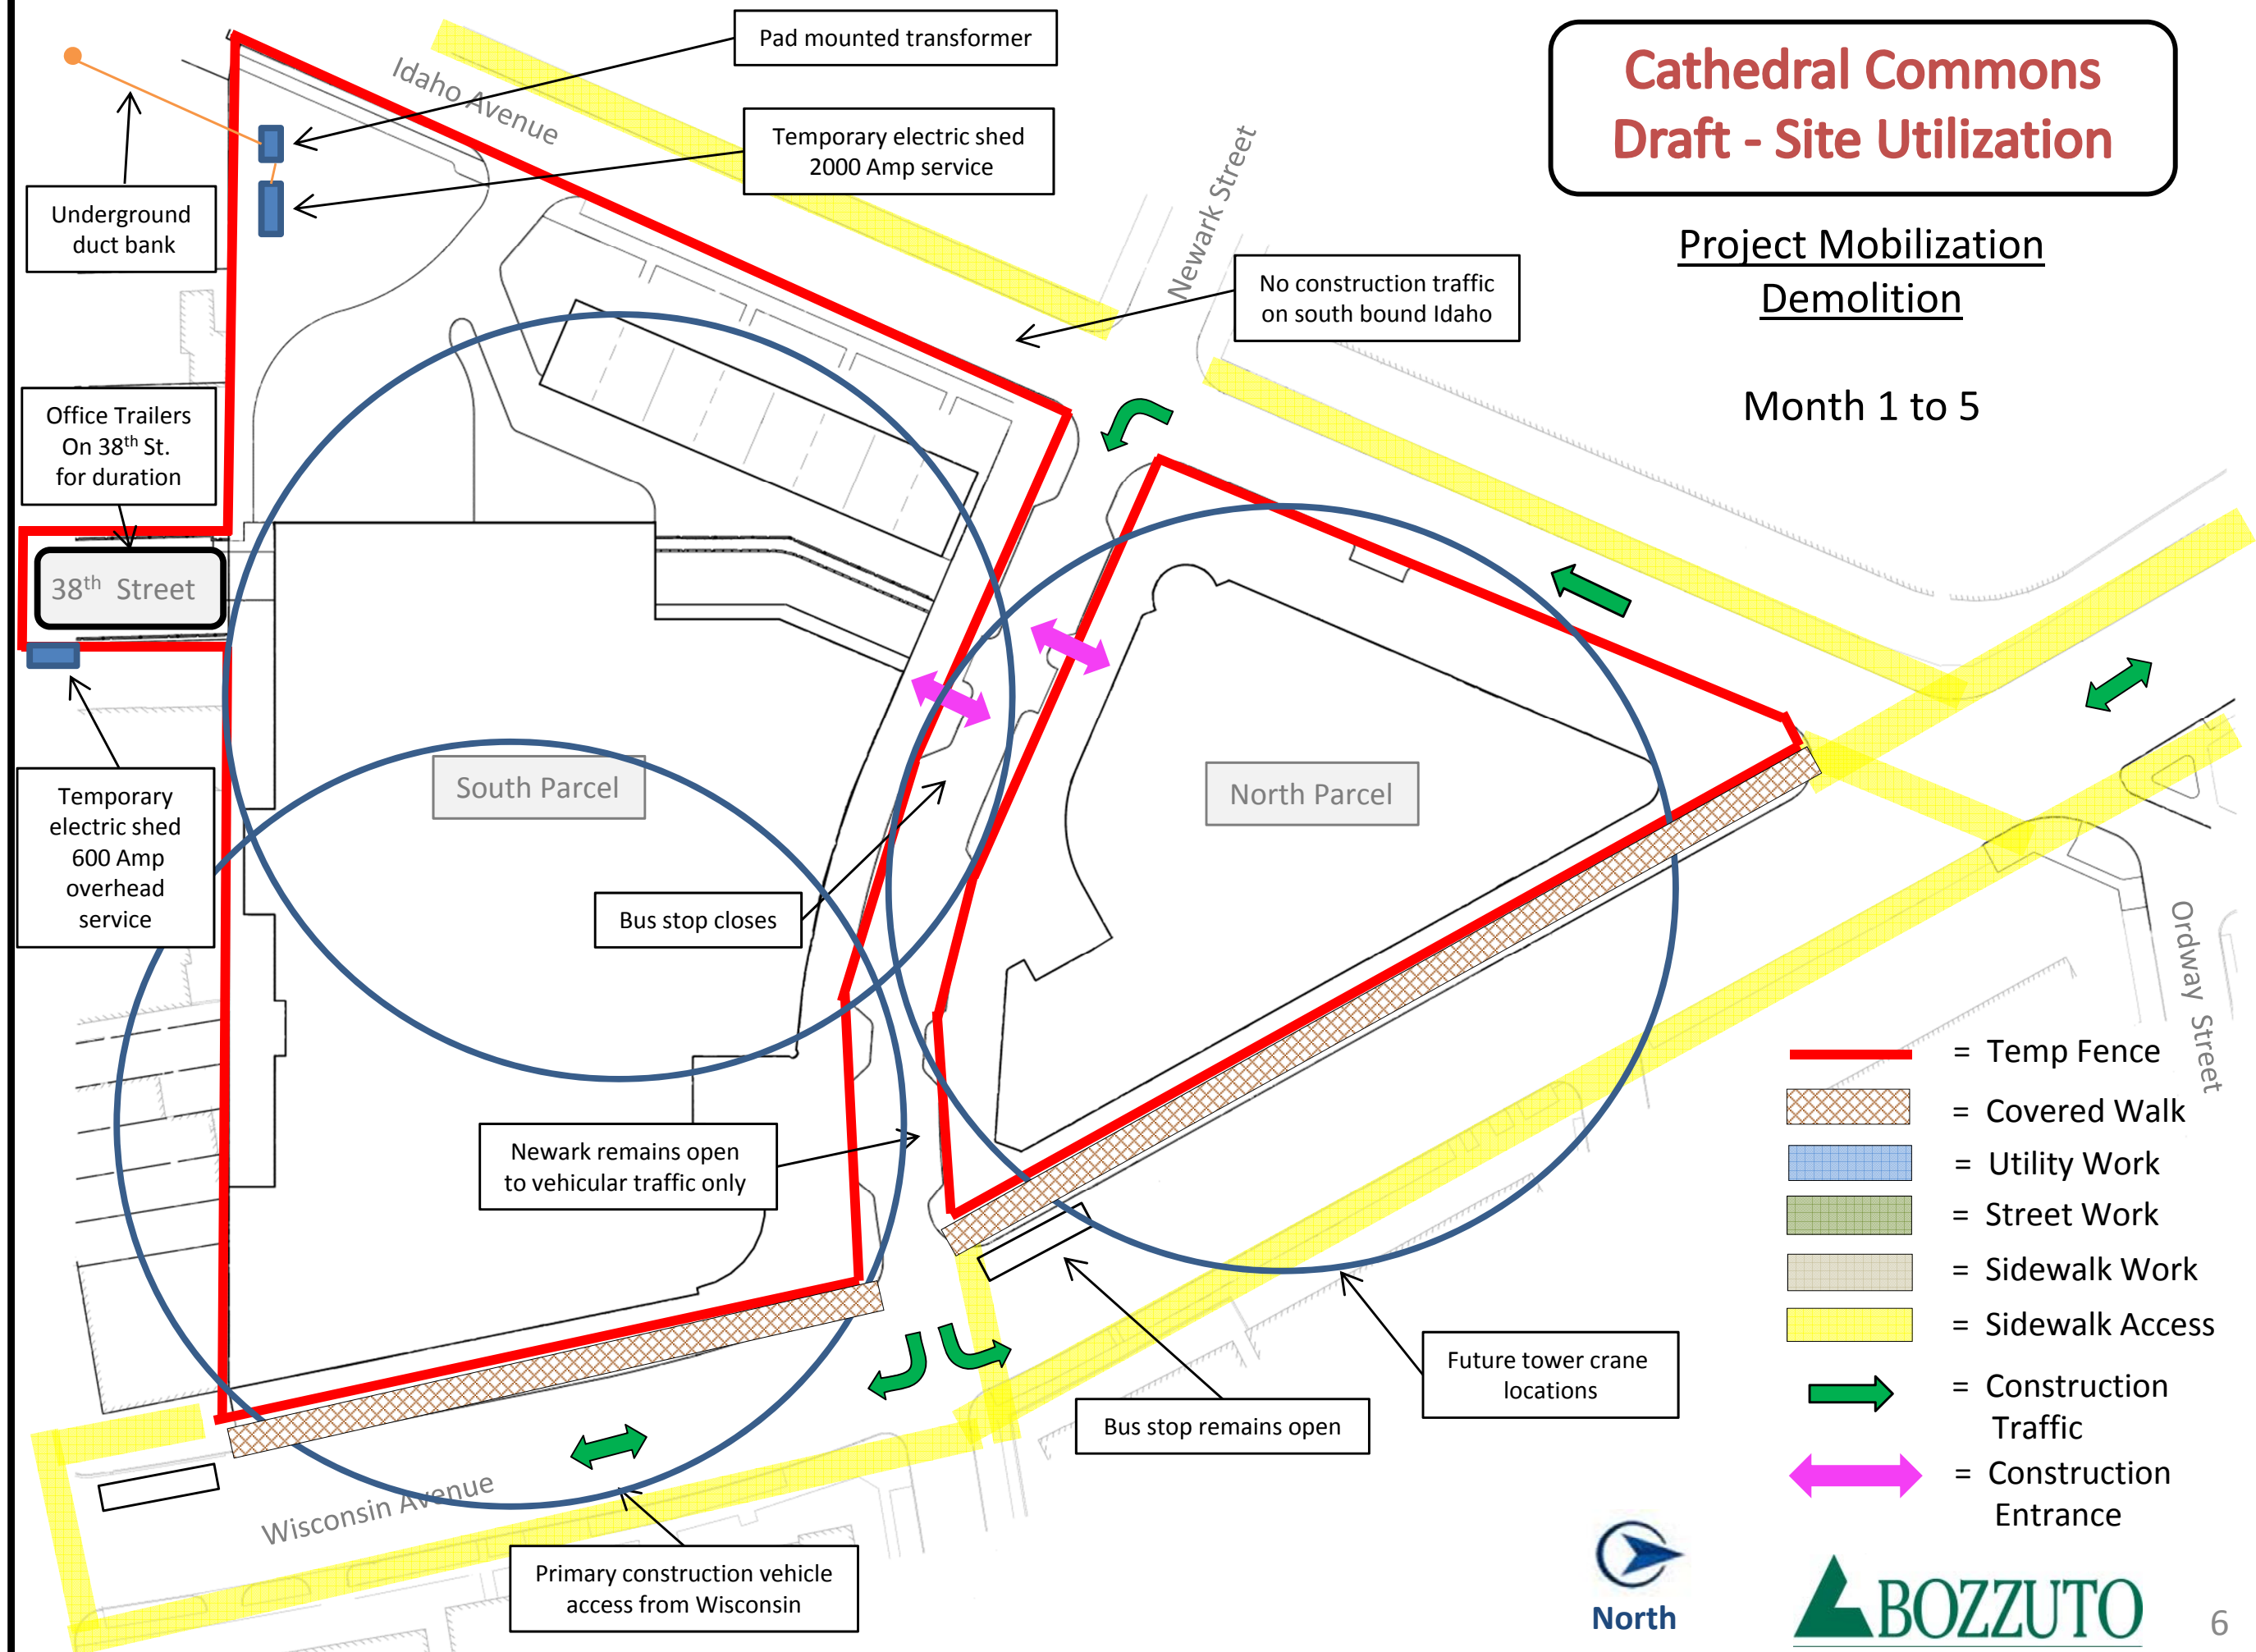




# Cathedral Commons Draft - Site Utilization

Building Excavation  
South Idaho Ave. Closed – Utility Work  
Newark St. Closed for Duration

Month 6 to 7

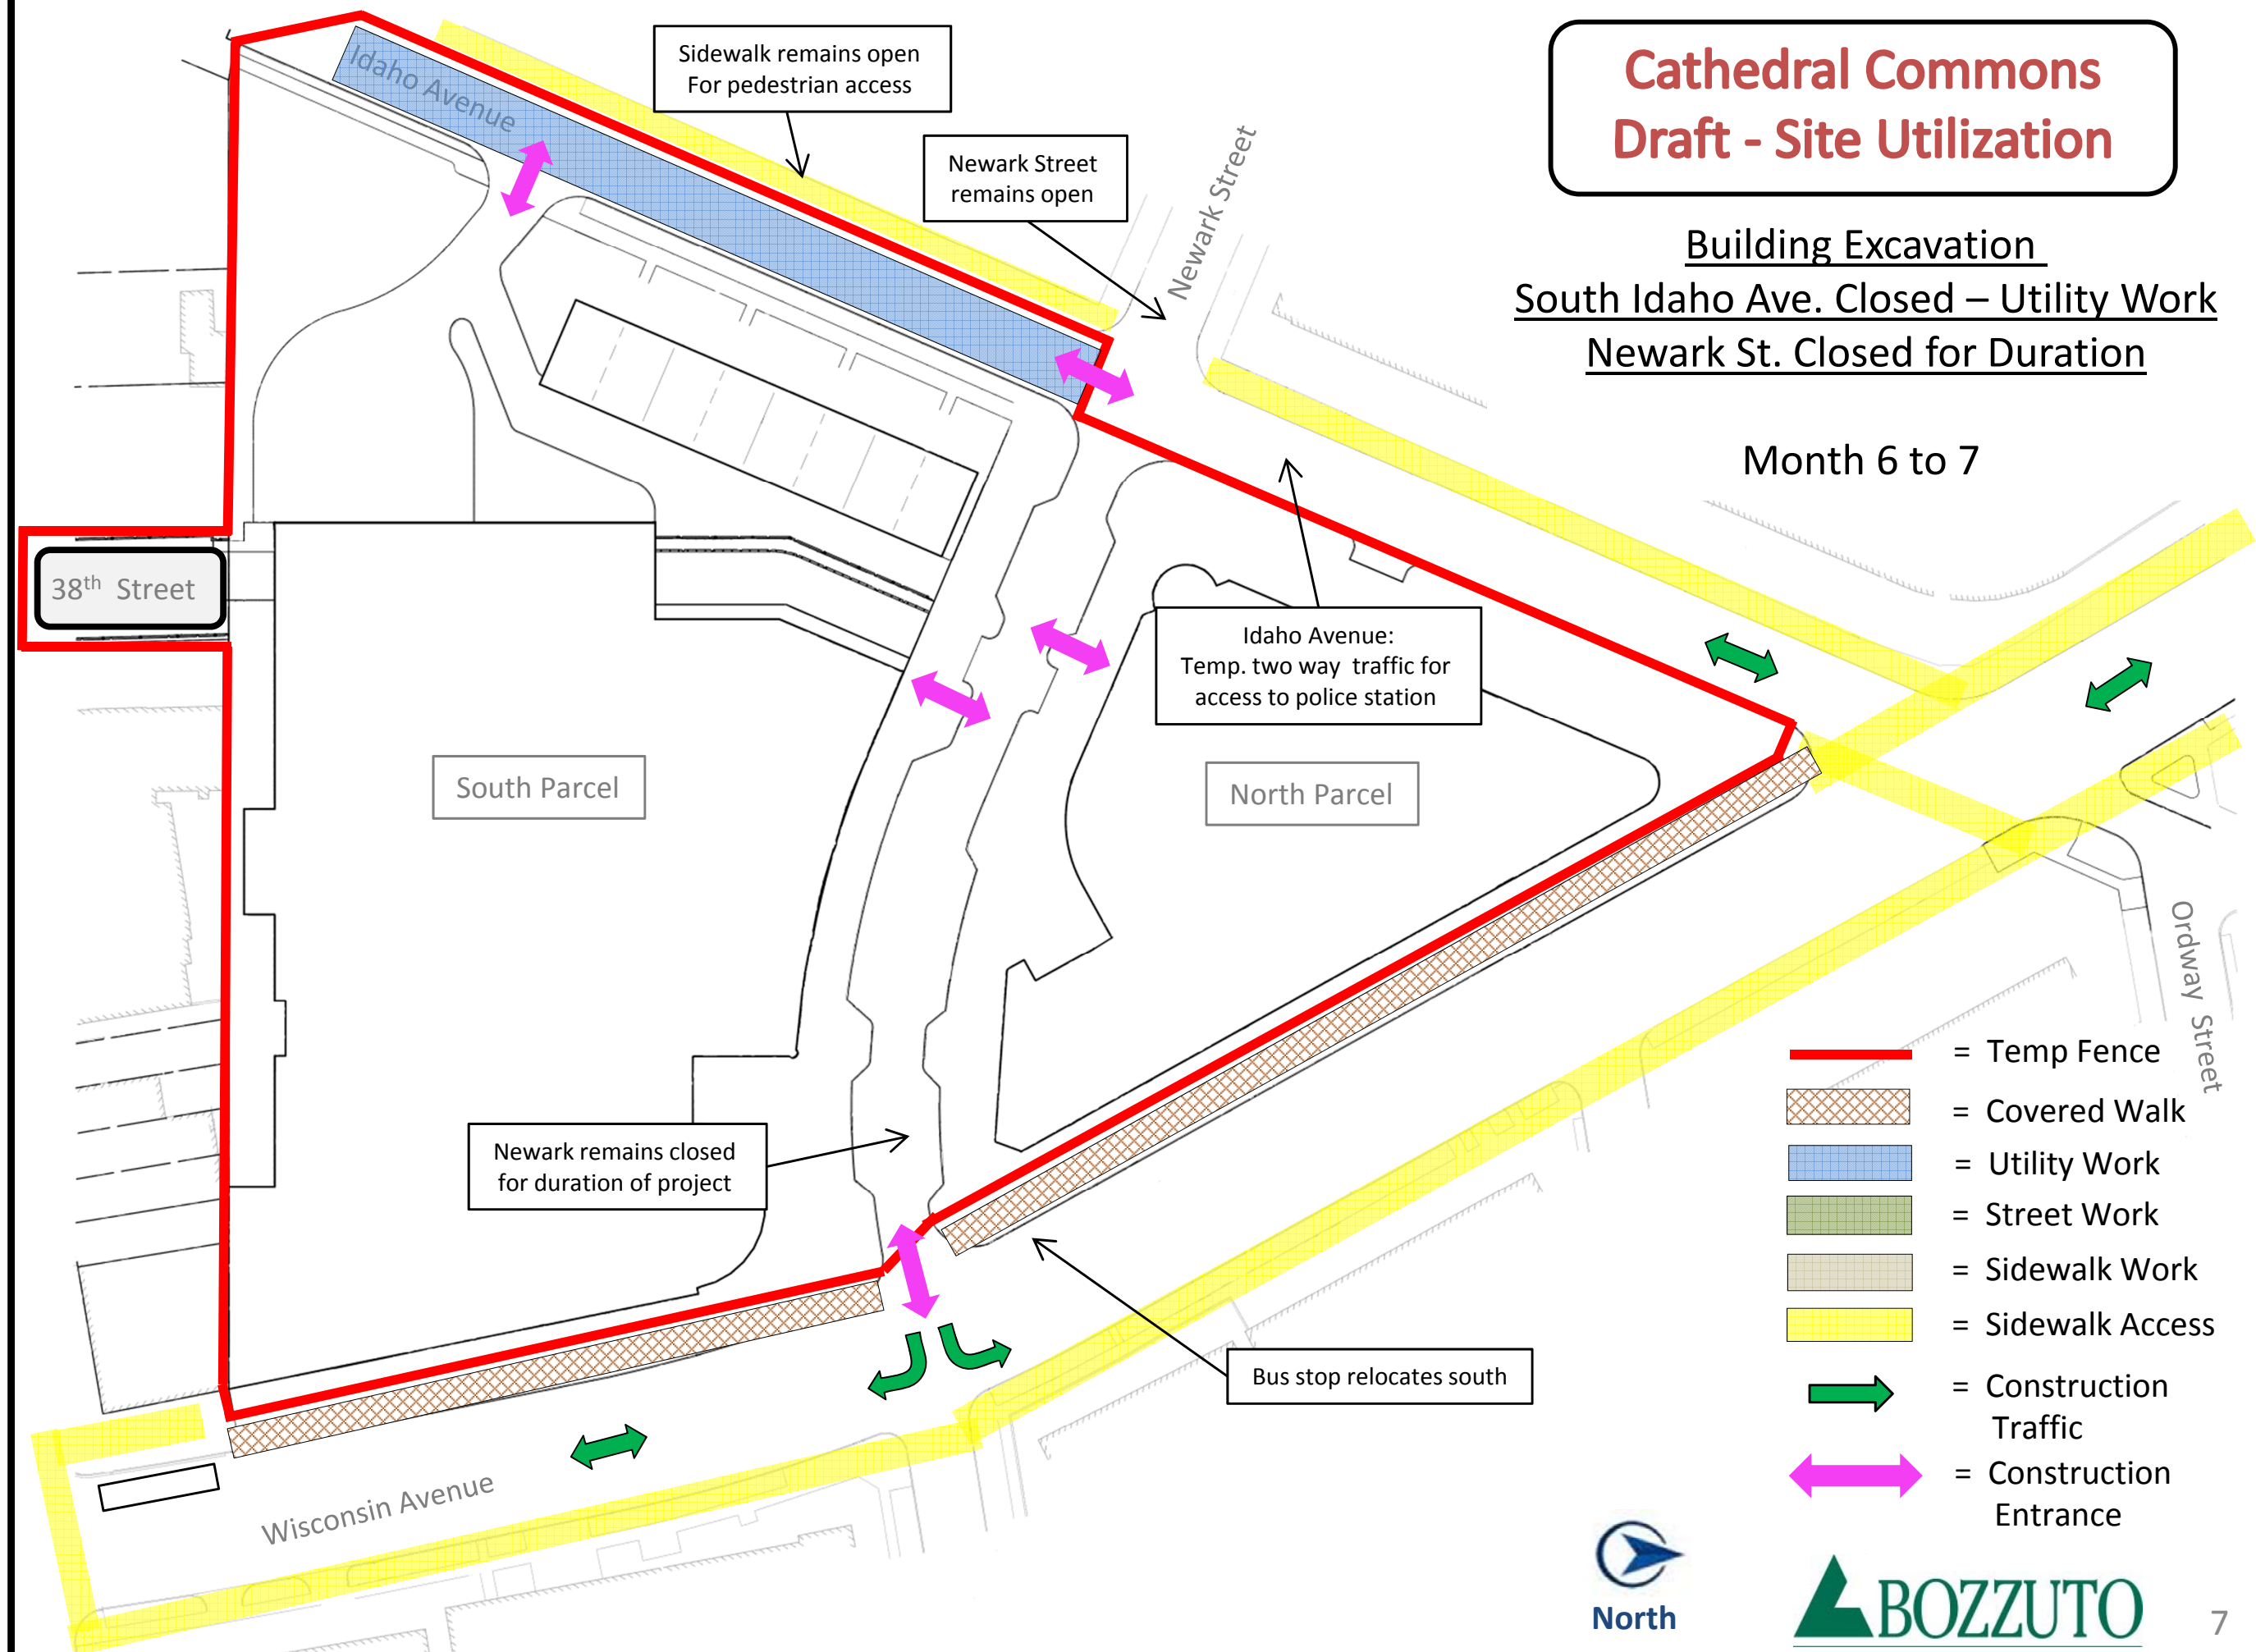


- = Temp Fence
- = Covered Walk
- = Utility Work
- = Street Work
- = Sidewalk Work
- = Sidewalk Access
- = Construction Traffic
- = Construction Entrance



# Cathedral Commons Draft - Site Utilization

Building Excavation  
North Idaho Ave. Closed – Utility Work  
Newark St. Closed for Duration  
New Traffic Signal Work

Month 8 to 9

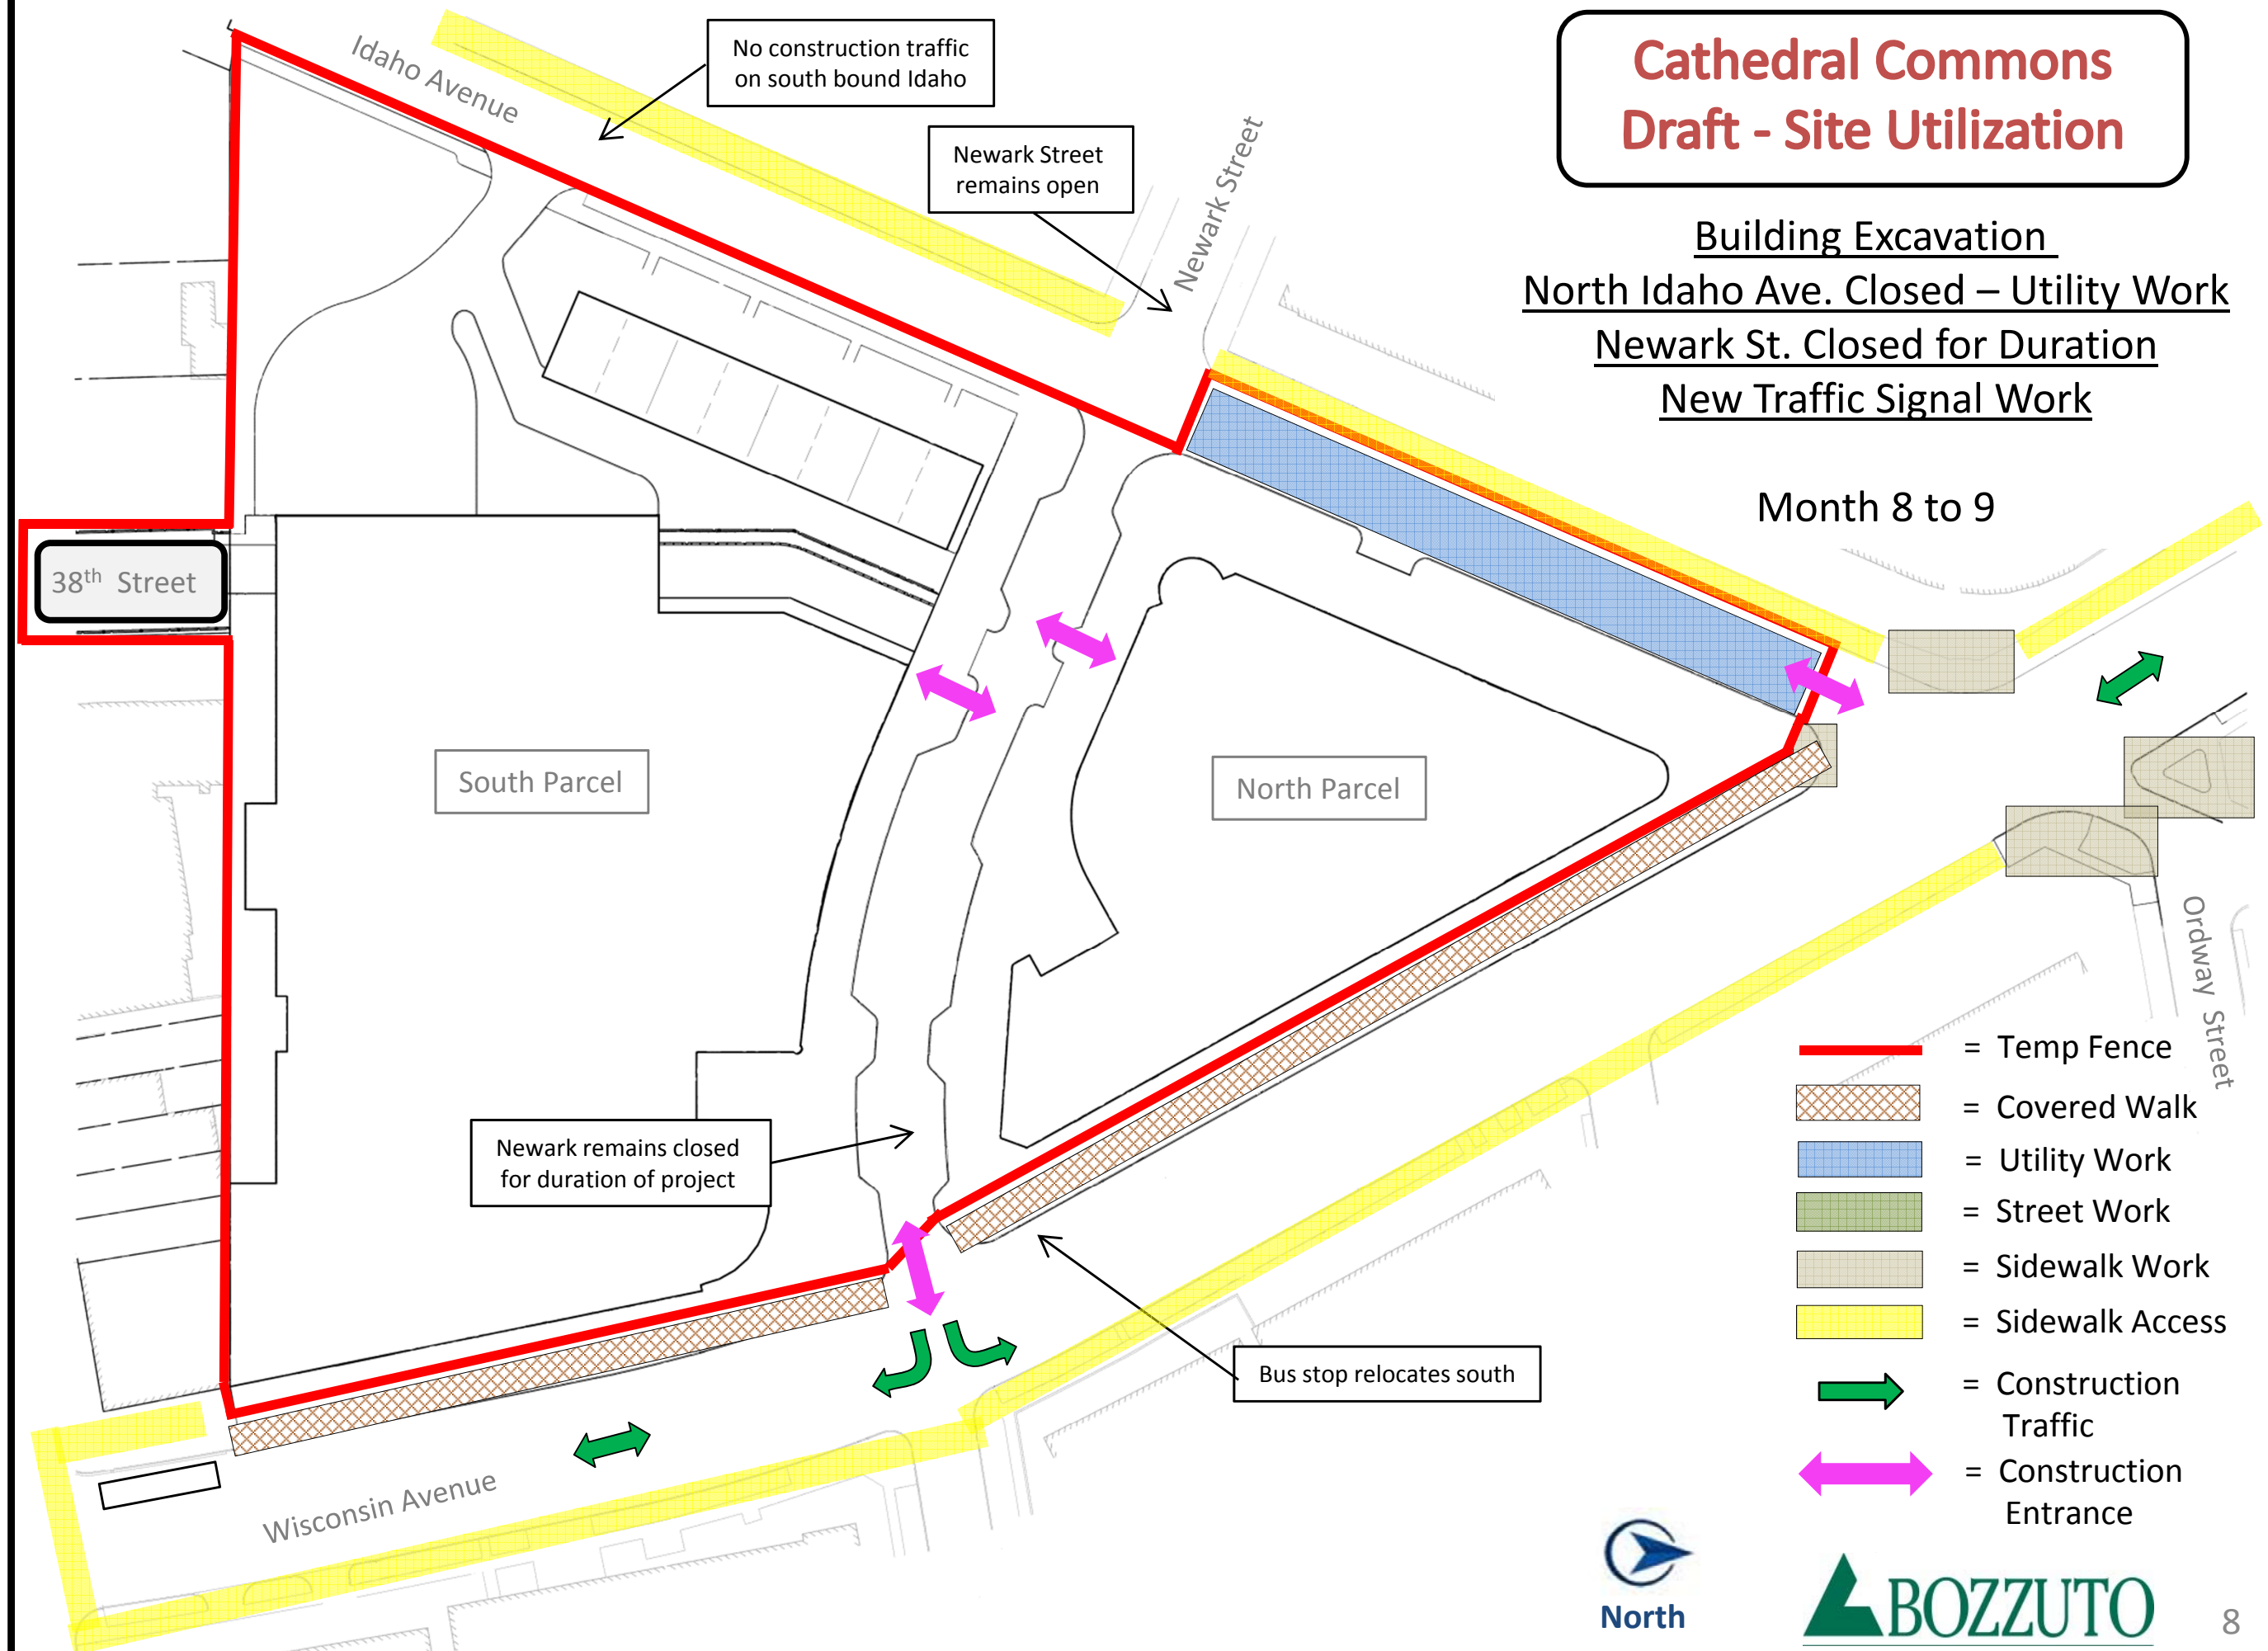



# Cathedral Commons Draft - Site Utilization


## Building Structure

South Idaho Ave. Closed - Street Work

Wisconsin Ave. Utility Work ([see detail](#))

New Traffic Signal Work

Month 9 to 10

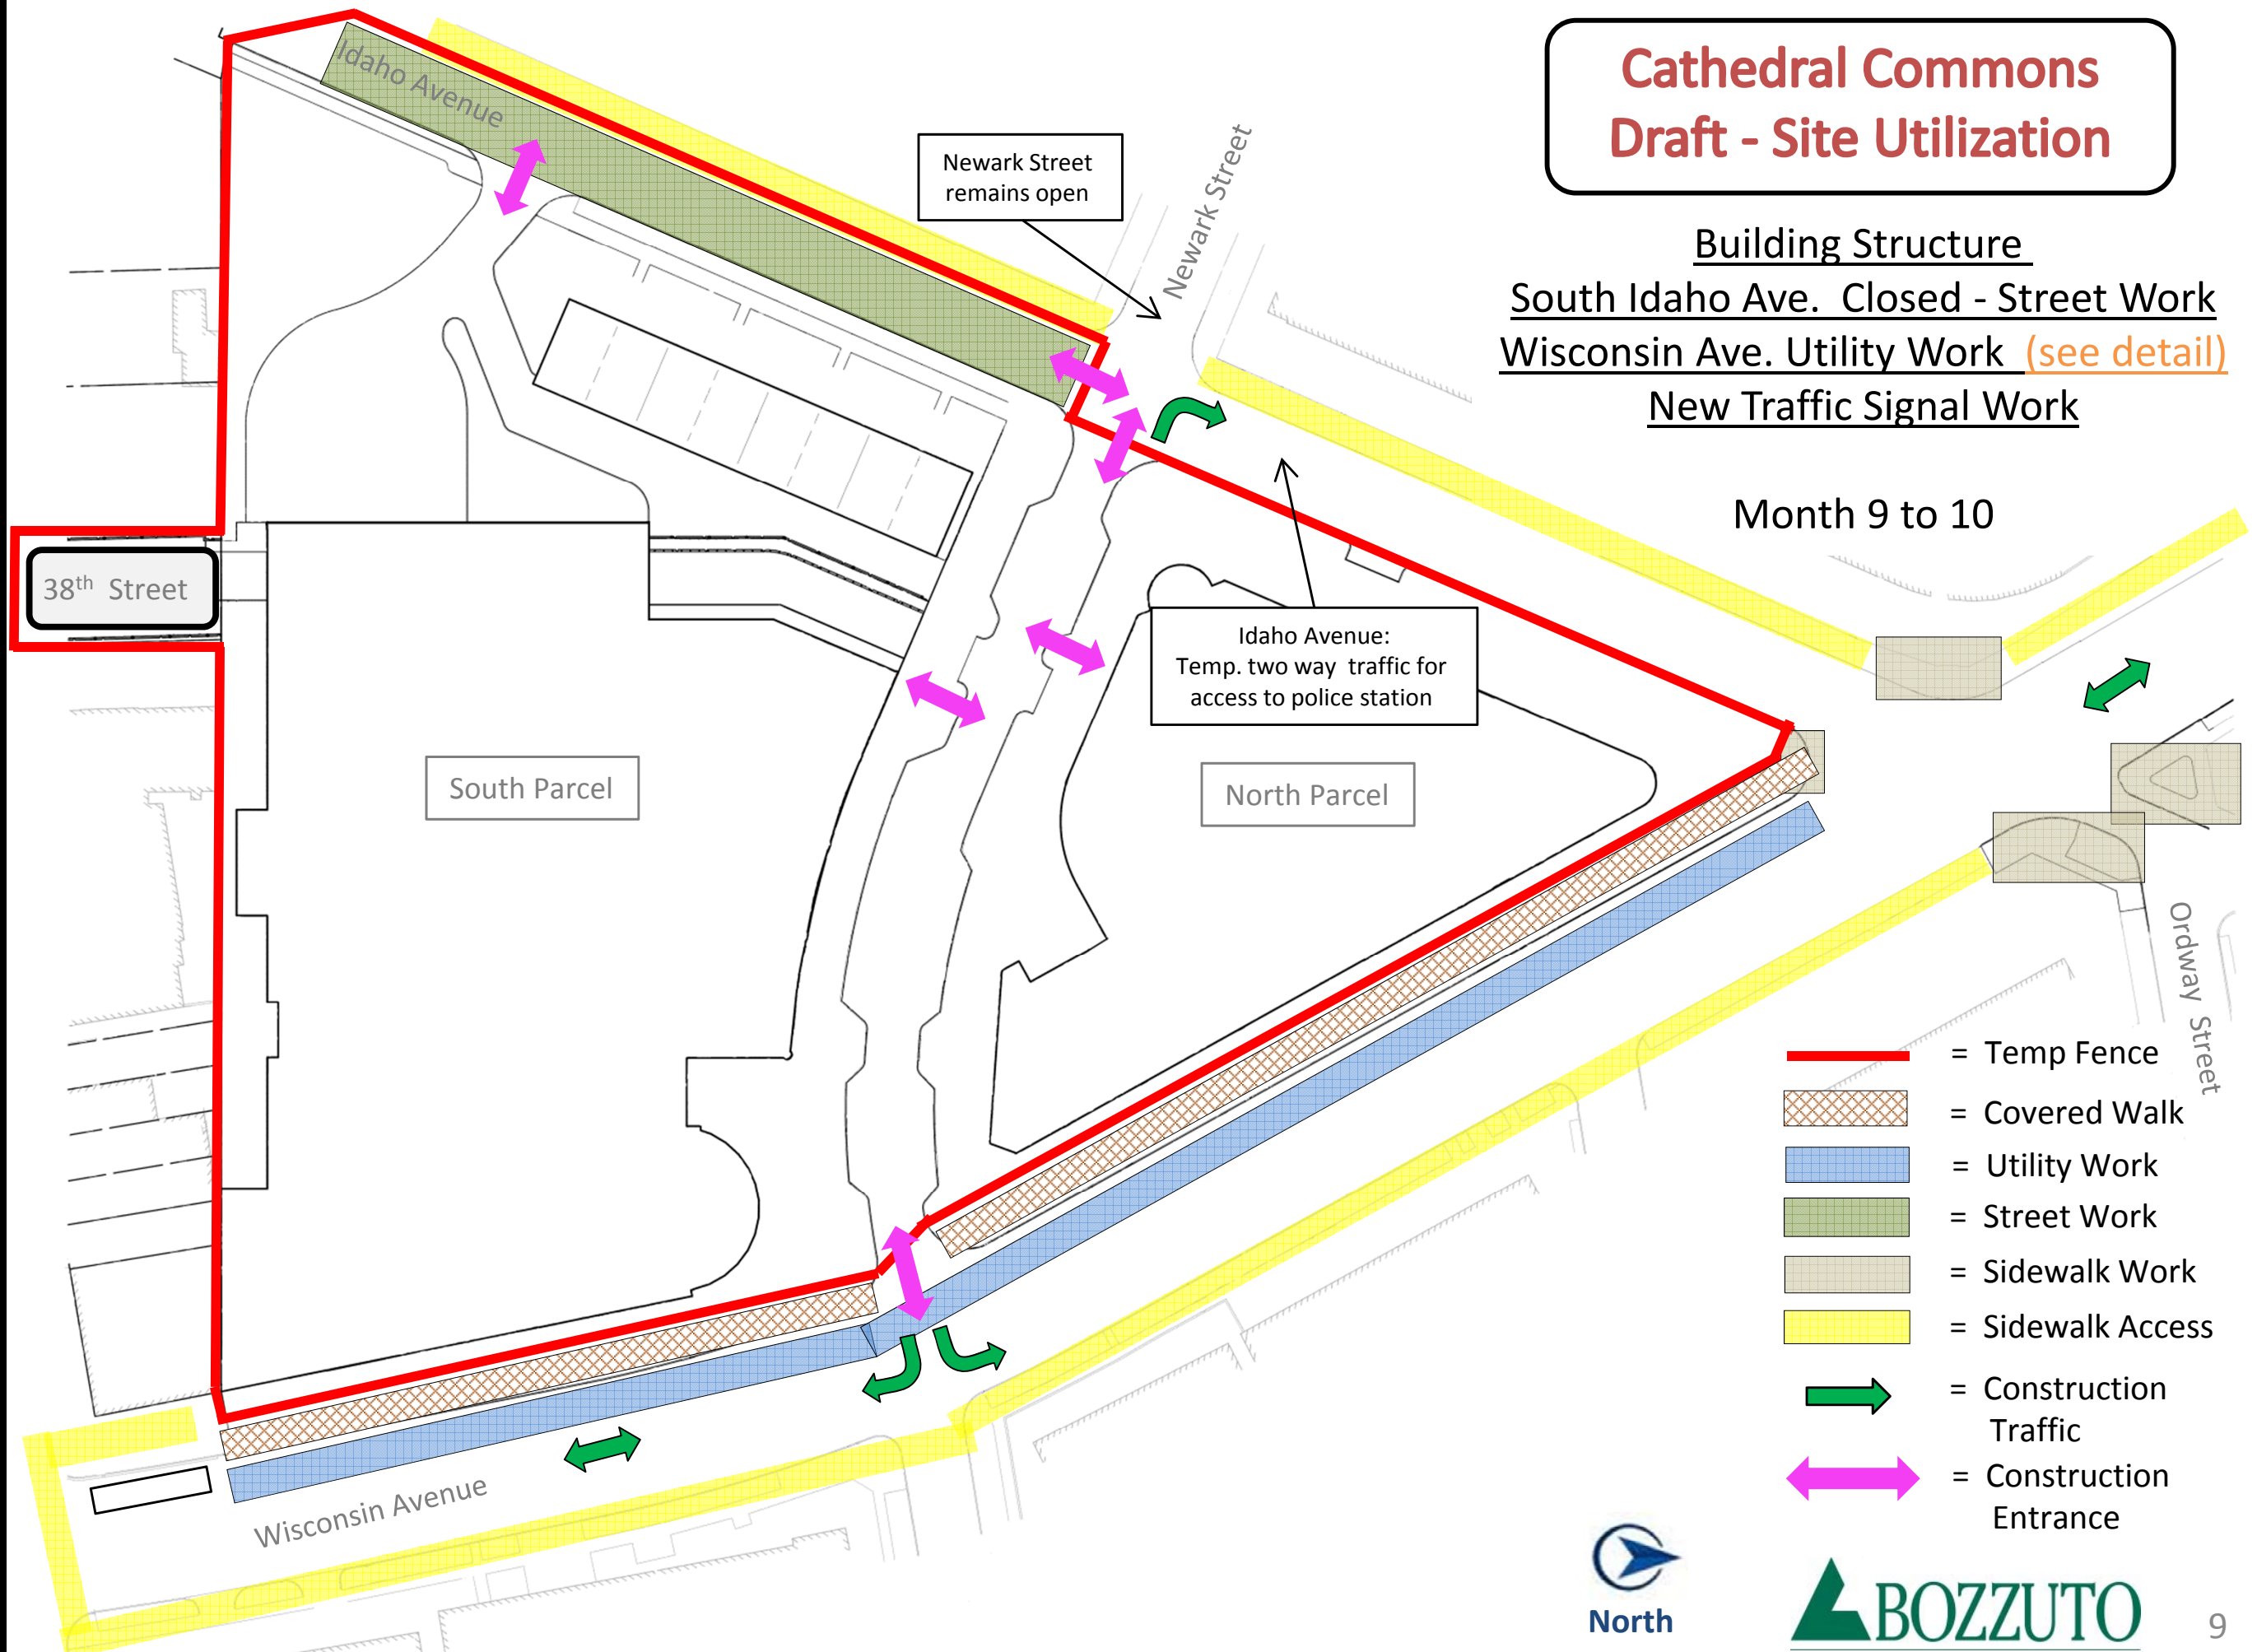

# Cathedral Commons Draft - Site Utilization


## Building Structure

North Idaho Ave. Closed - Street Work

Wisconsin Ave. Utility Work (see detail)

New Traffic Signal Work

Month 10 to 11

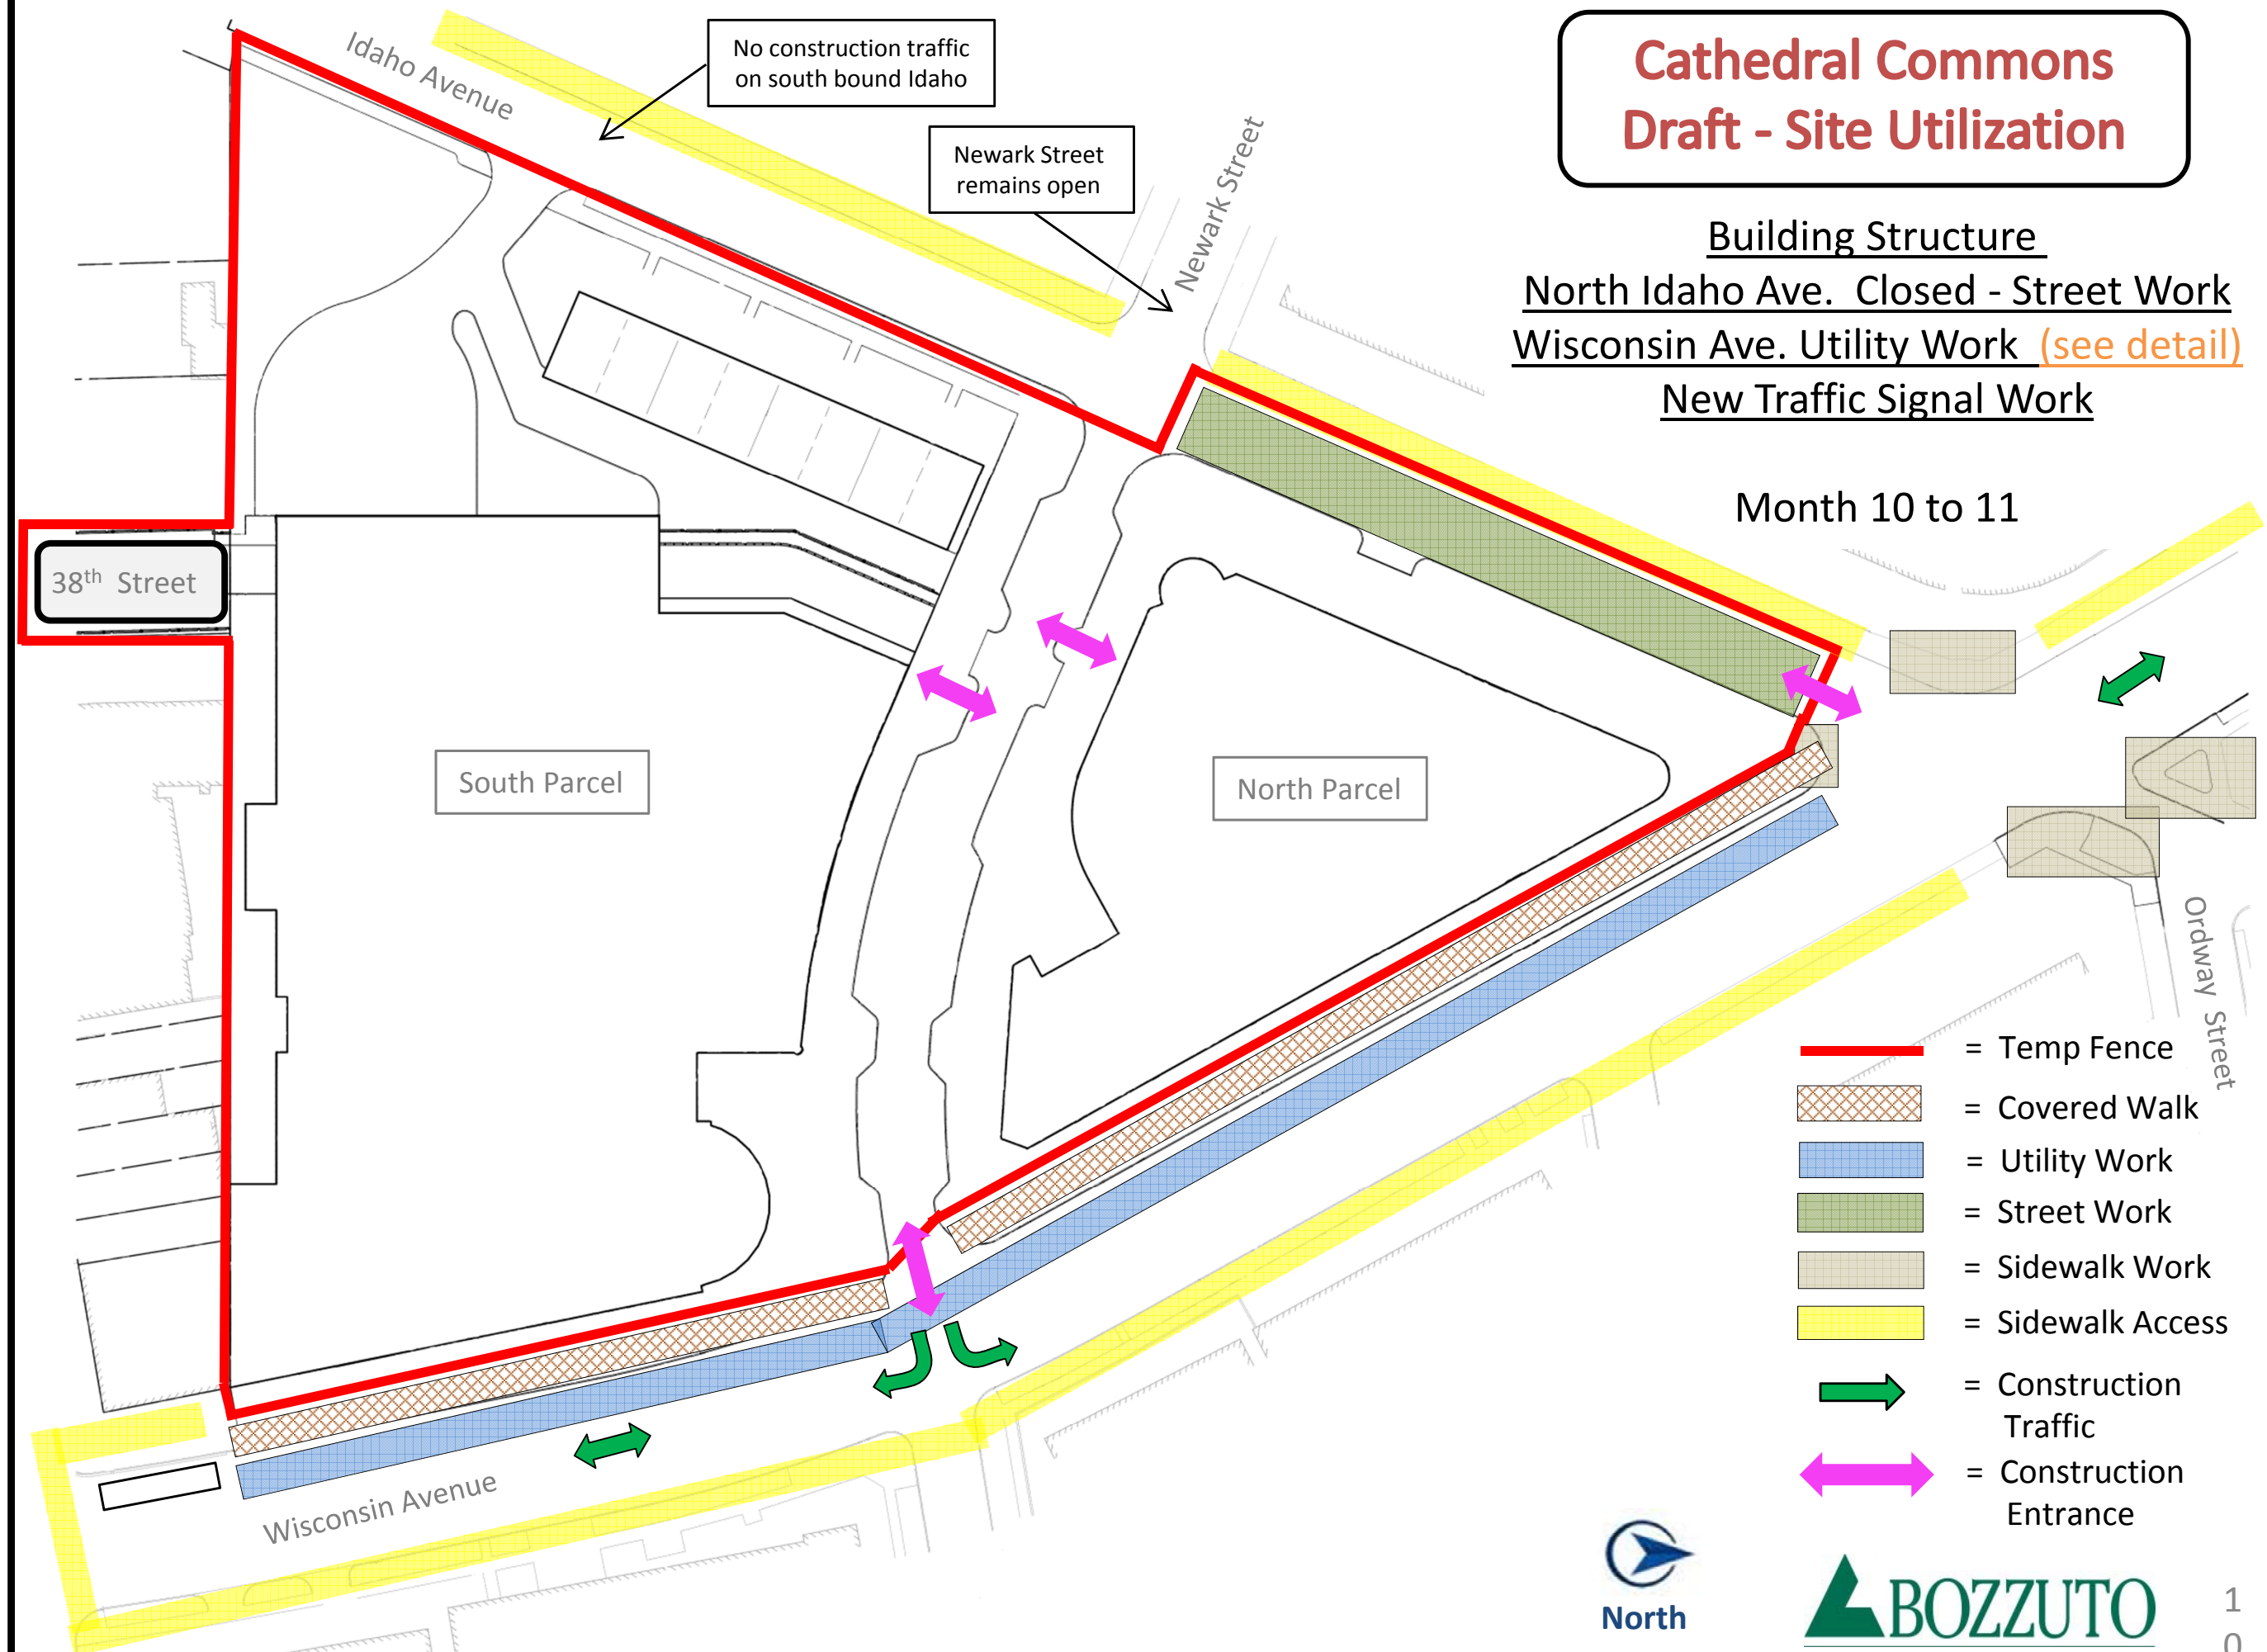

## Wisconsin Ave. Utility Work - Detail

38<sup>th</sup> Street

Newark Street

North Parcel



Wisconsin Avenue

Ordway Street


- 
- North



# Cathedral Commons Draft - Site Utilization

Wisconsin Ave. Utility Work - Detail


Sequence 2

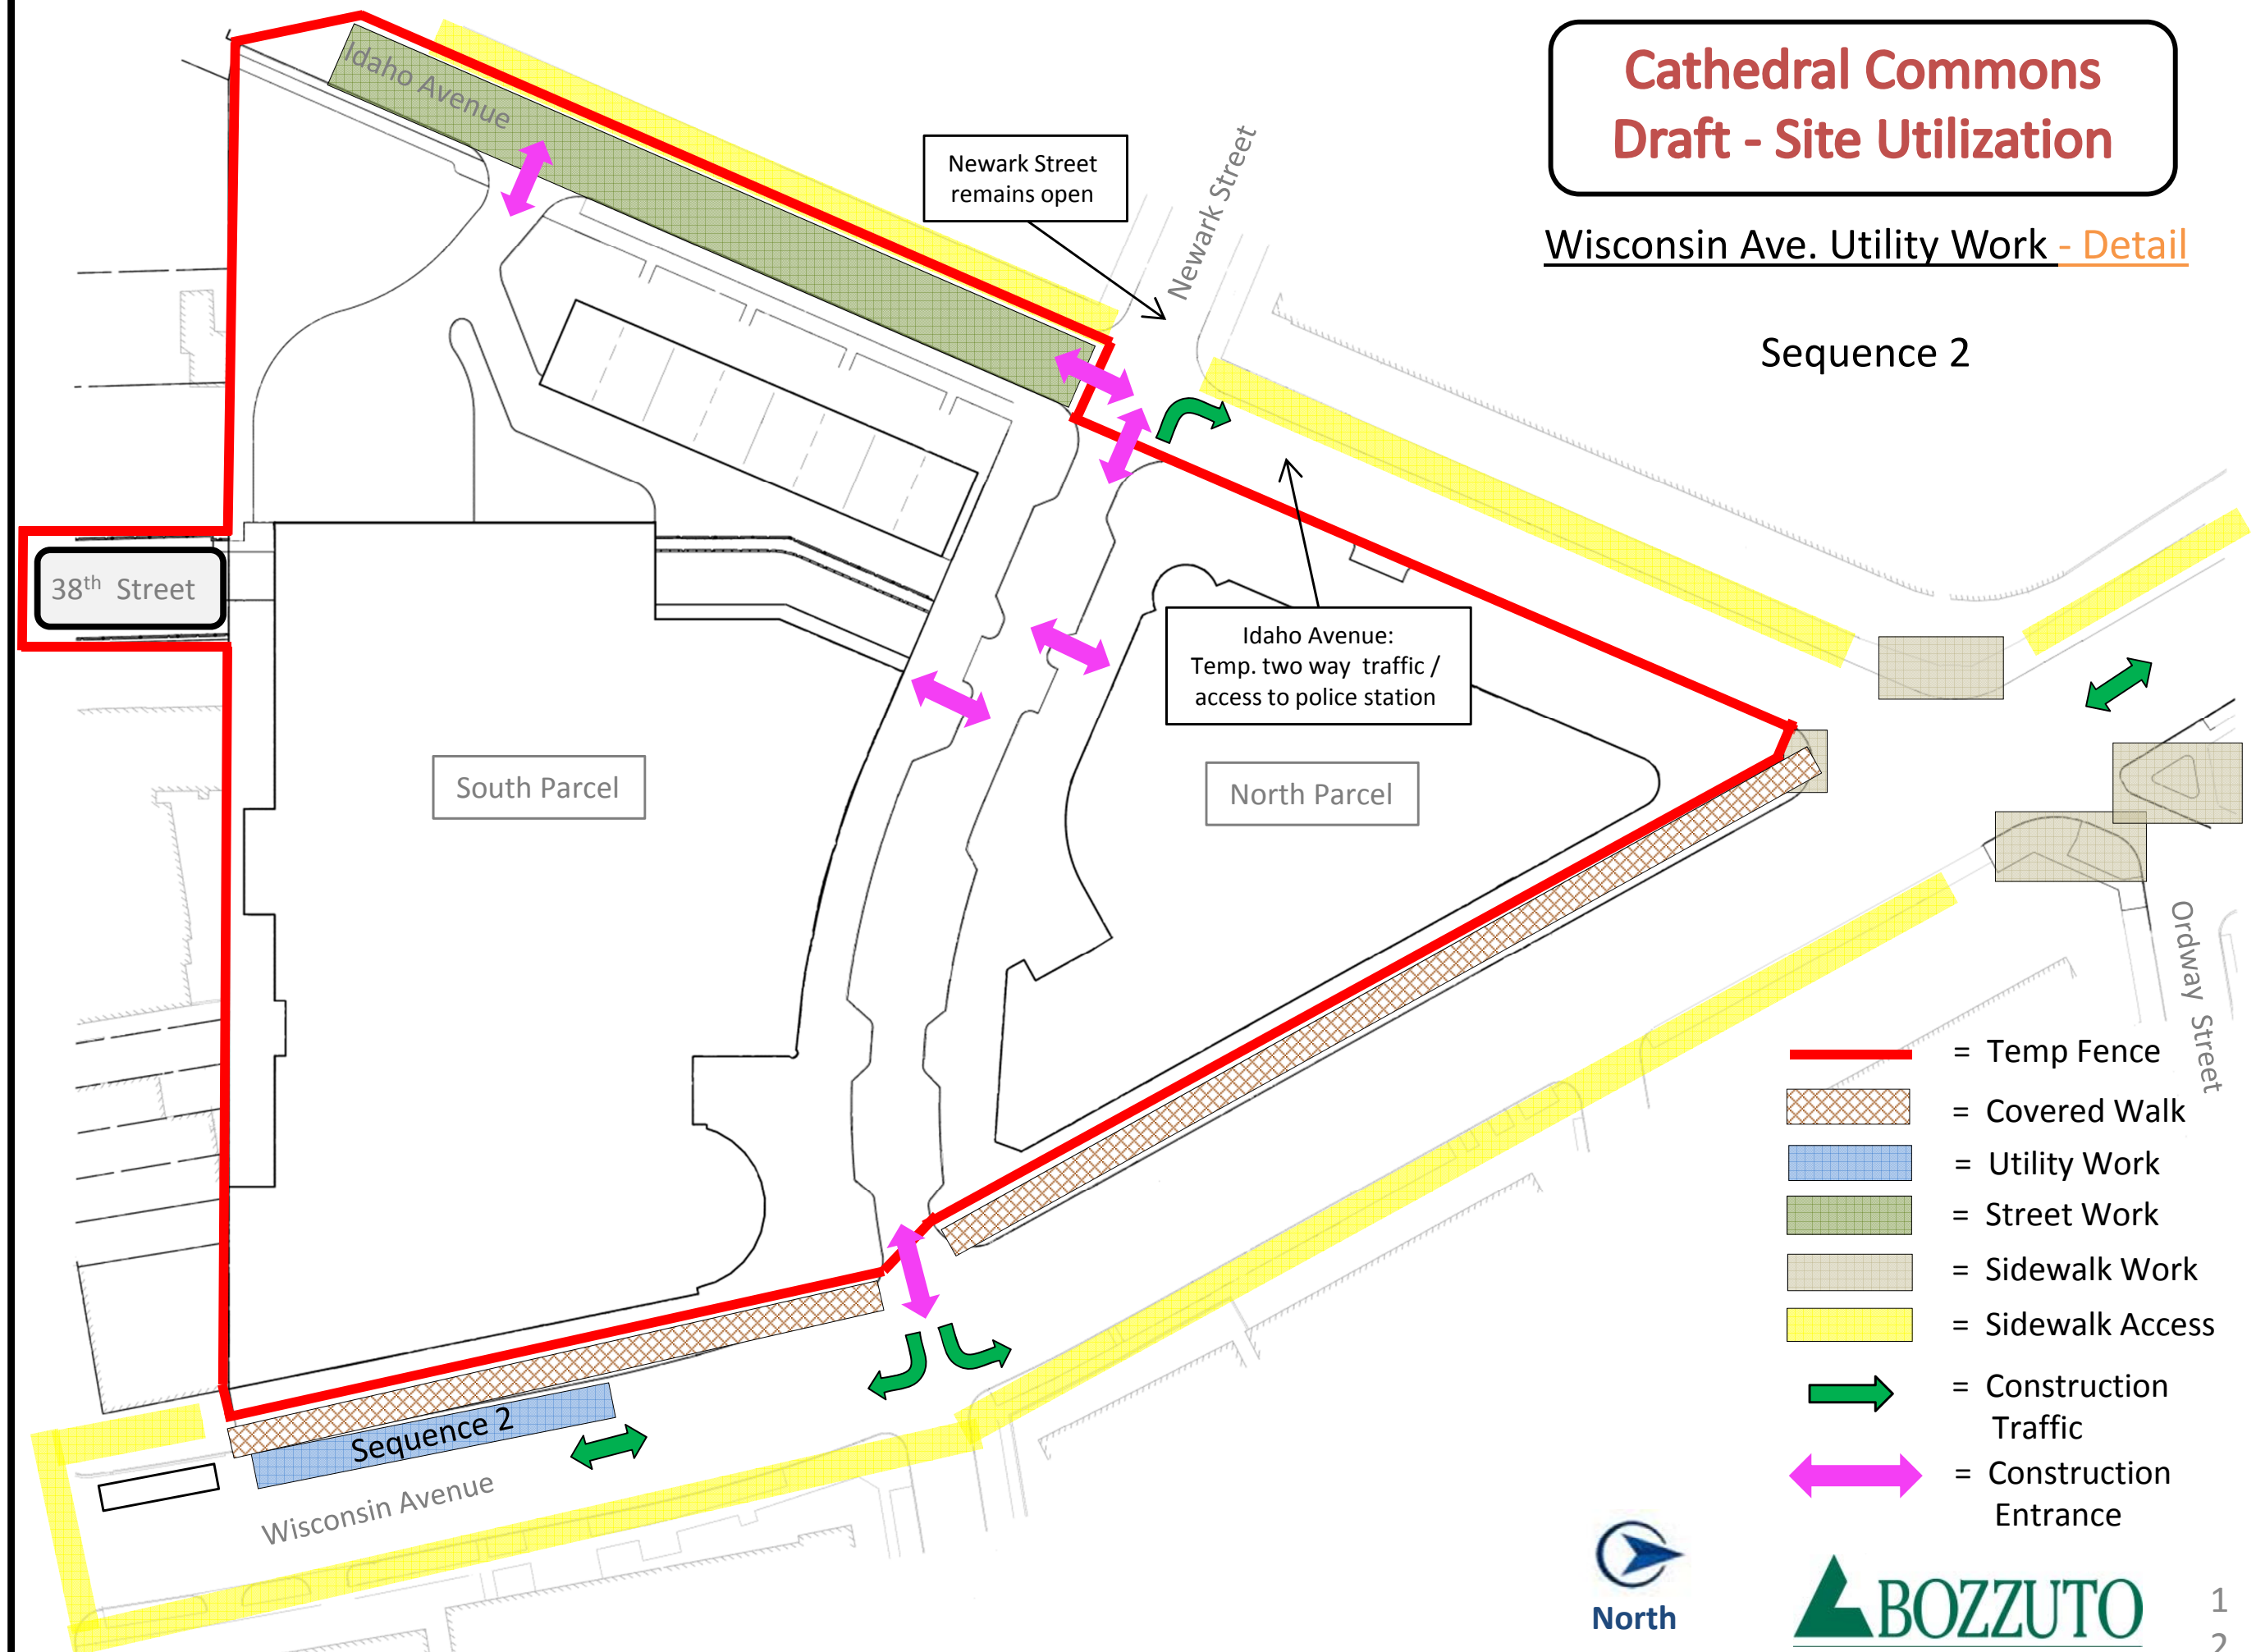

# Cathedral Commons Draft - Site Utilization

Wisconsin Ave. Utility Work - Detail


Sequence 3

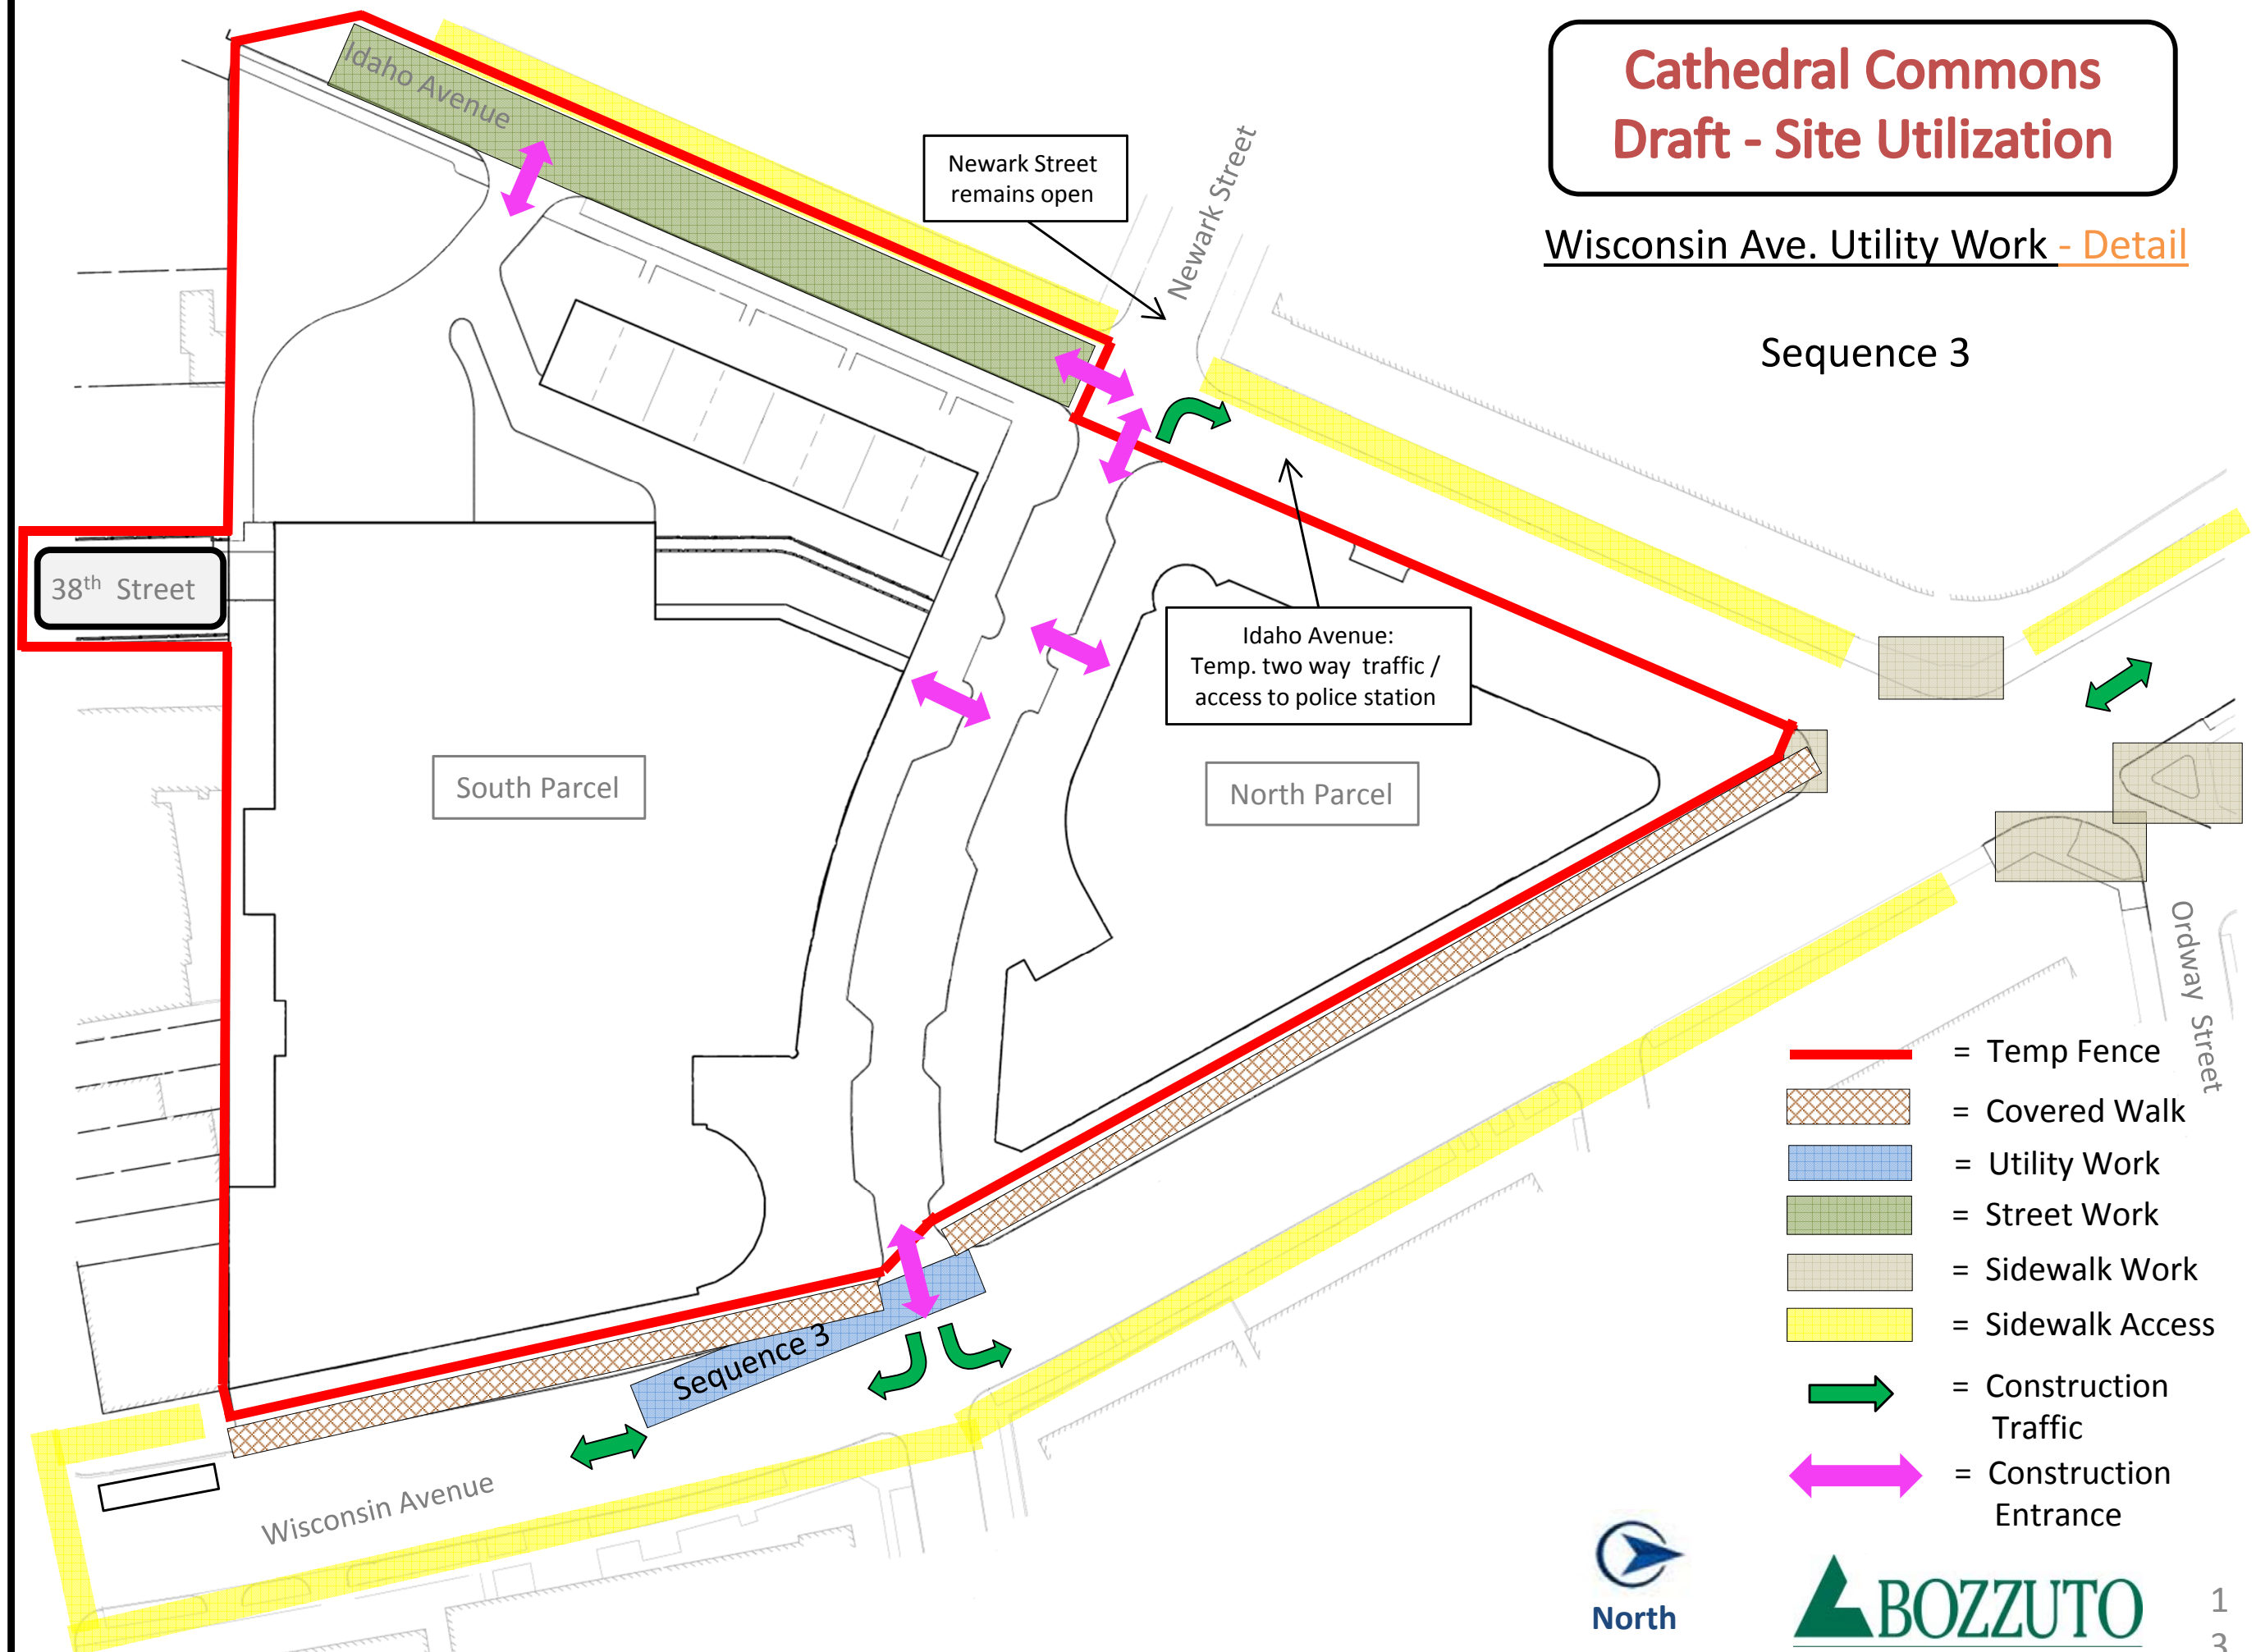

# Cathedral Commons Draft - Site Utilization

Wisconsin Ave. Utility Work - Detail

Sequence 4

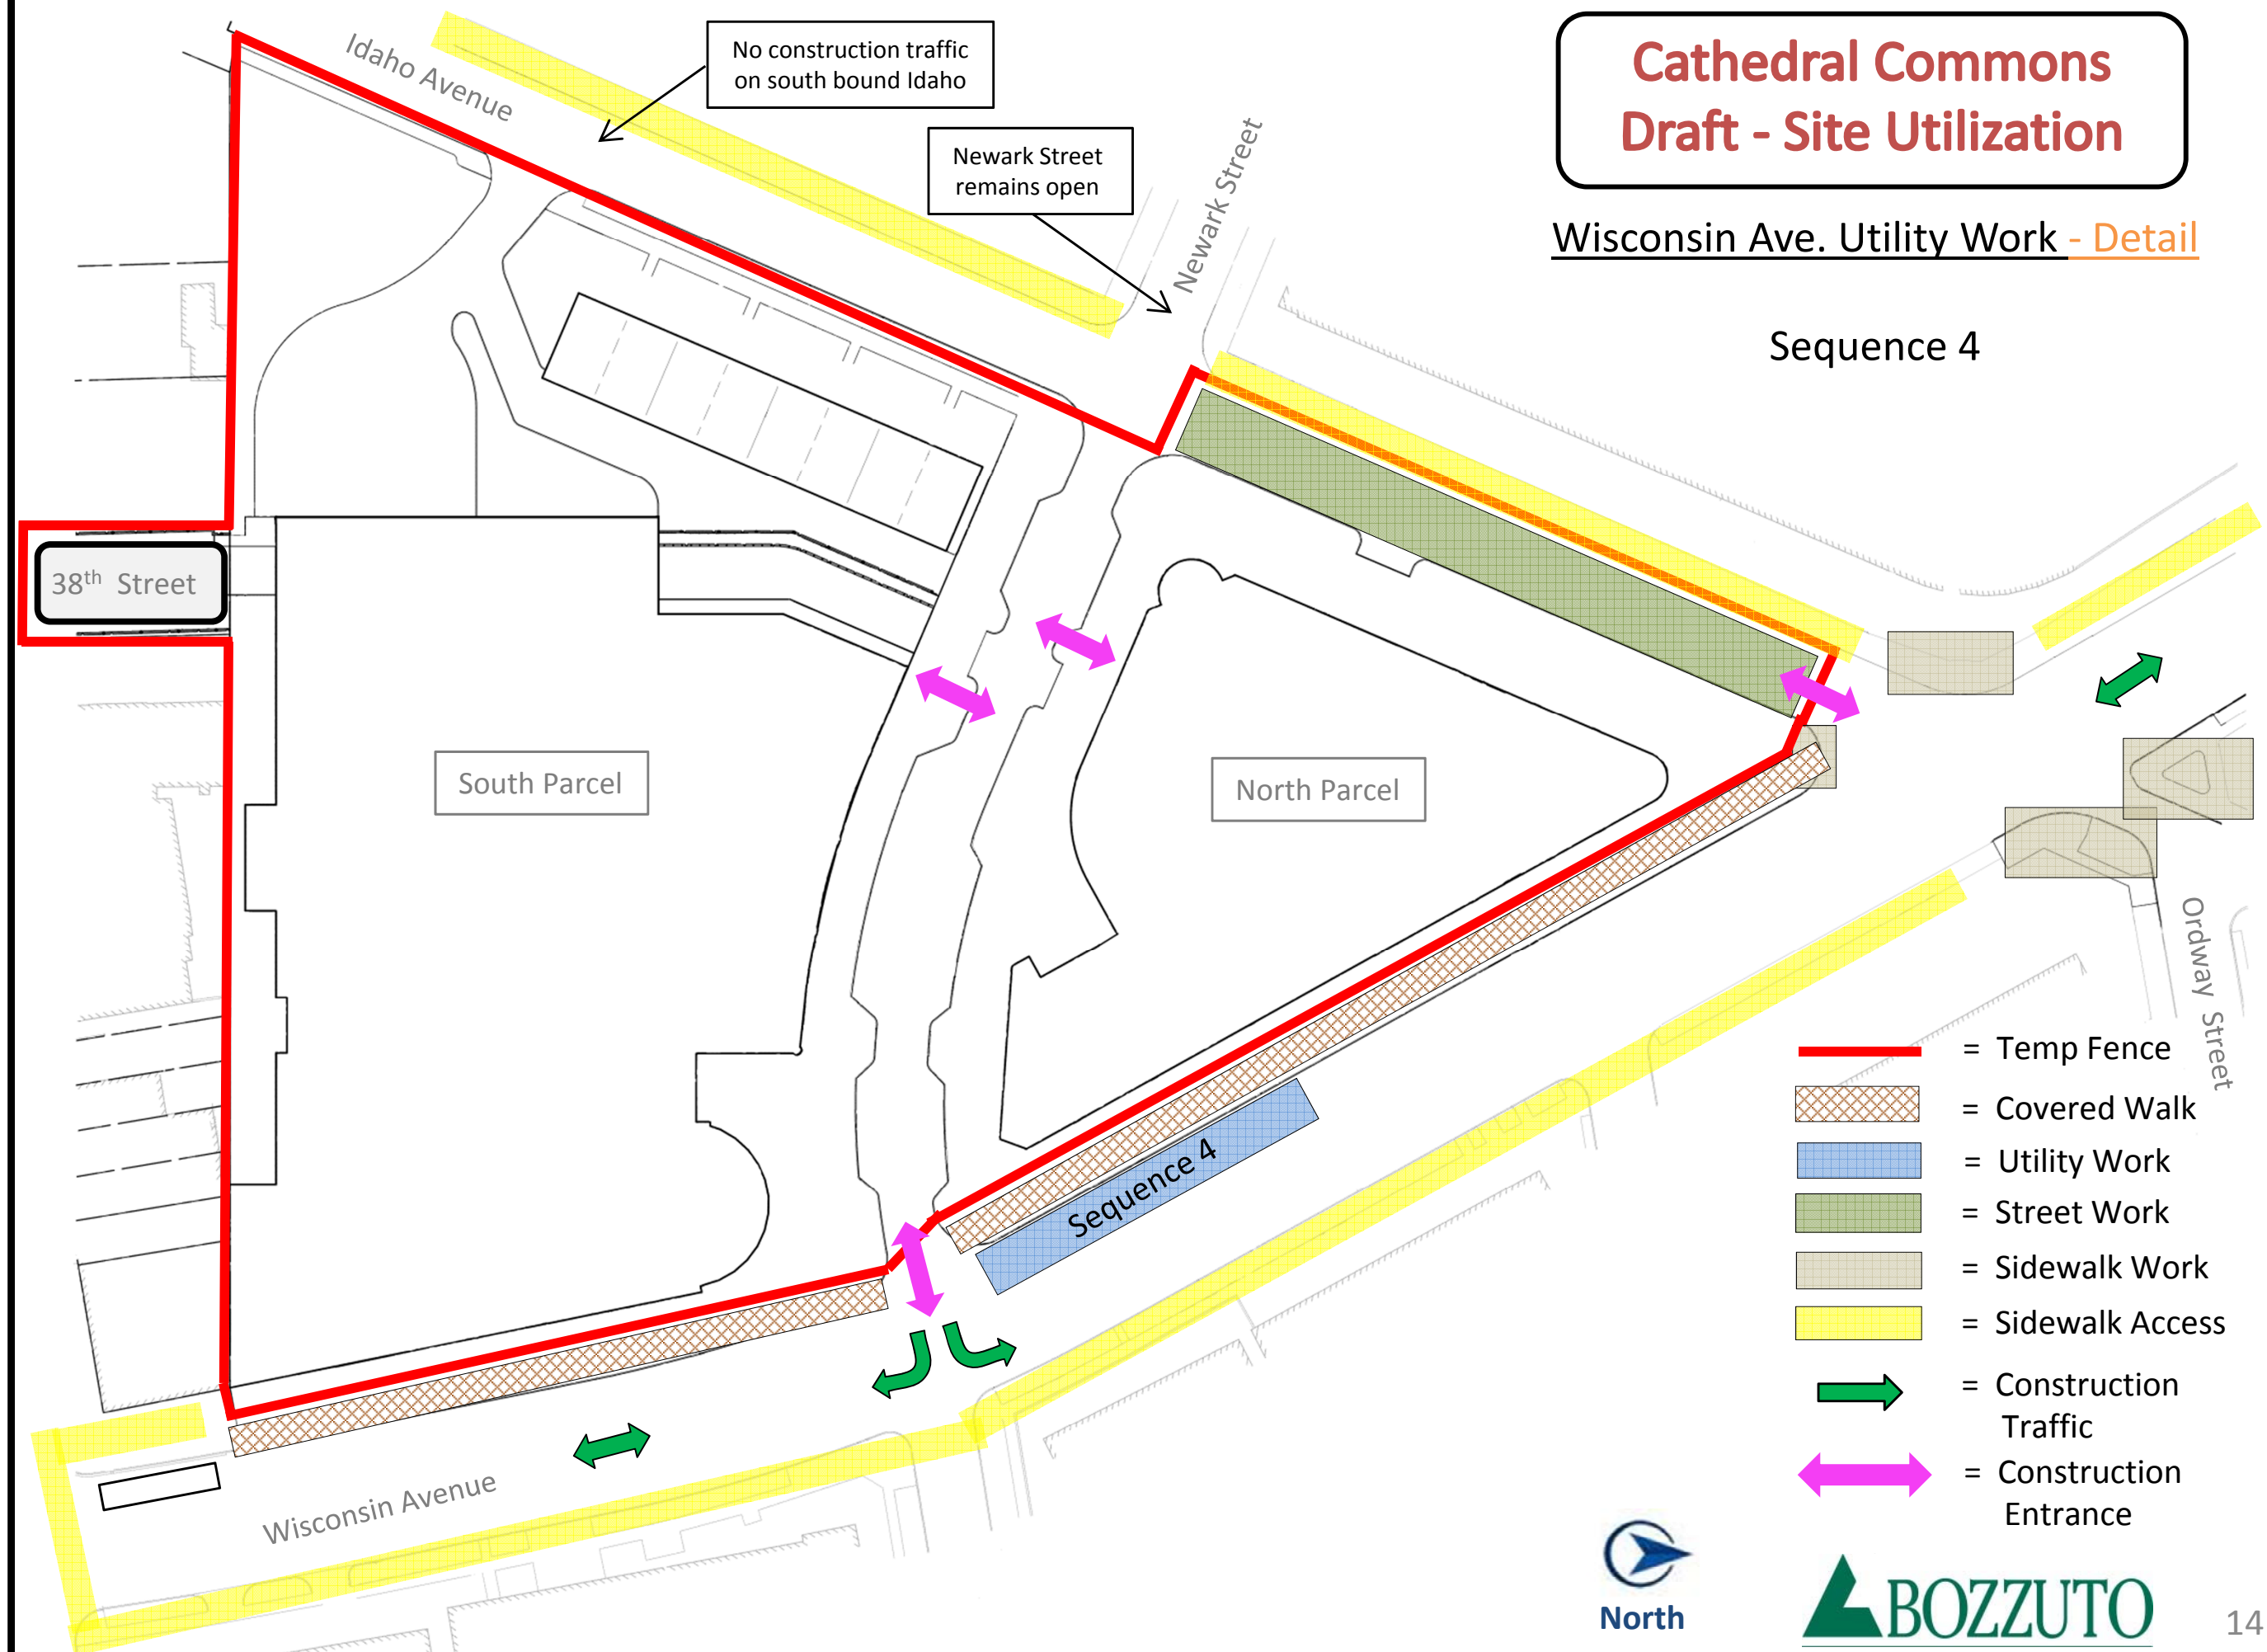




# Cathedral Commons Draft - Site Utilization

Wisconsin Ave. Utility Work - Detail


Sequence 5

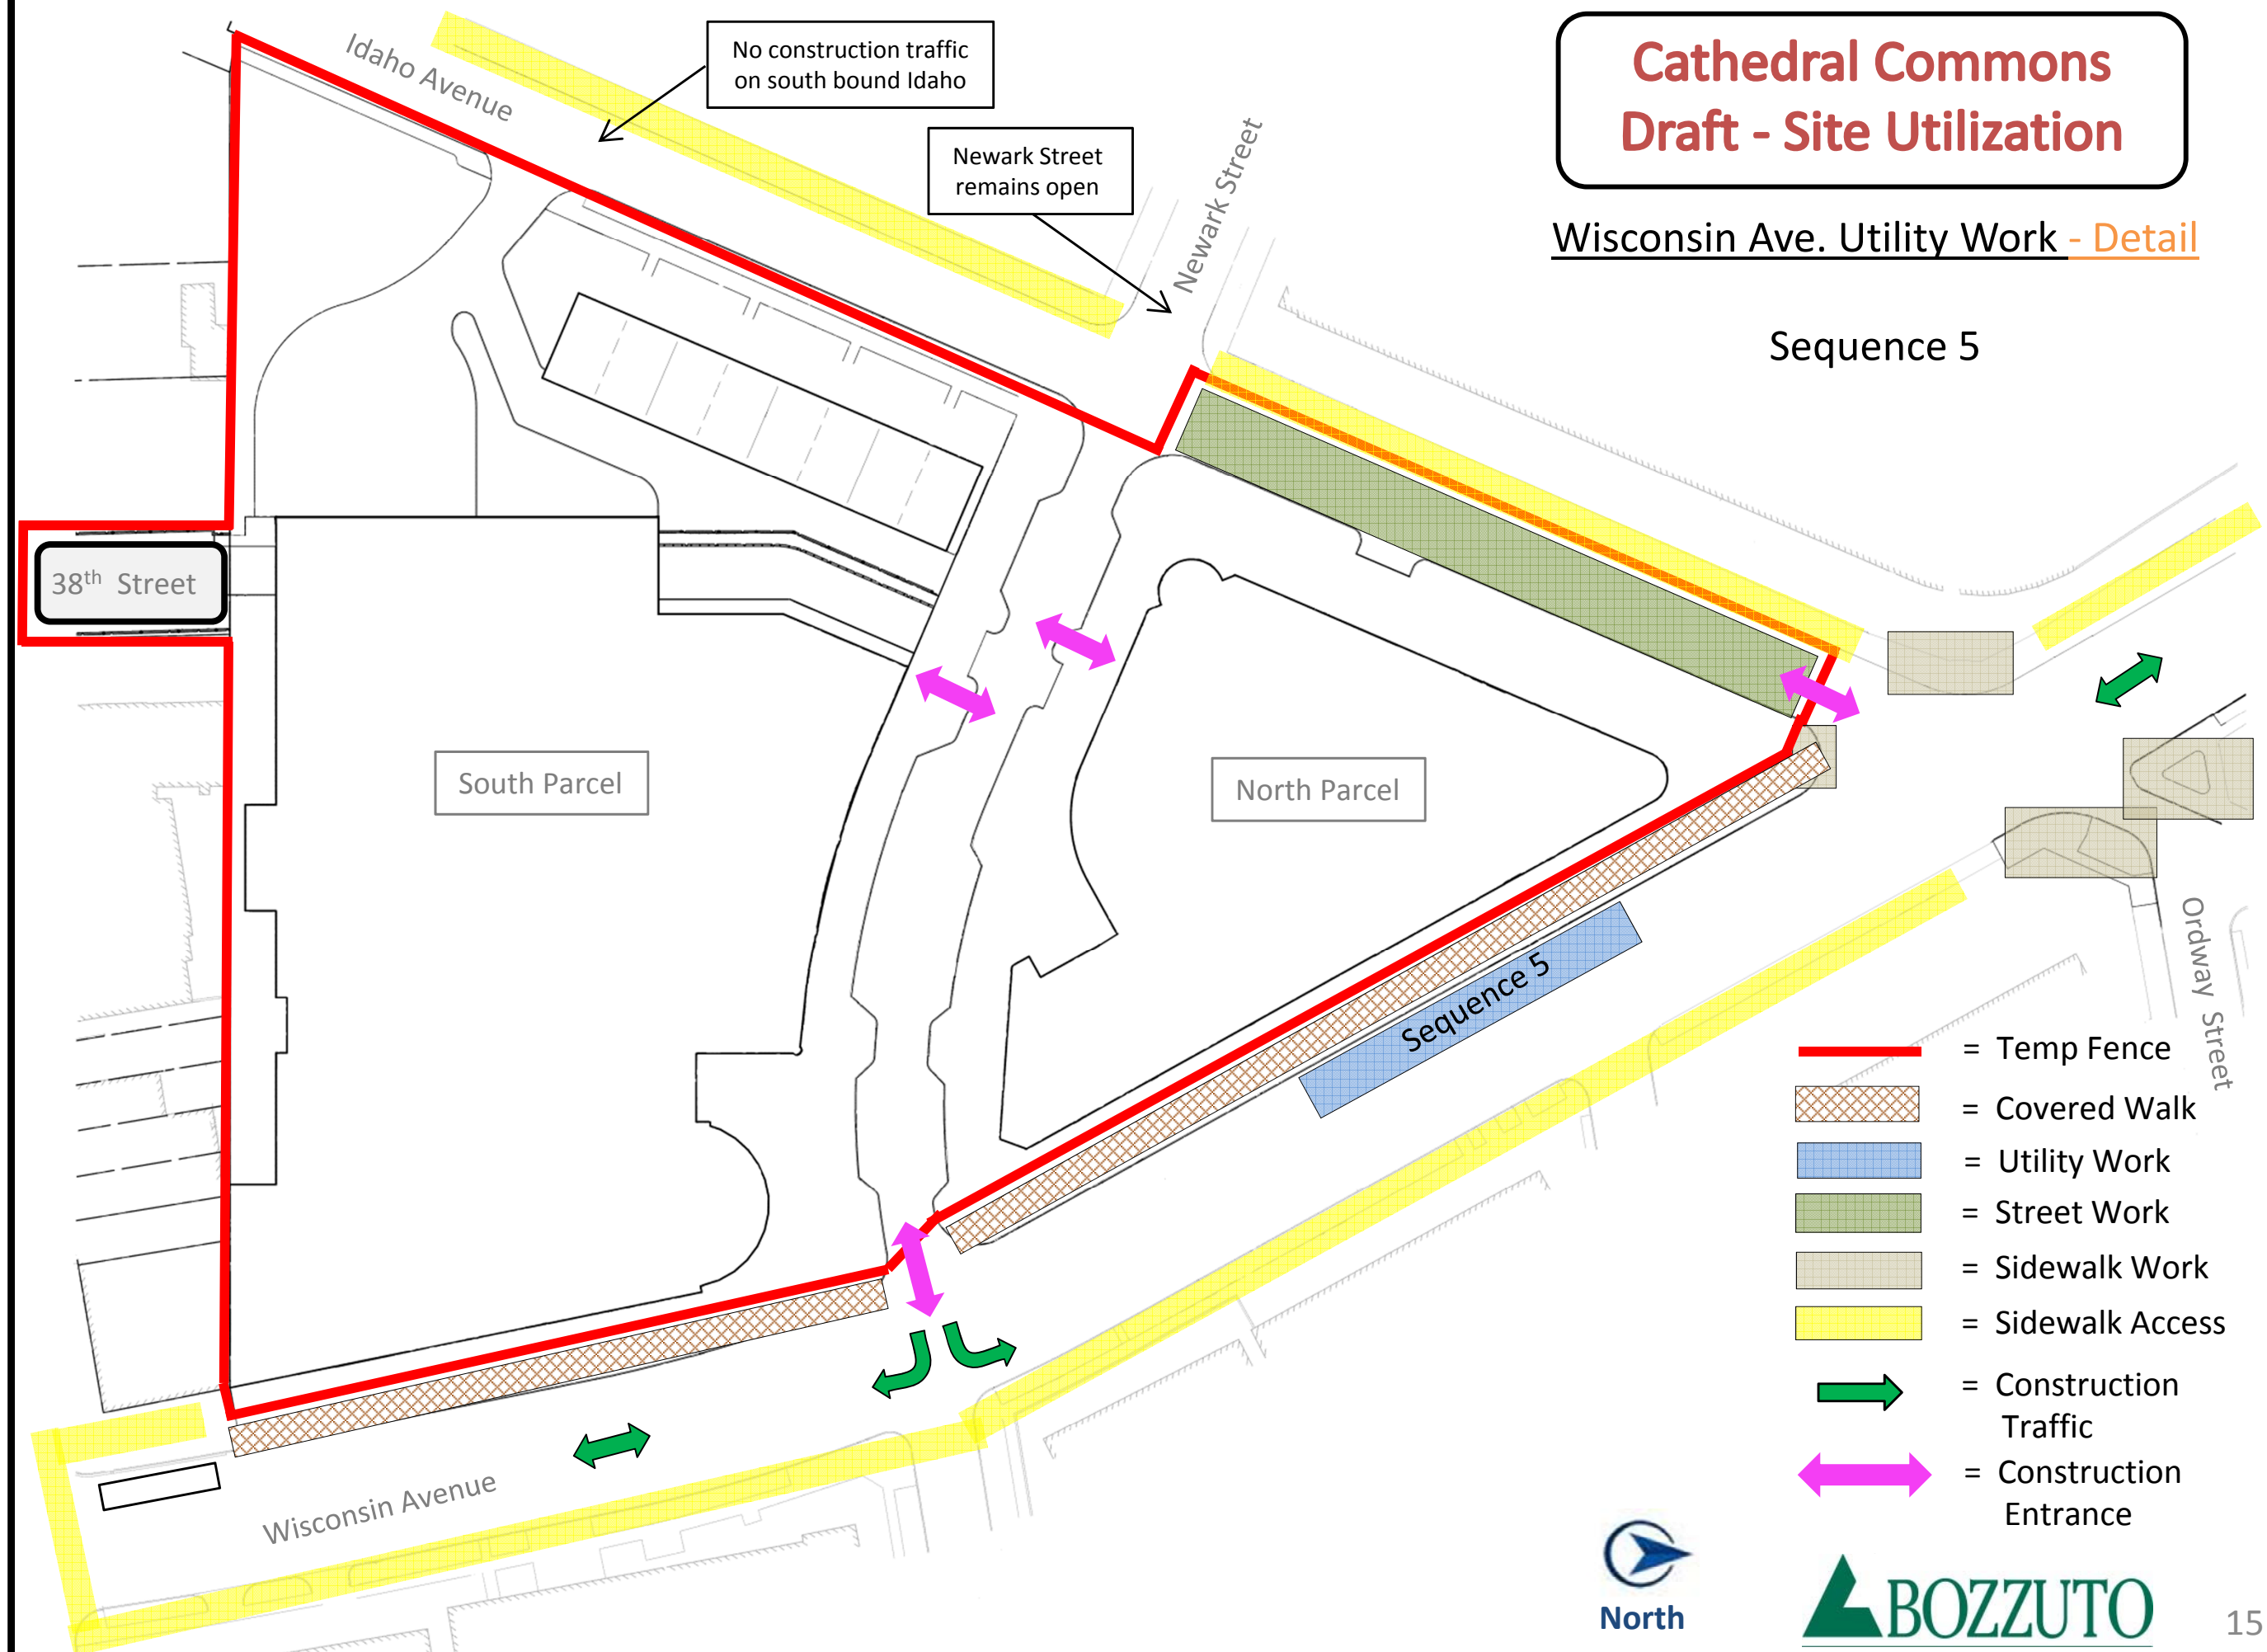

# Cathedral Commons Draft - Site Utilization

Wisconsin Ave. Utility Work - Detail

Sequence 6

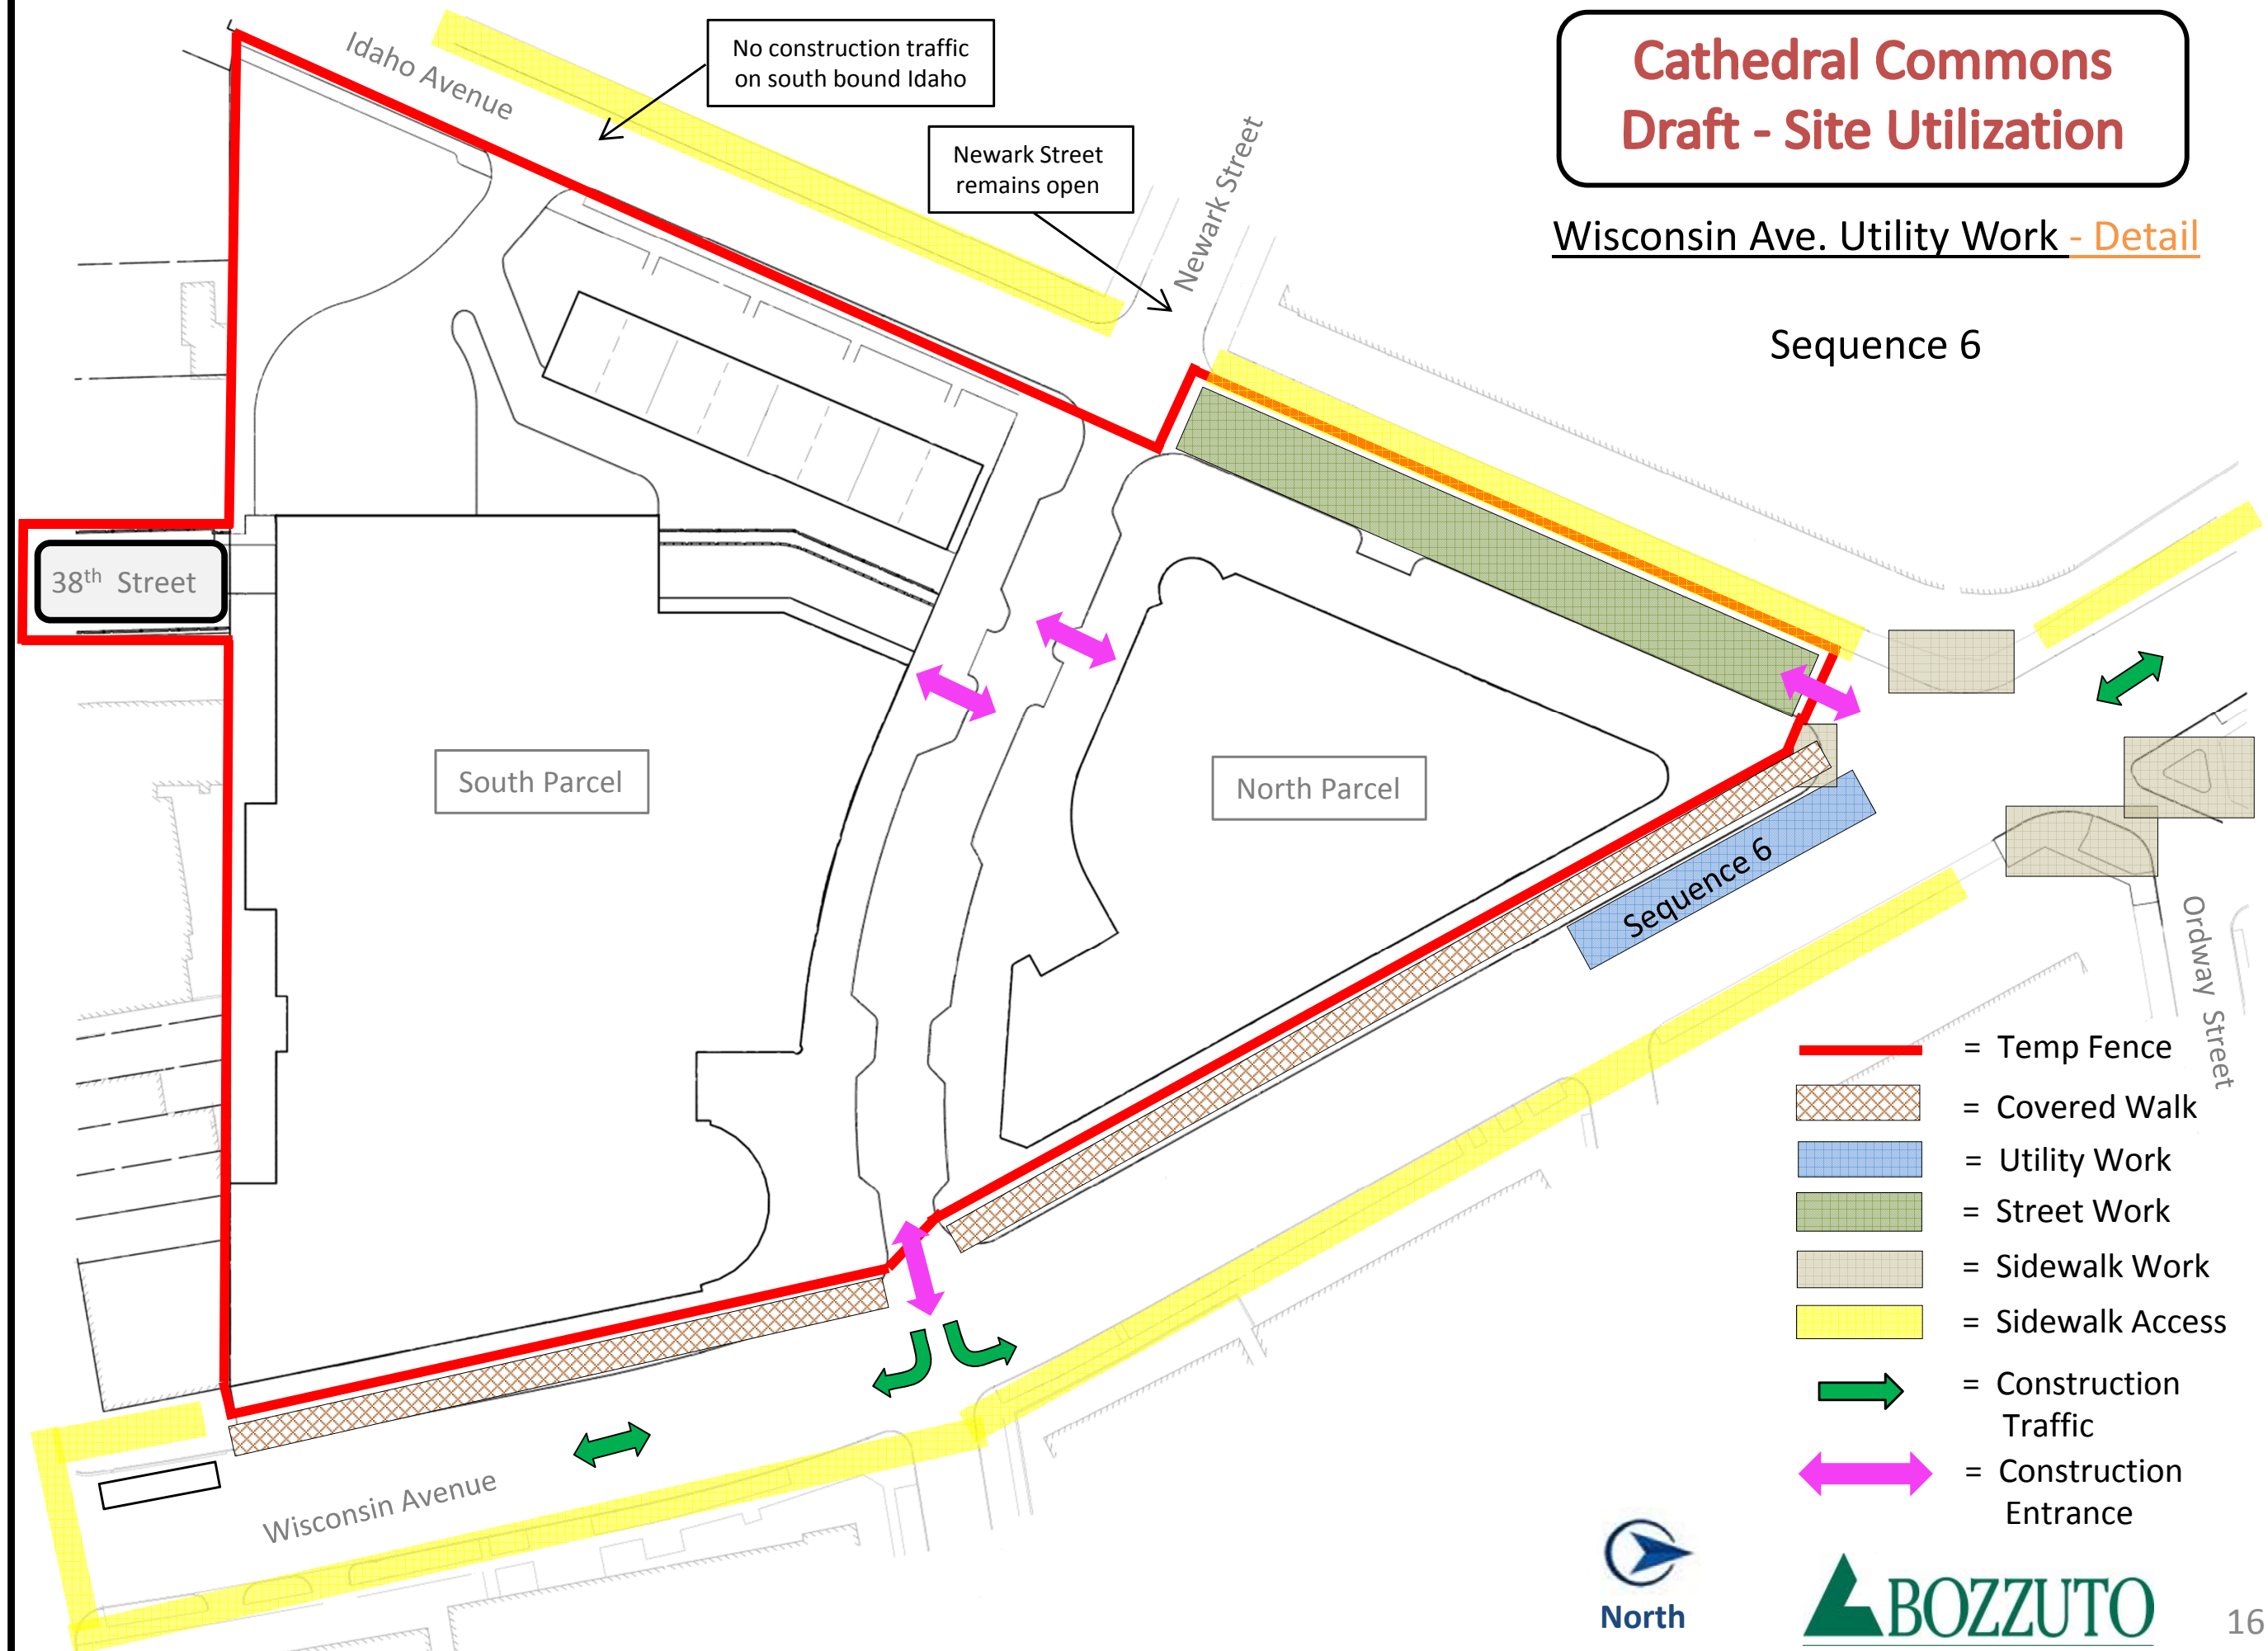


# Cathedral Commons Draft - Site Utilization

Building Structure  
Newark St. Utility Work  
Alley Utility work

Month 12 to 14

New traffic signal  
Operational on Wisconsin  
2 way traffic on Idaho Ave

- = Temp Fence
- = Covered Walk
- = Utility Work
- = Street Work
- = Sidewalk Work
- = Sidewalk Access
- = Construction Traffic
- = Construction Entrance

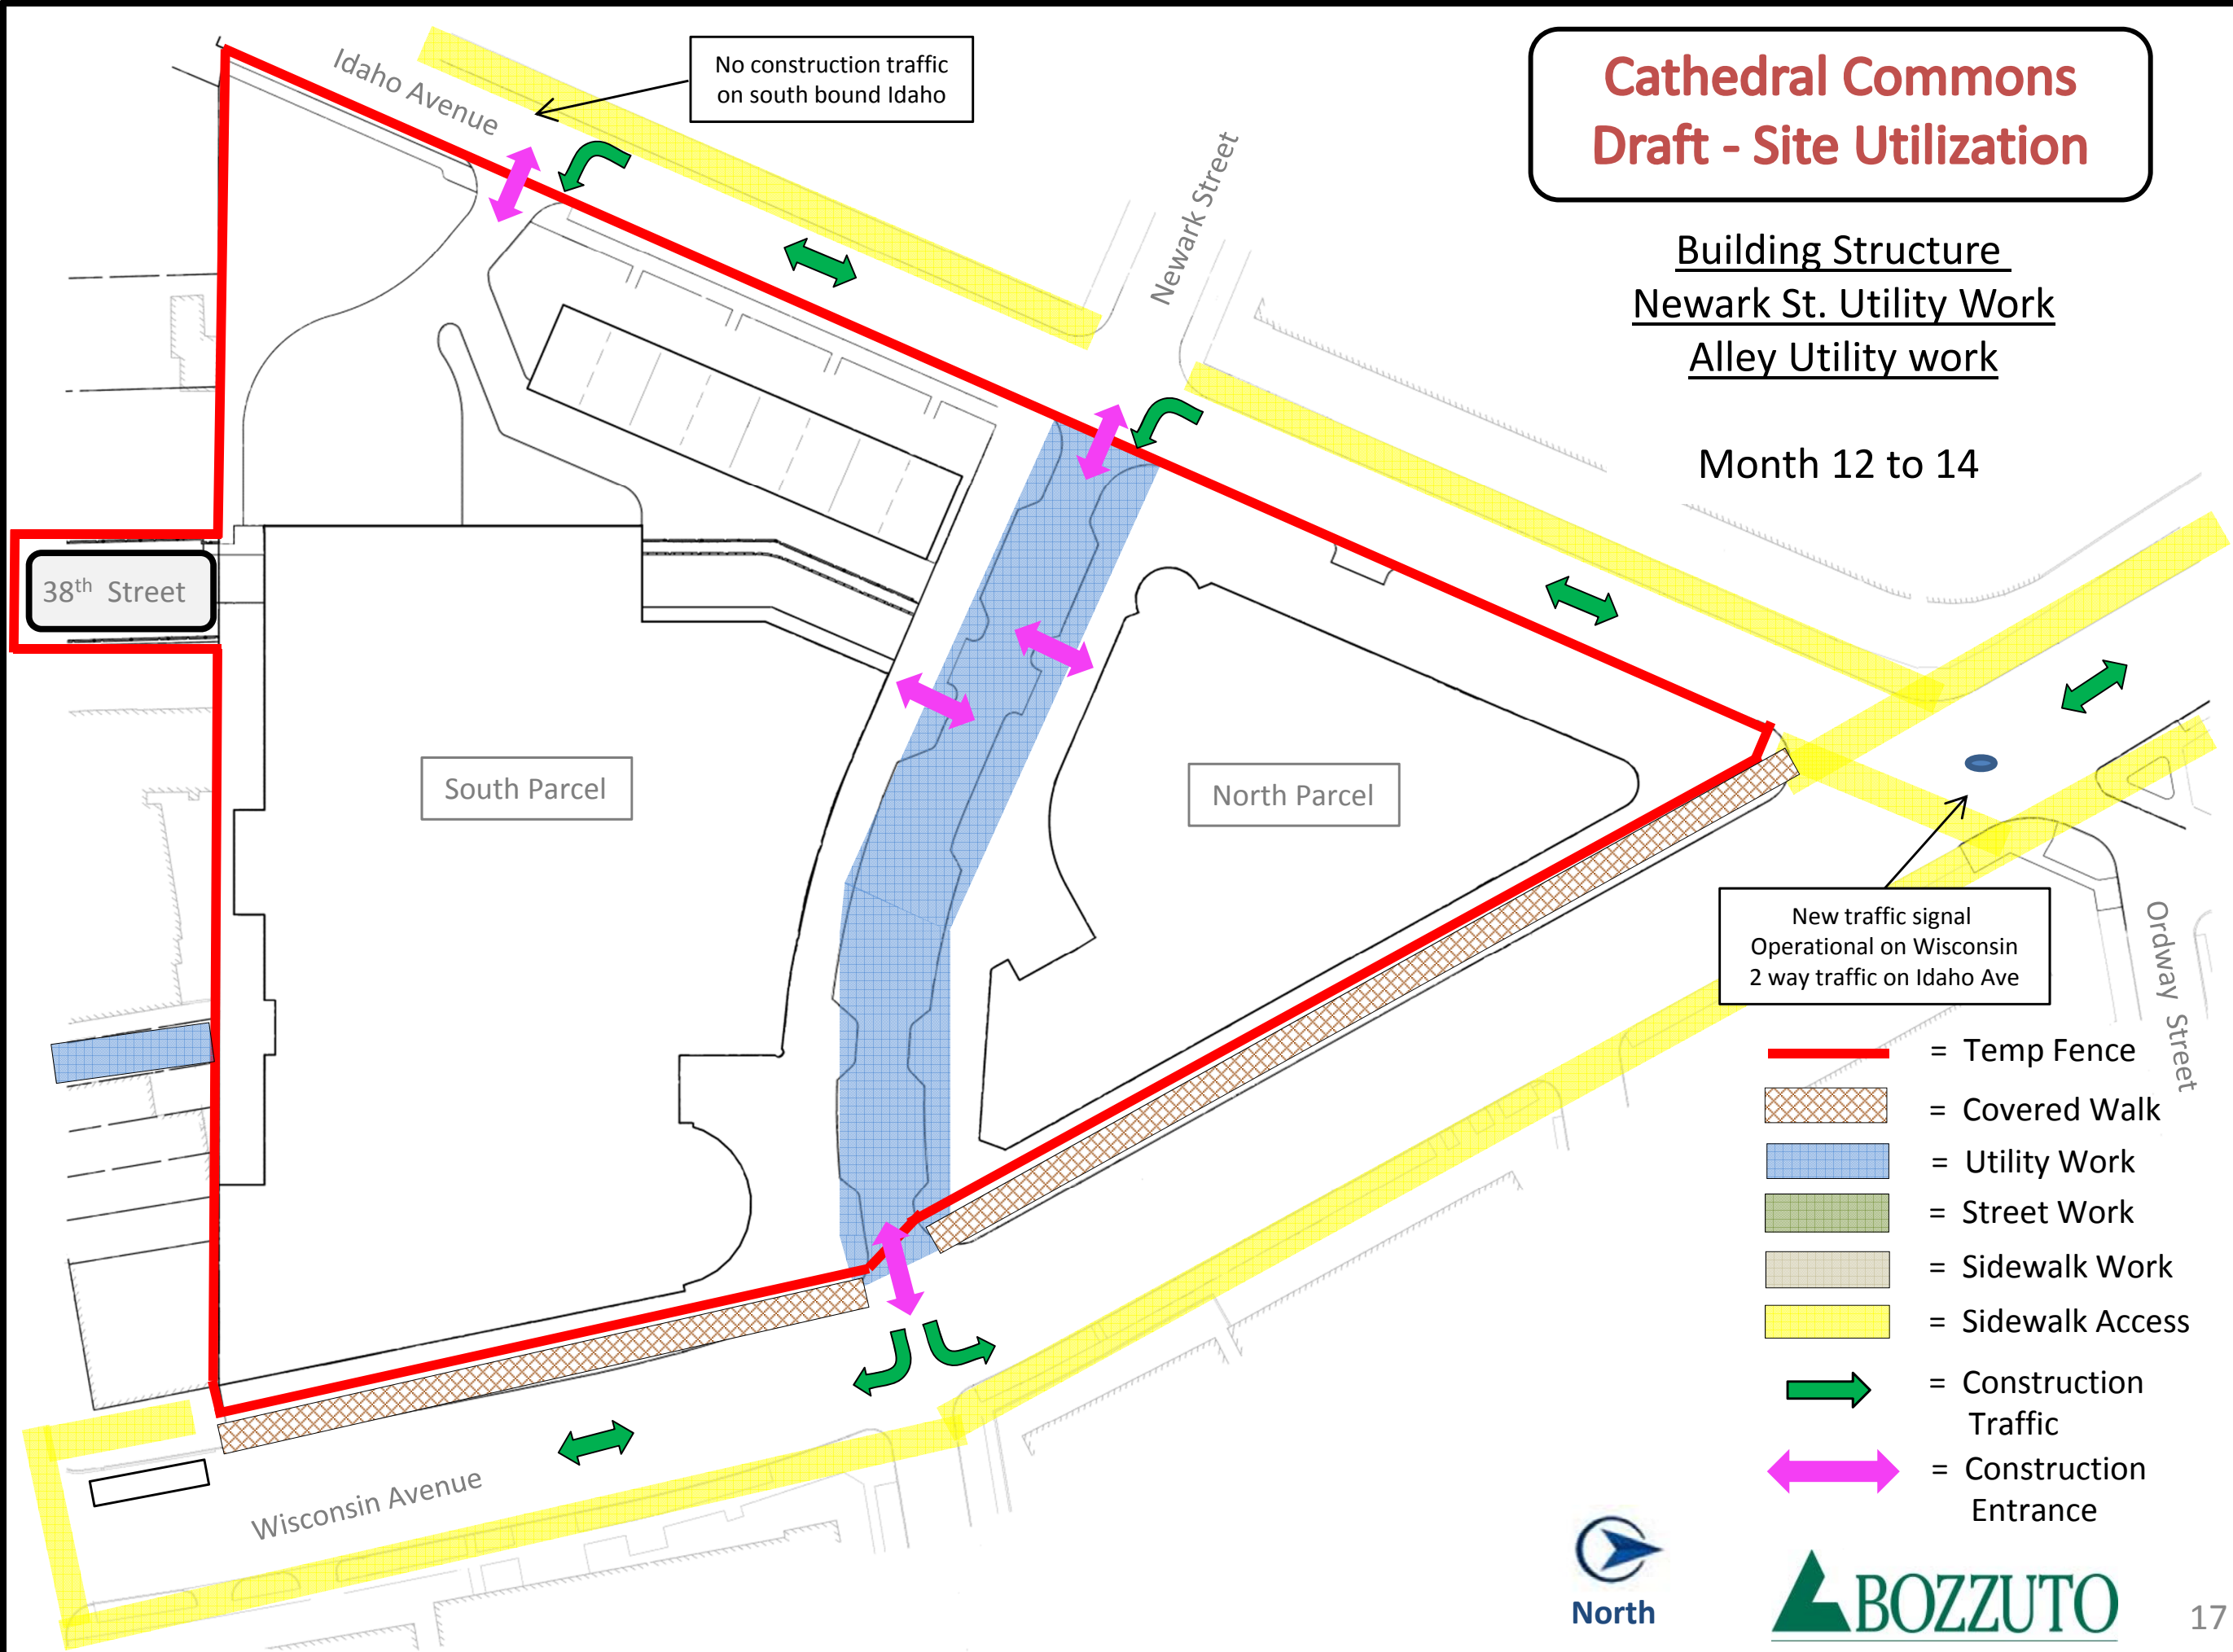




# Cathedral Commons Draft - Site Utilization

Building Envelope

Interior Finishes

Month 15 to 16

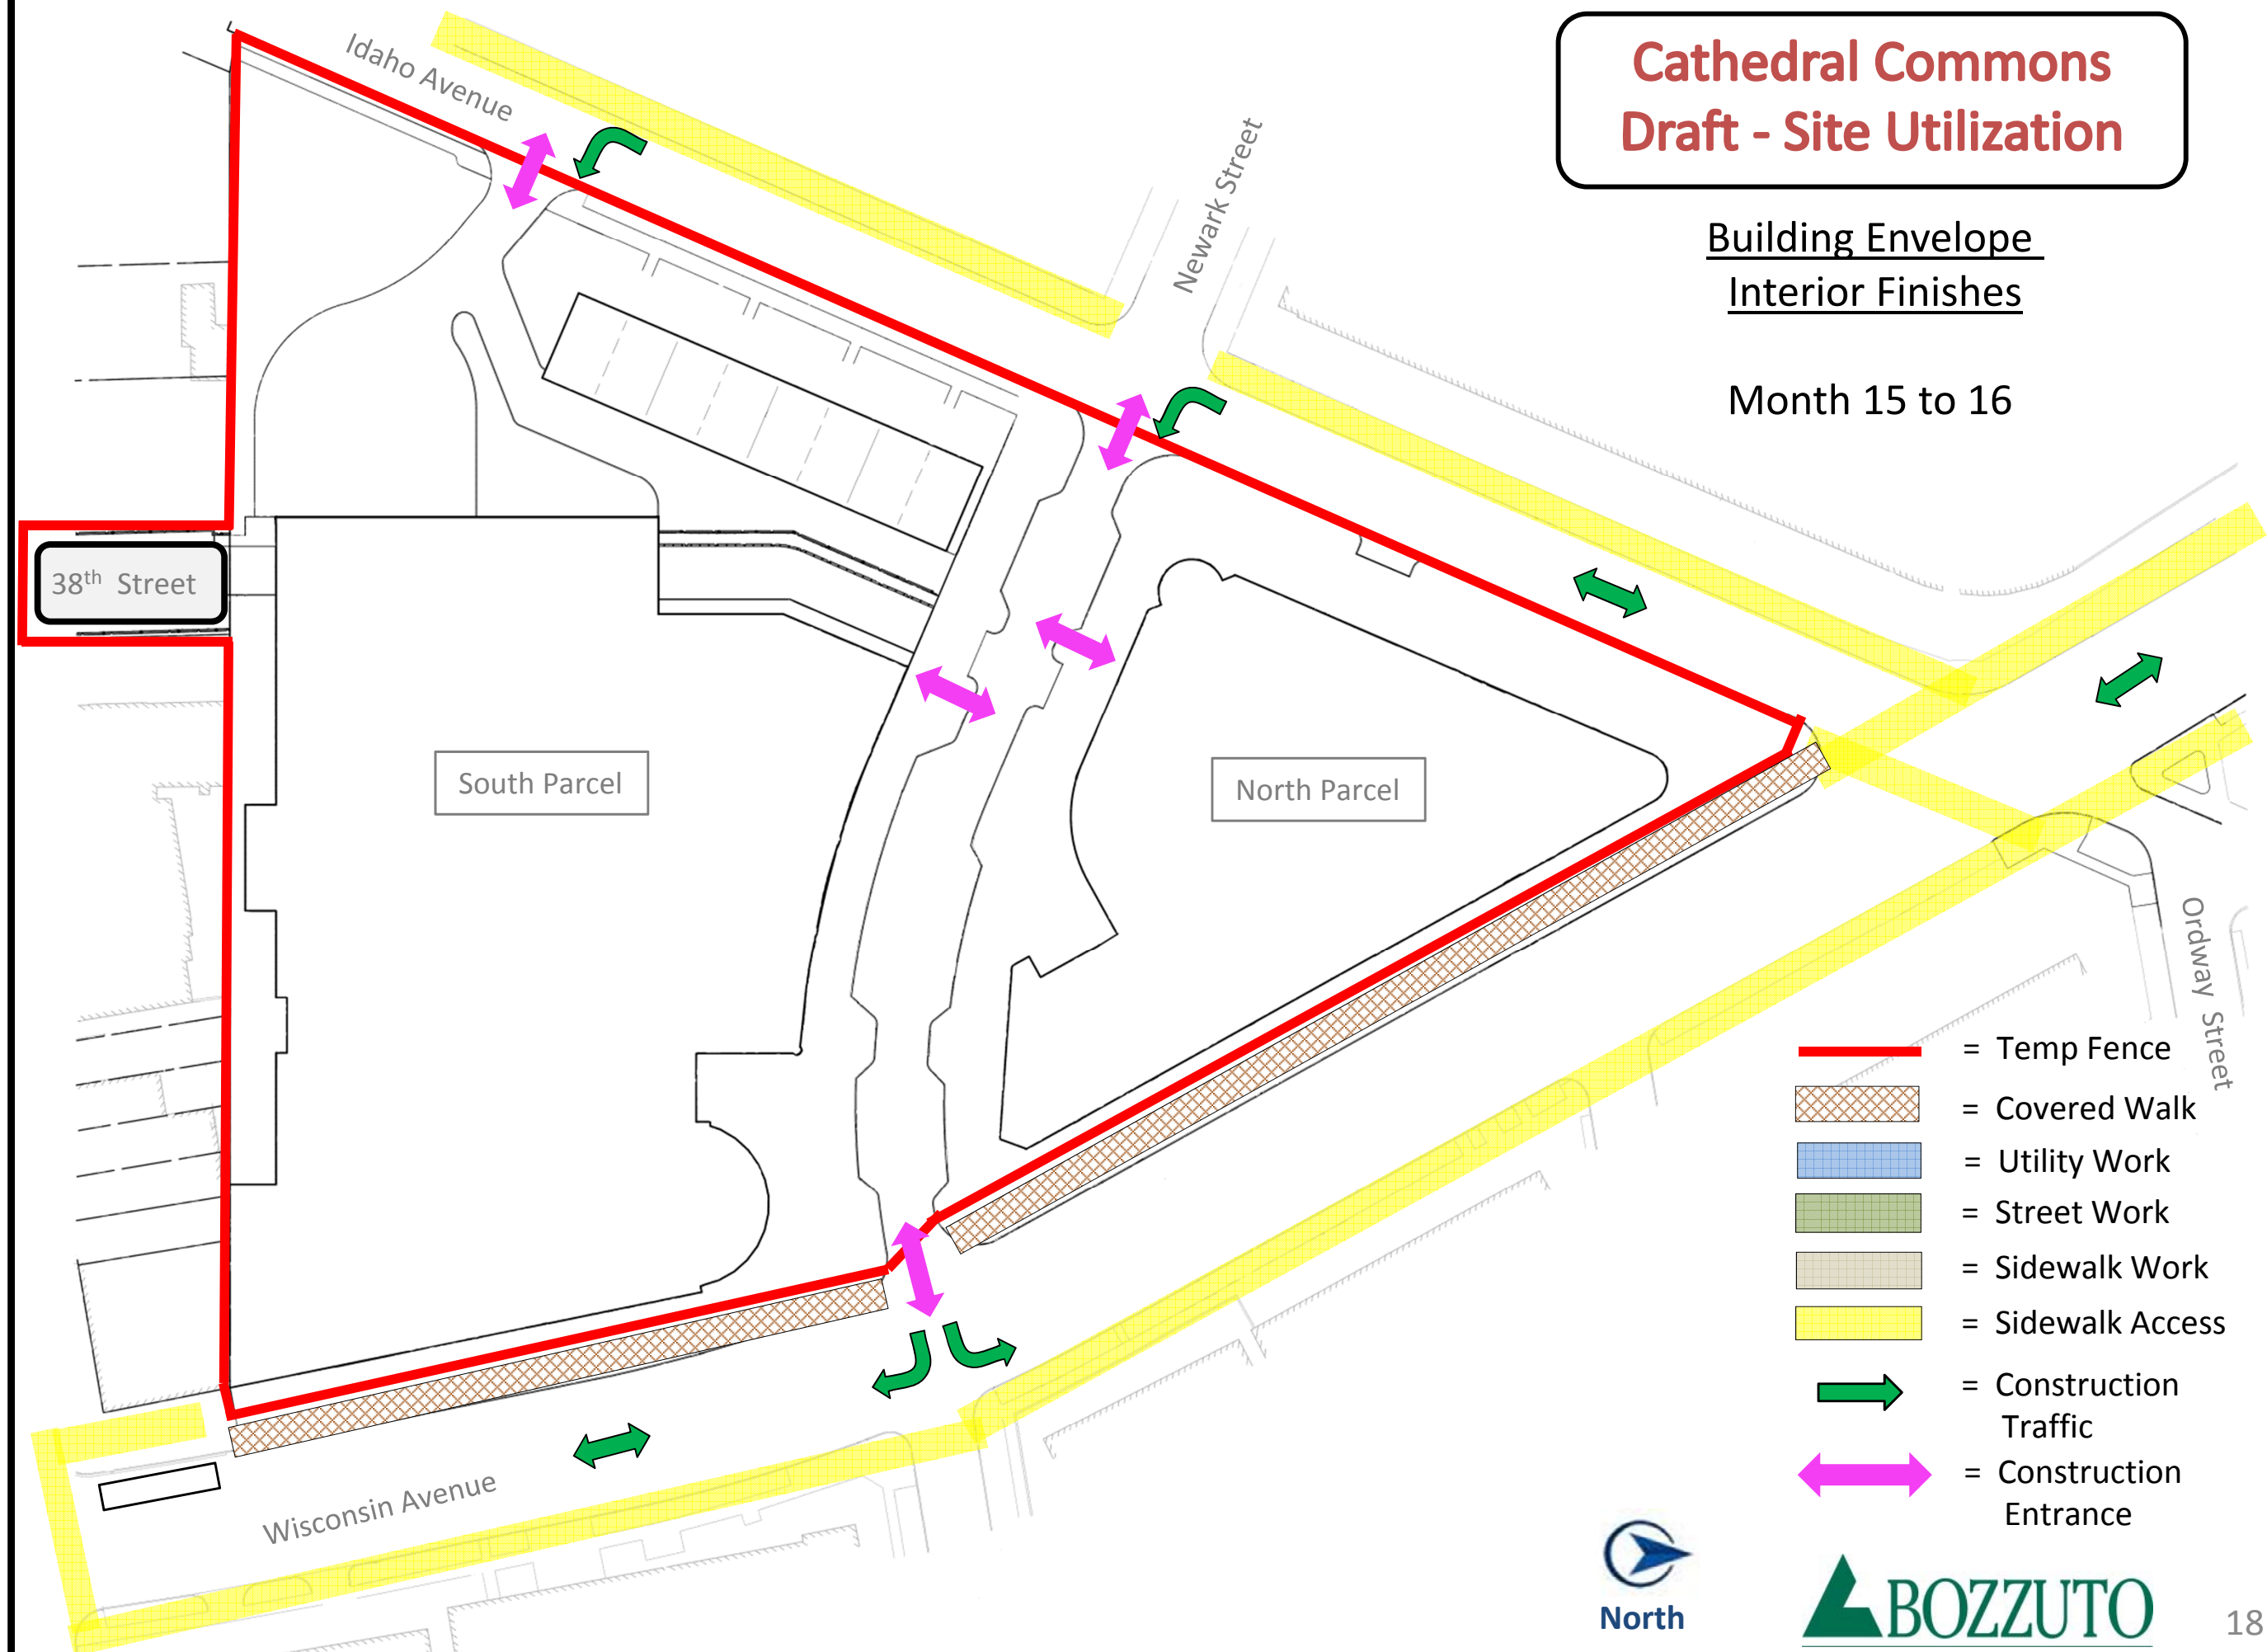

= Temp Fence

= Covered Walk

= Utility Work

= Street Work

= Sidewalk Work

= Sidewalk Access

= Construction  
Traffic

= Construction  
Entrance




North



# Cathedral Commons Draft - Site Utilization

Interior Finishes  
South Parcel Hardscape


Month 17 to 18

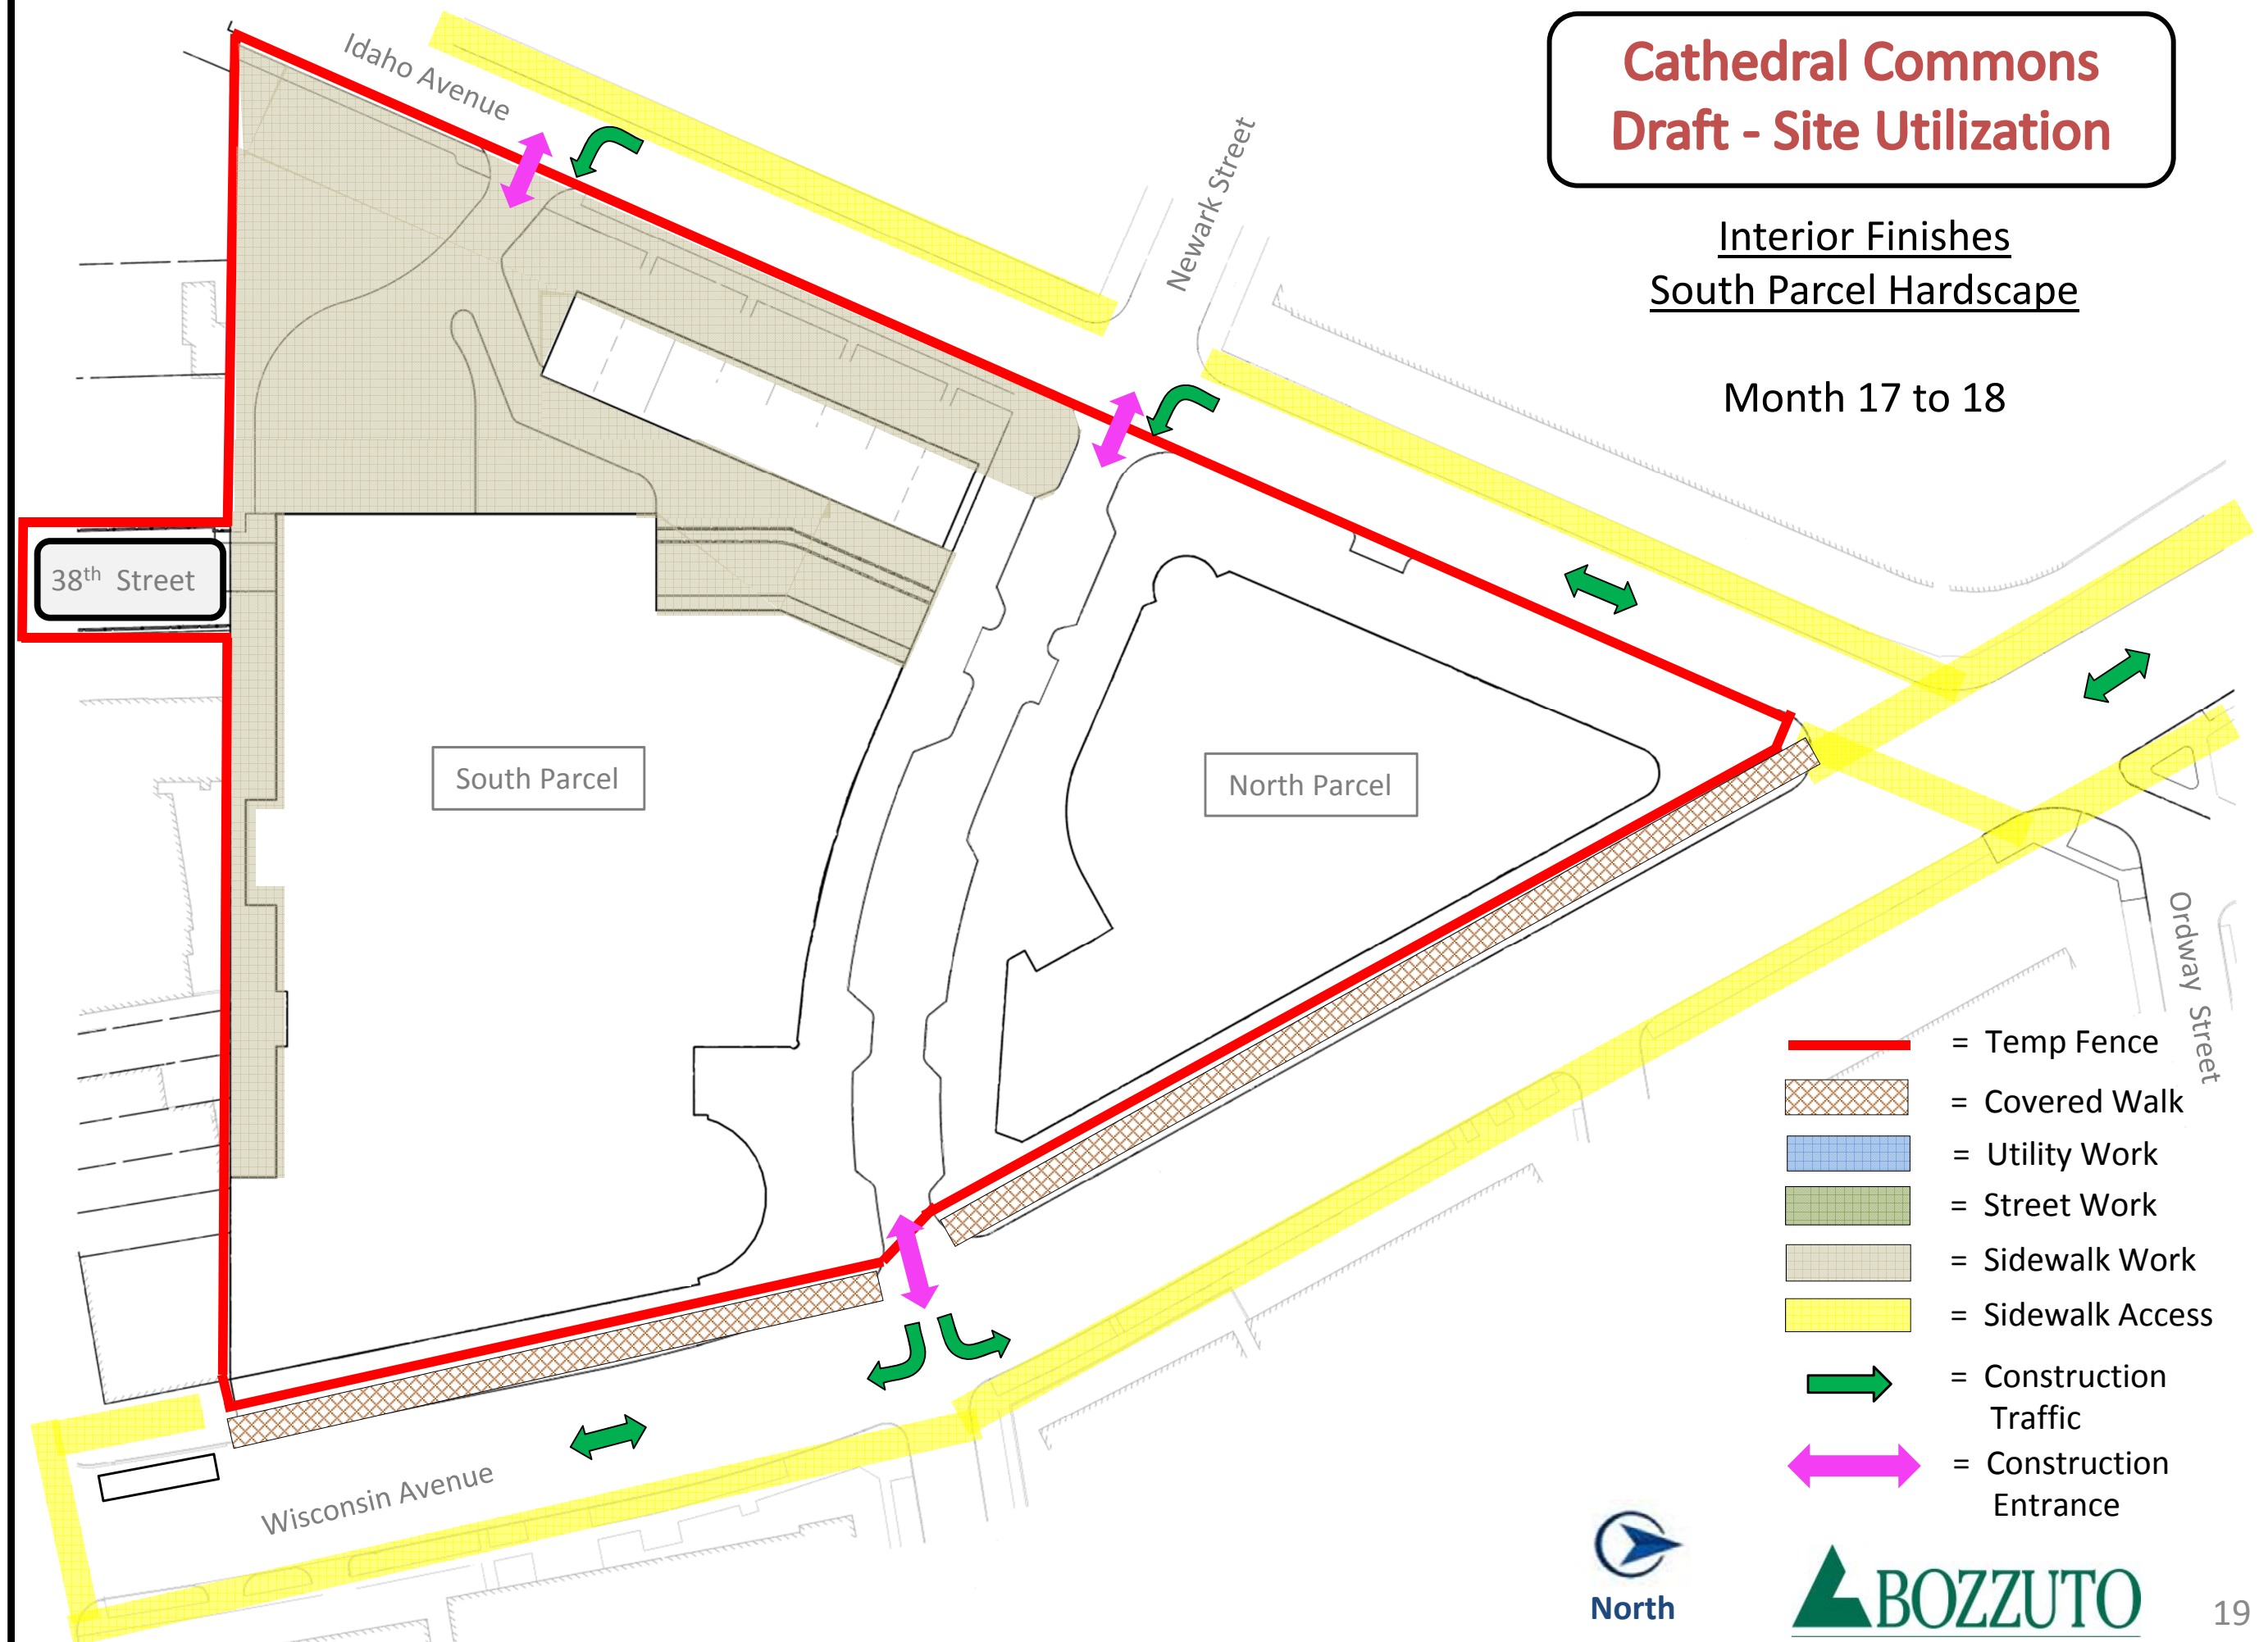

# Cathedral Commons Draft - Site Utilization

Interior Finishes  
South Parcel Hardscape  
North Parcel Hardscape

Month 19 to 20

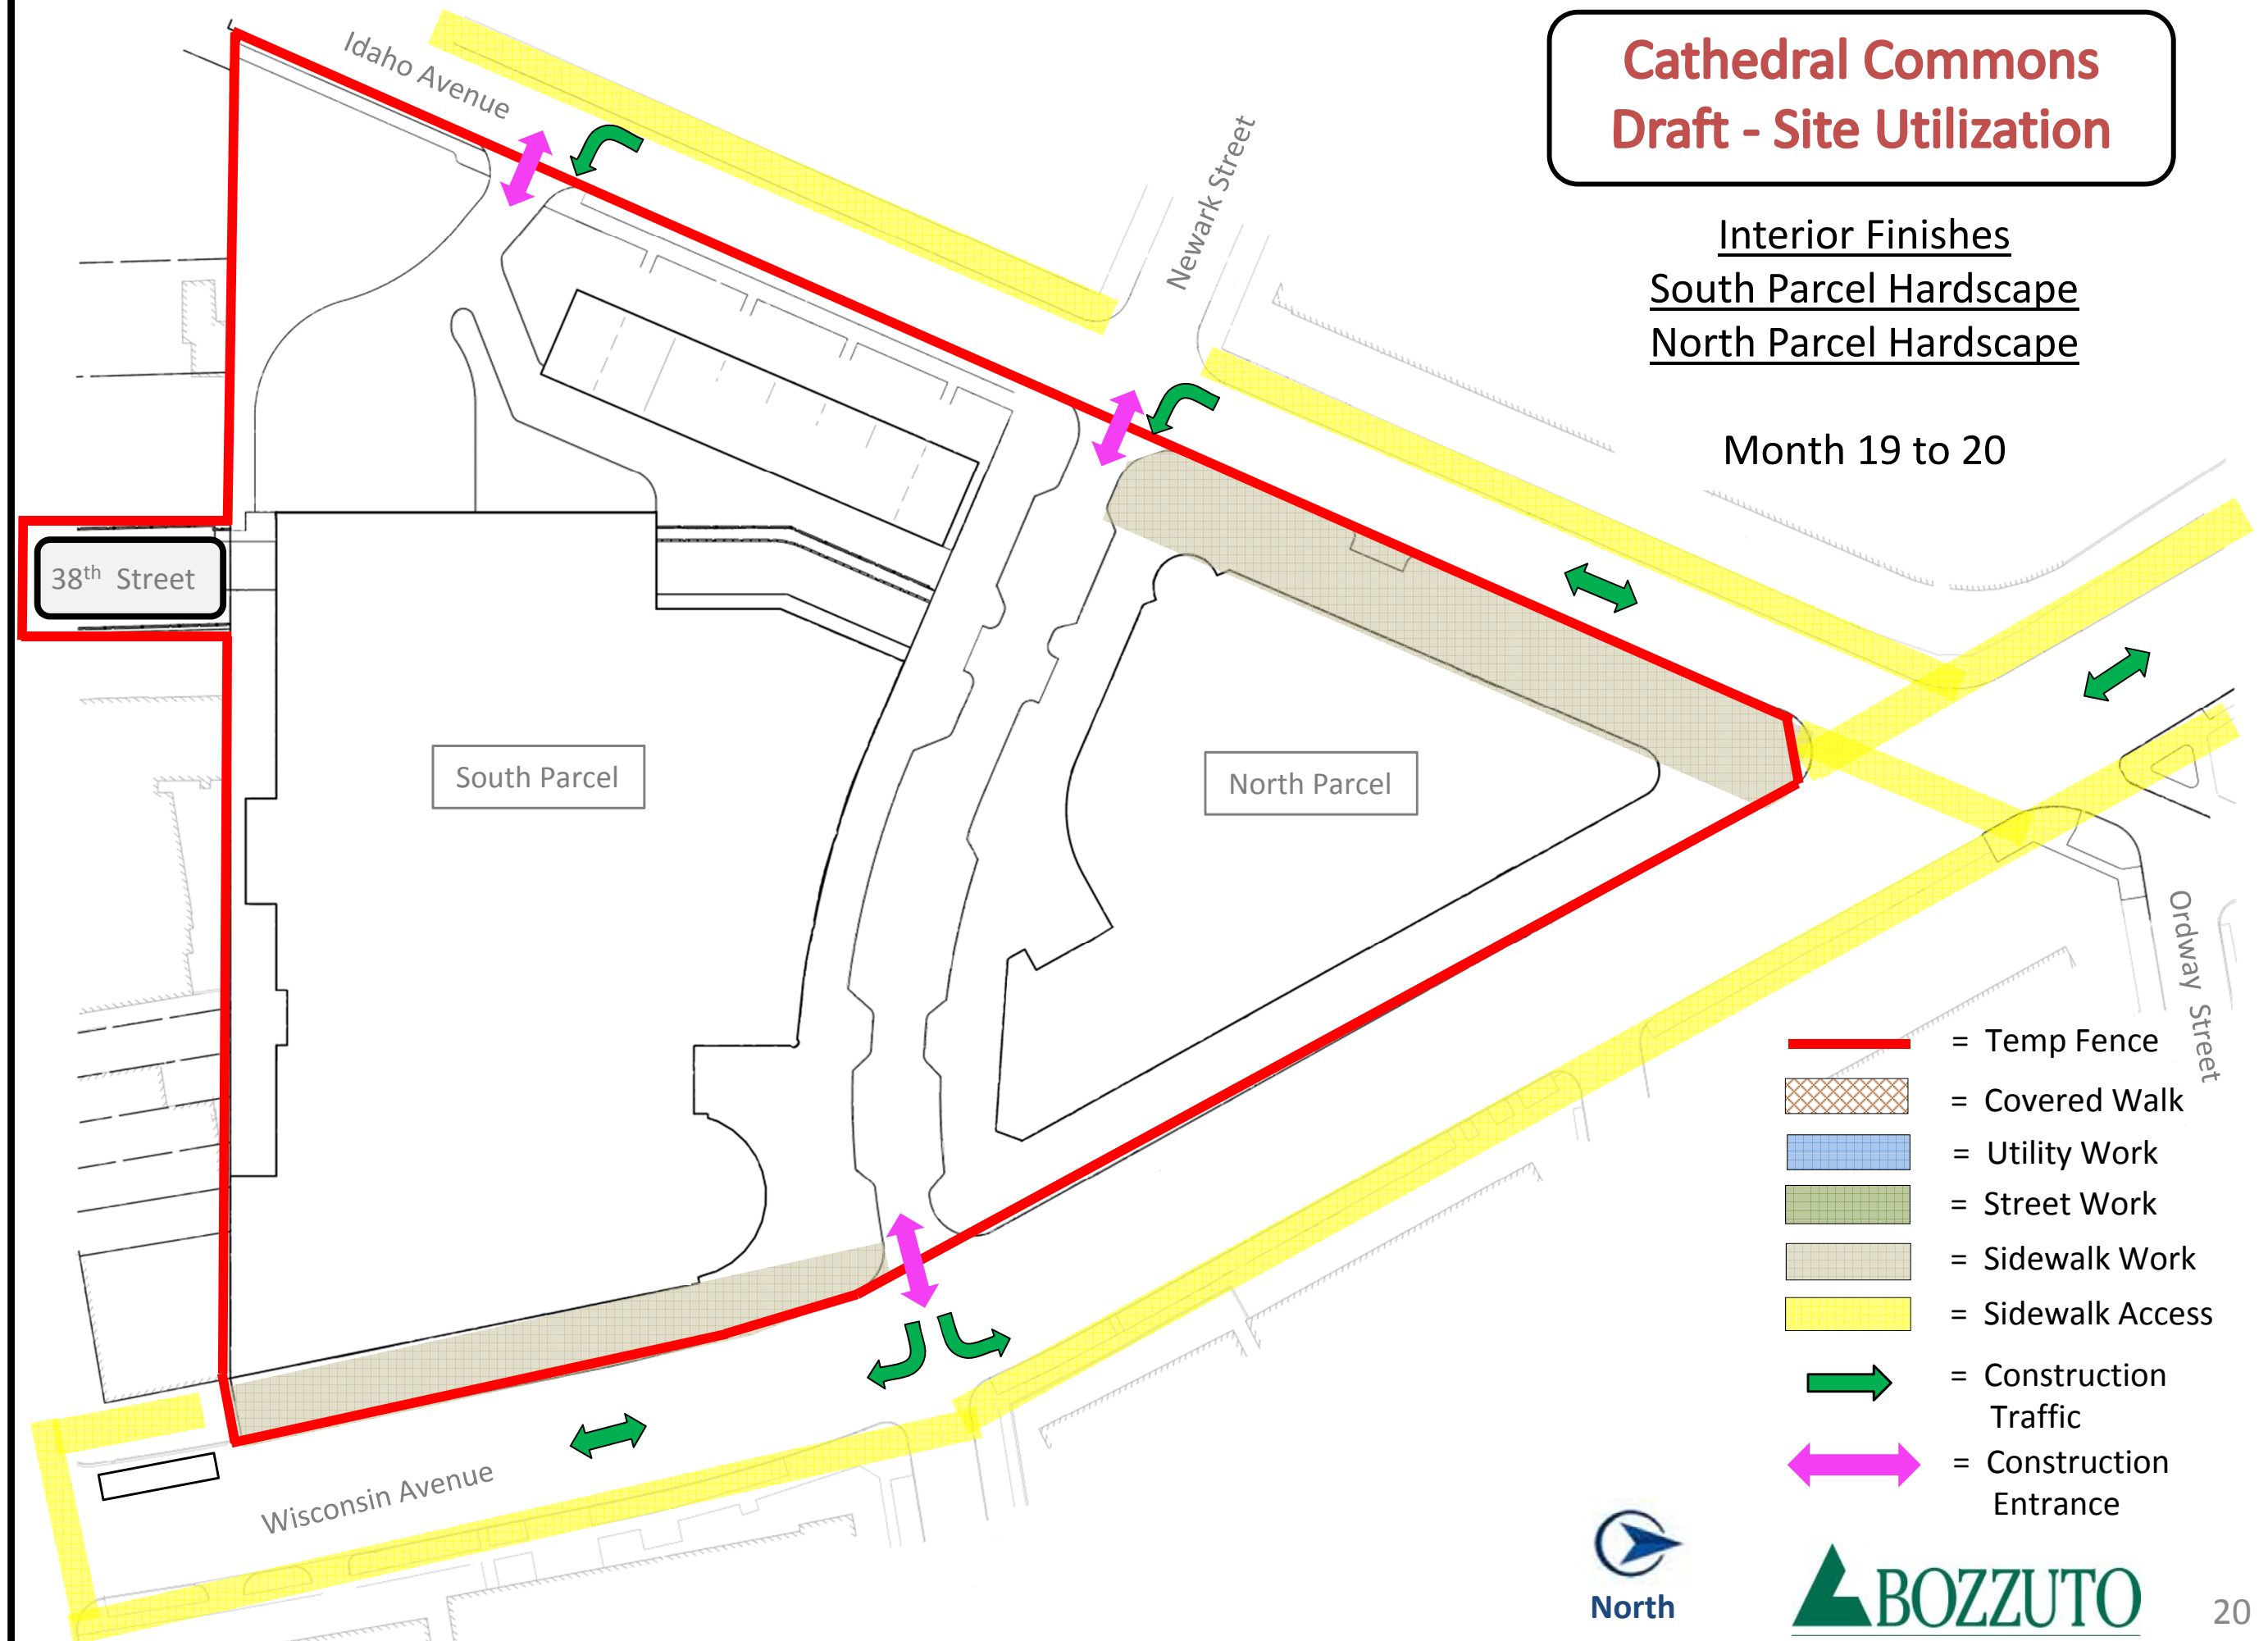




# Cathedral Commons Draft - Site Utilization

Interior Finishes  
South Parcel Hardscape  
North Parcel Hardscape


Month 20 to 21

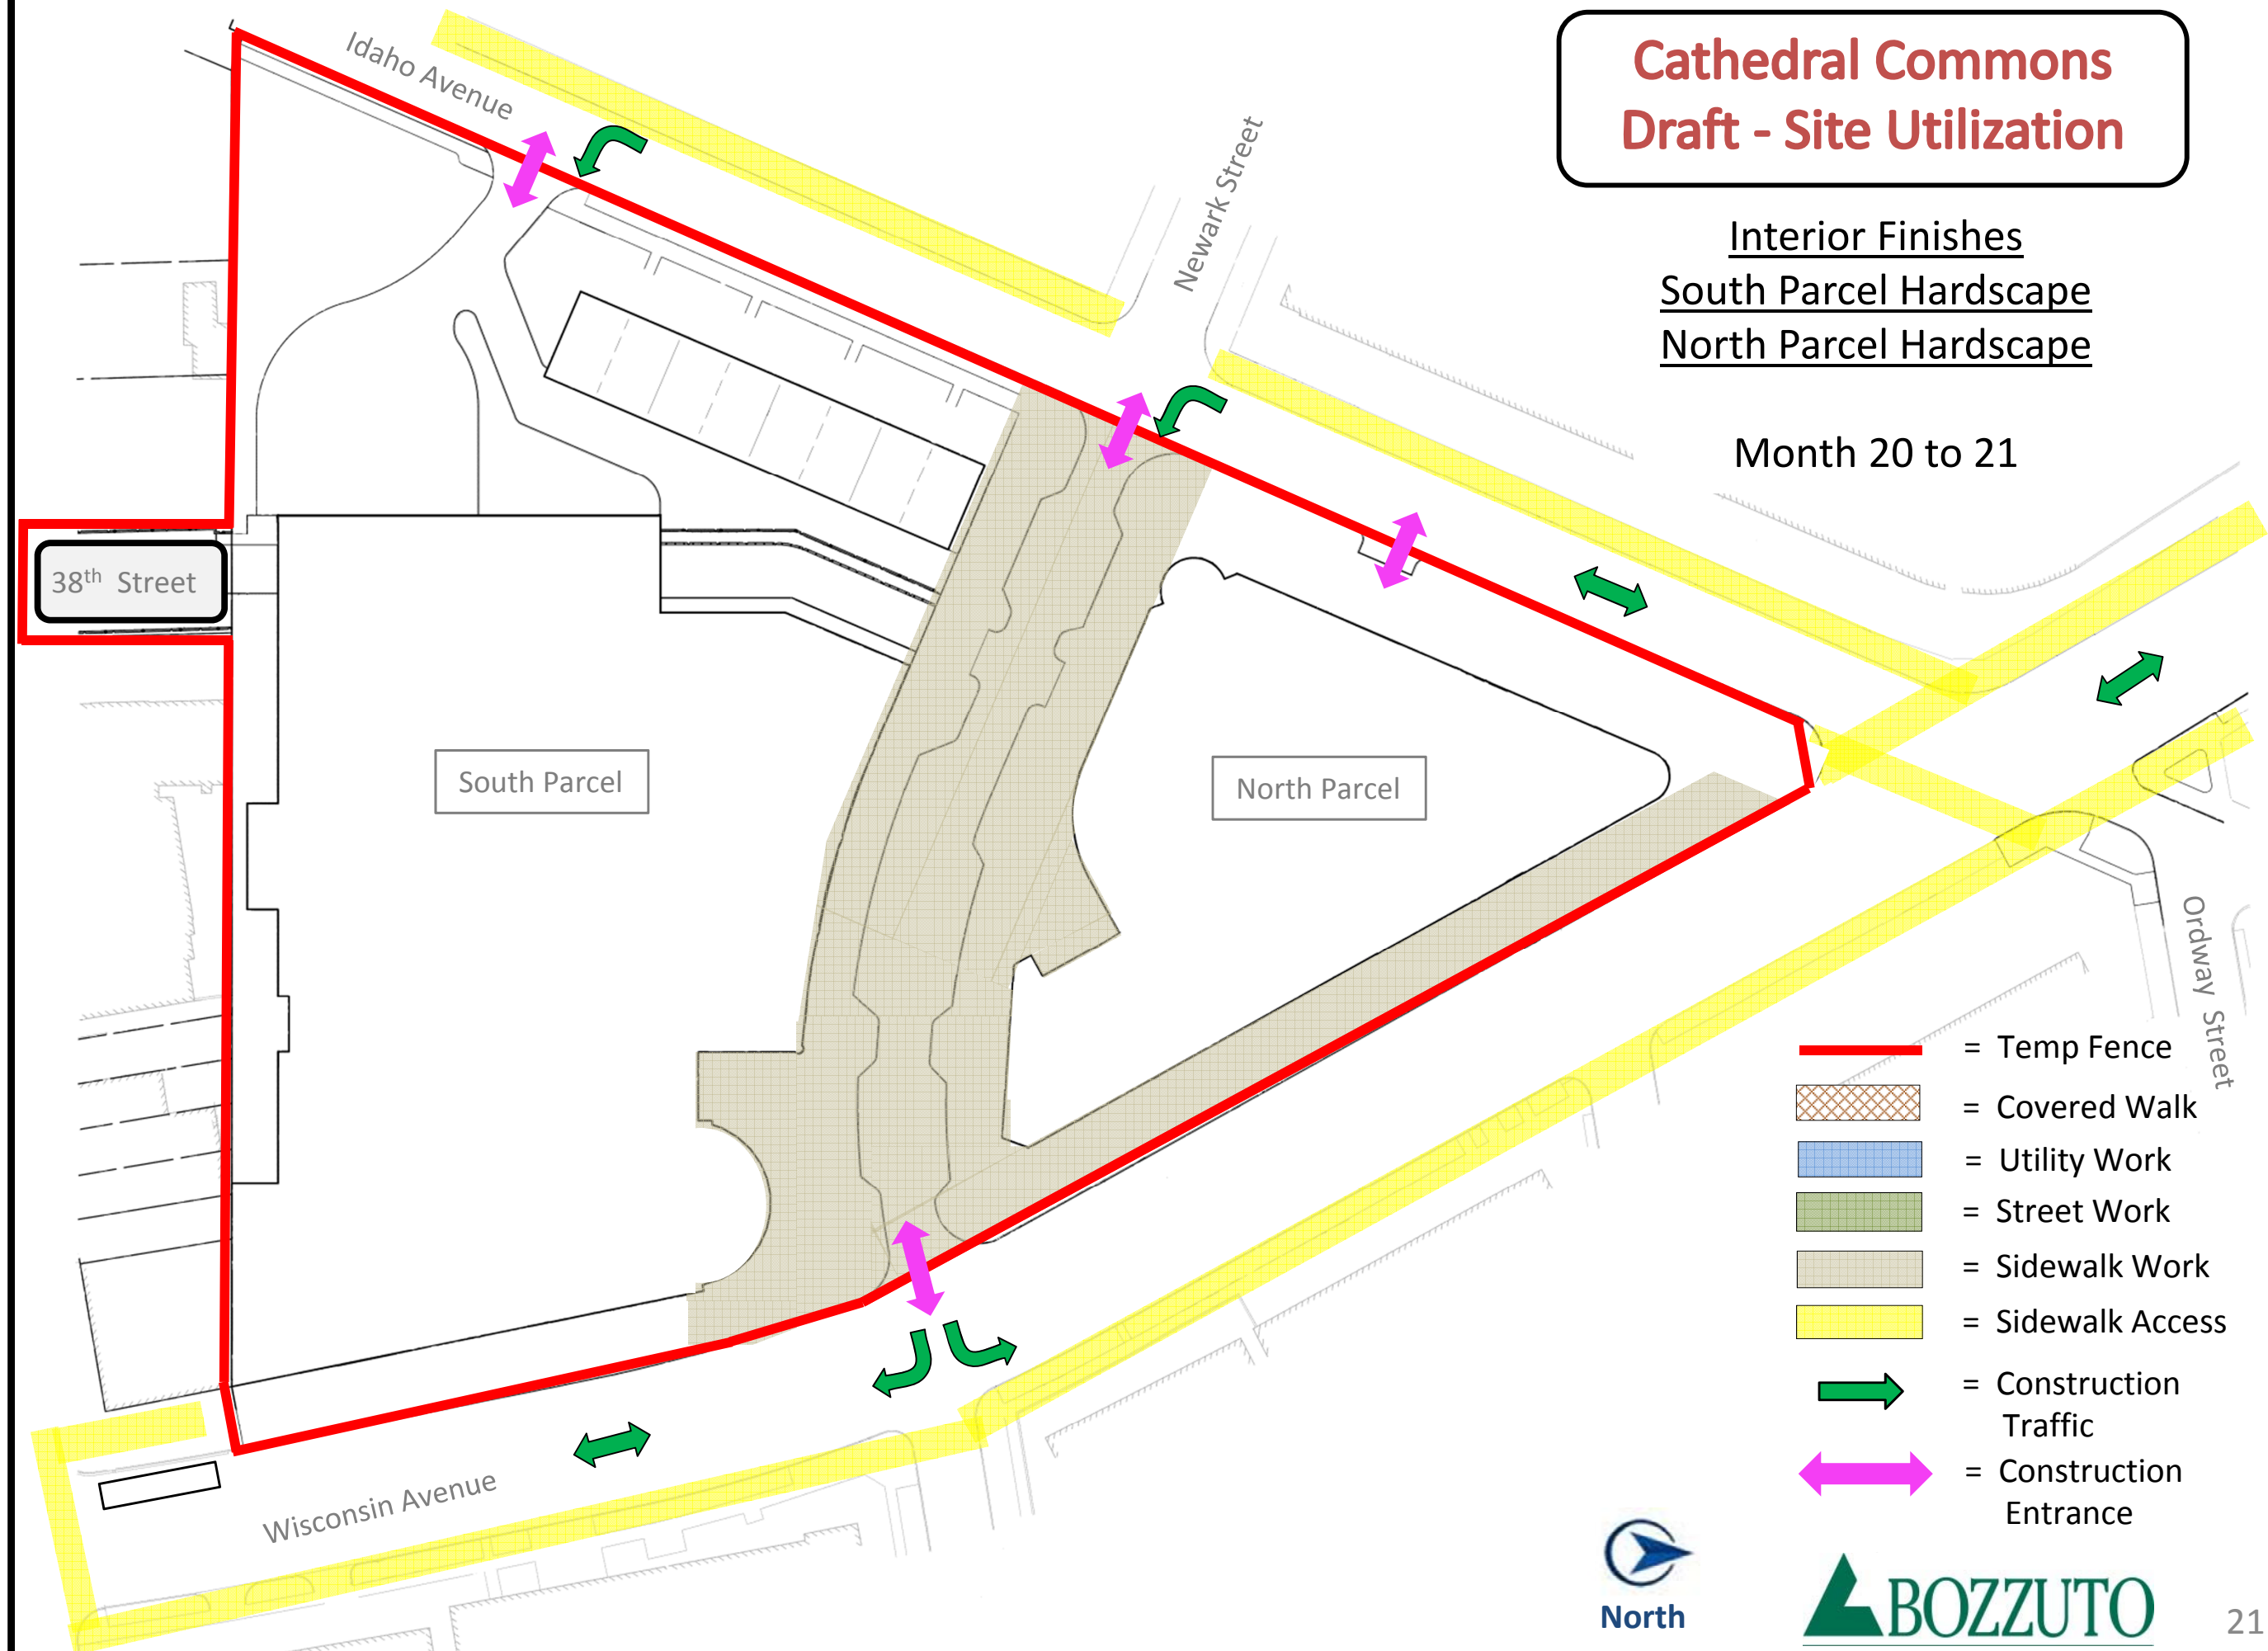

# Cathedral Commons Draft - Site Utilization

Interior Finishes  
North Parcel Hardscape – Phase 1

Month 20

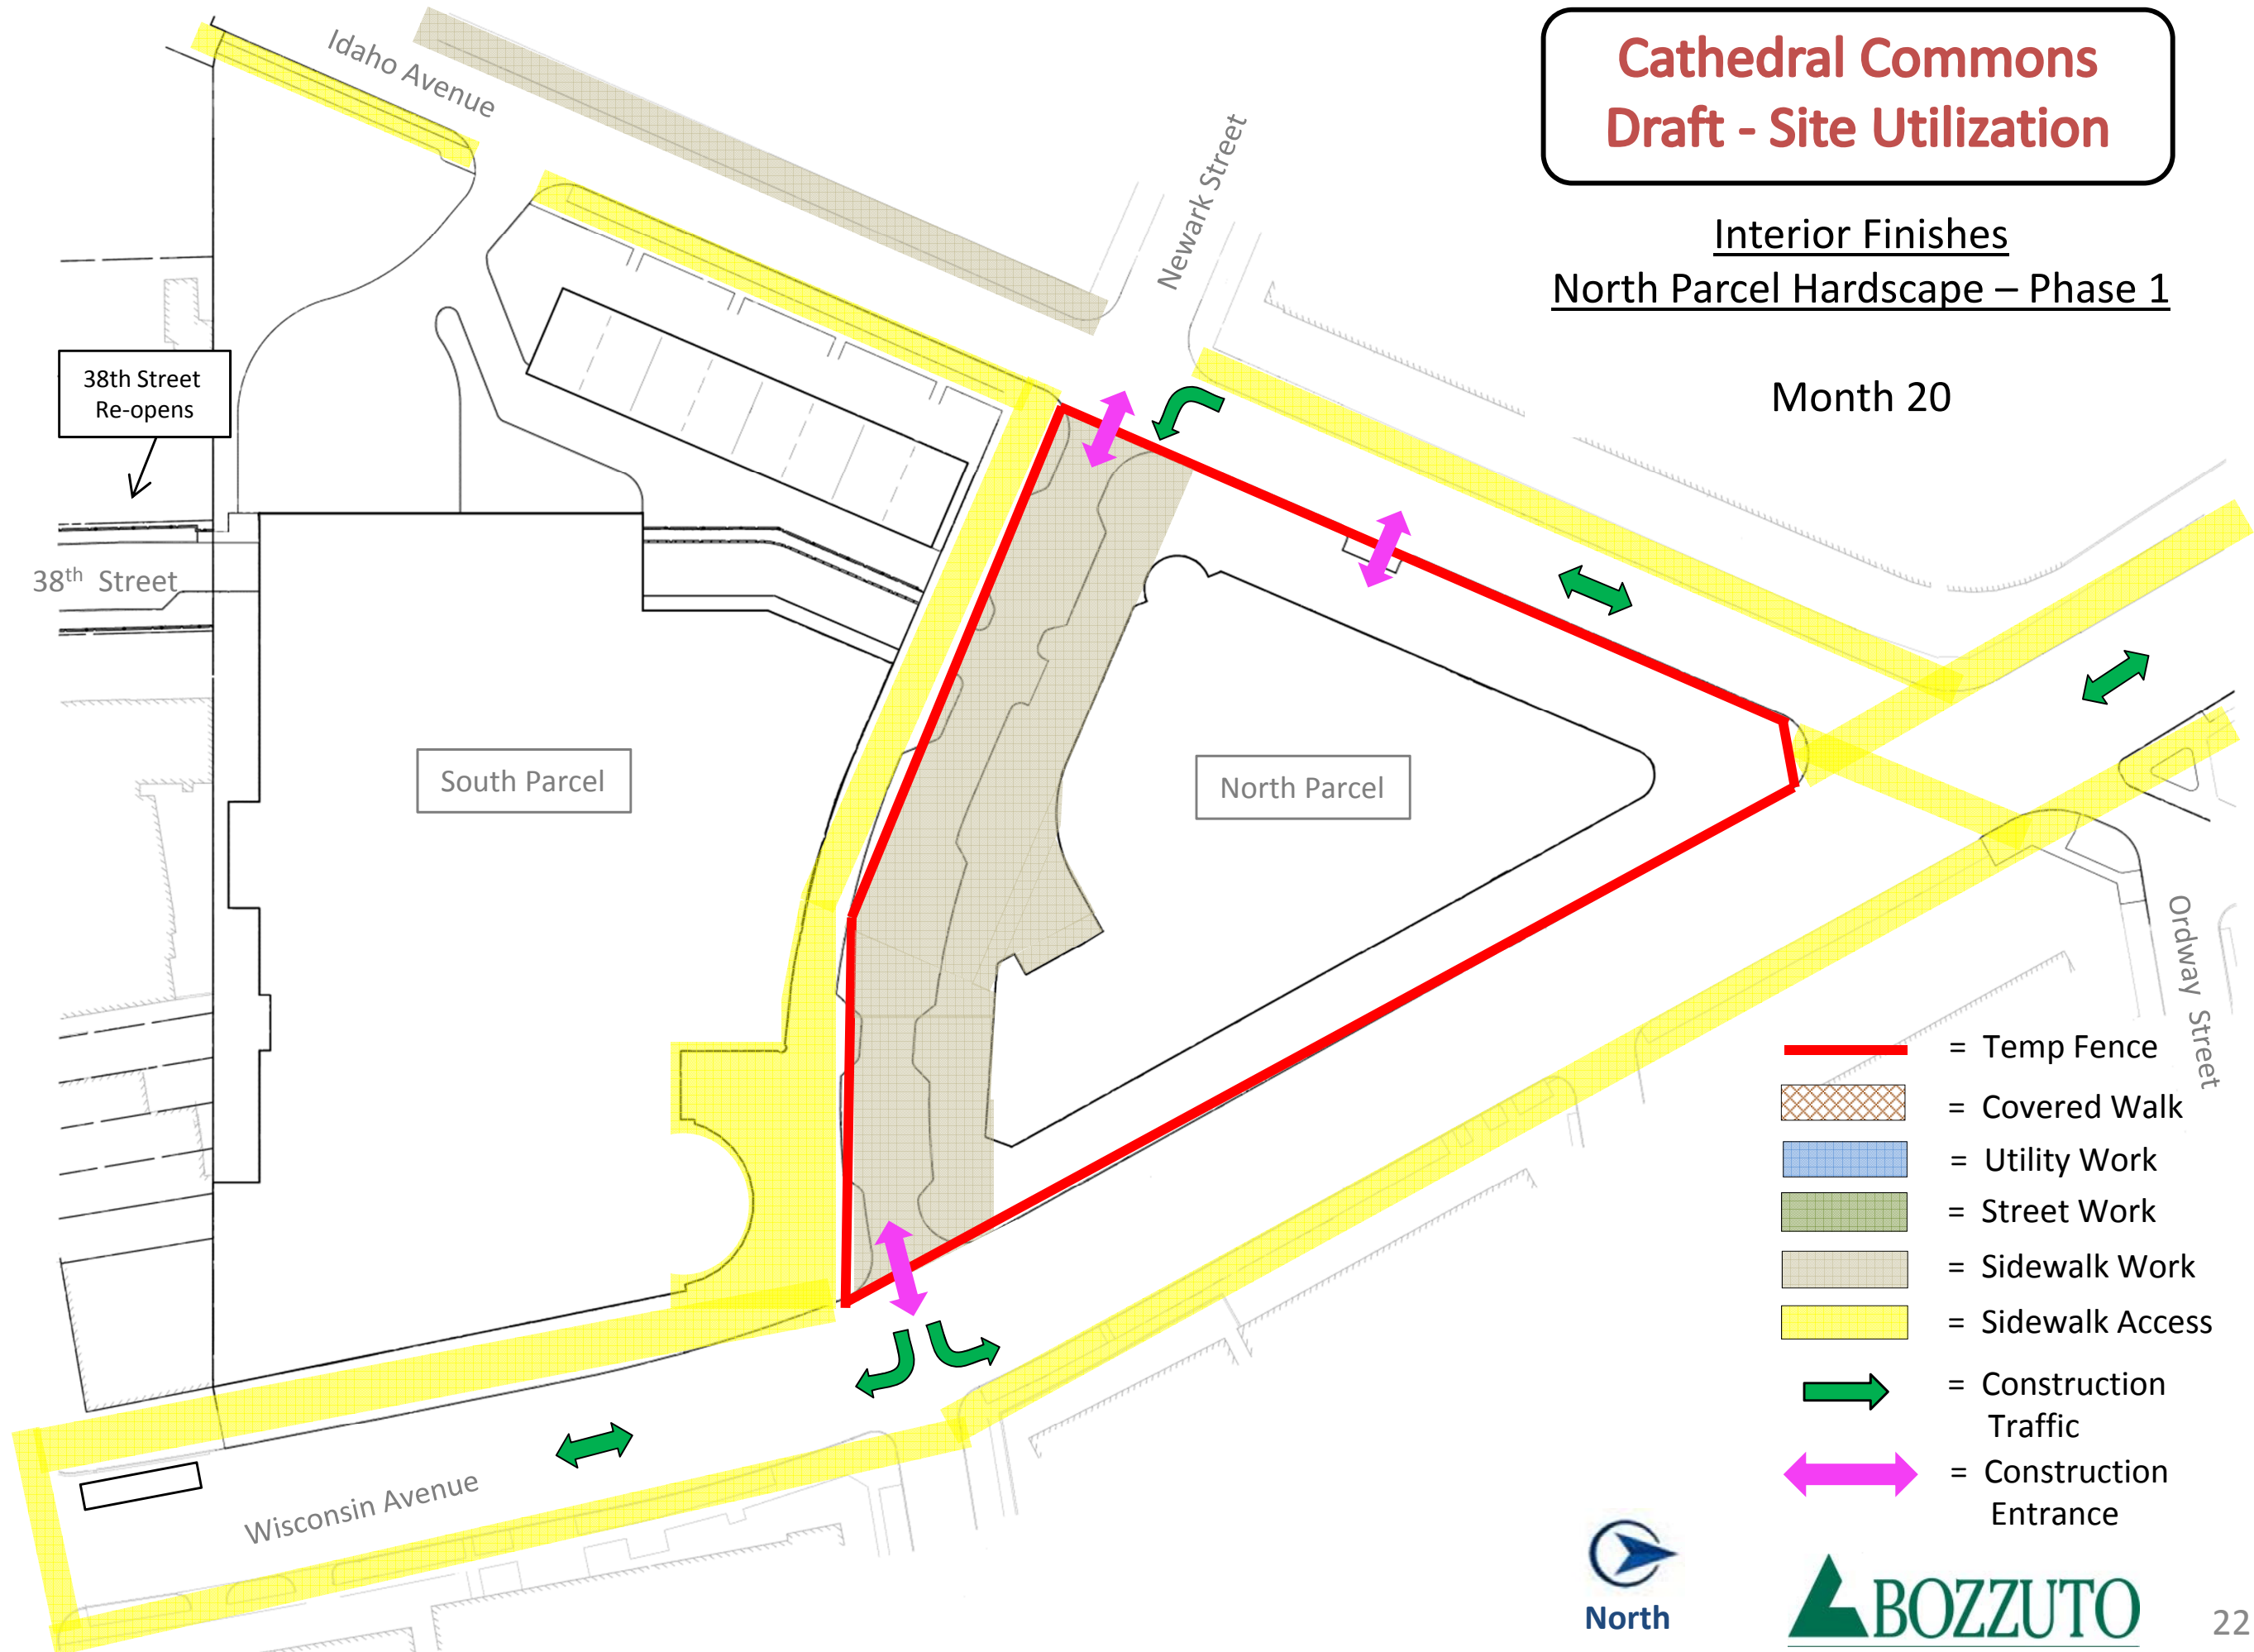


- = Temp Fence
- = Covered Walk
- = Utility Work
- = Street Work
- = Sidewalk Work
- = Sidewalk Access
- ➡ = Construction Traffic
- ↔ = Construction Entrance

# Cathedral Commons Draft - Site Utilization

Interior Finishes  
North Parcel Hardscape – Phase 2

Month 21

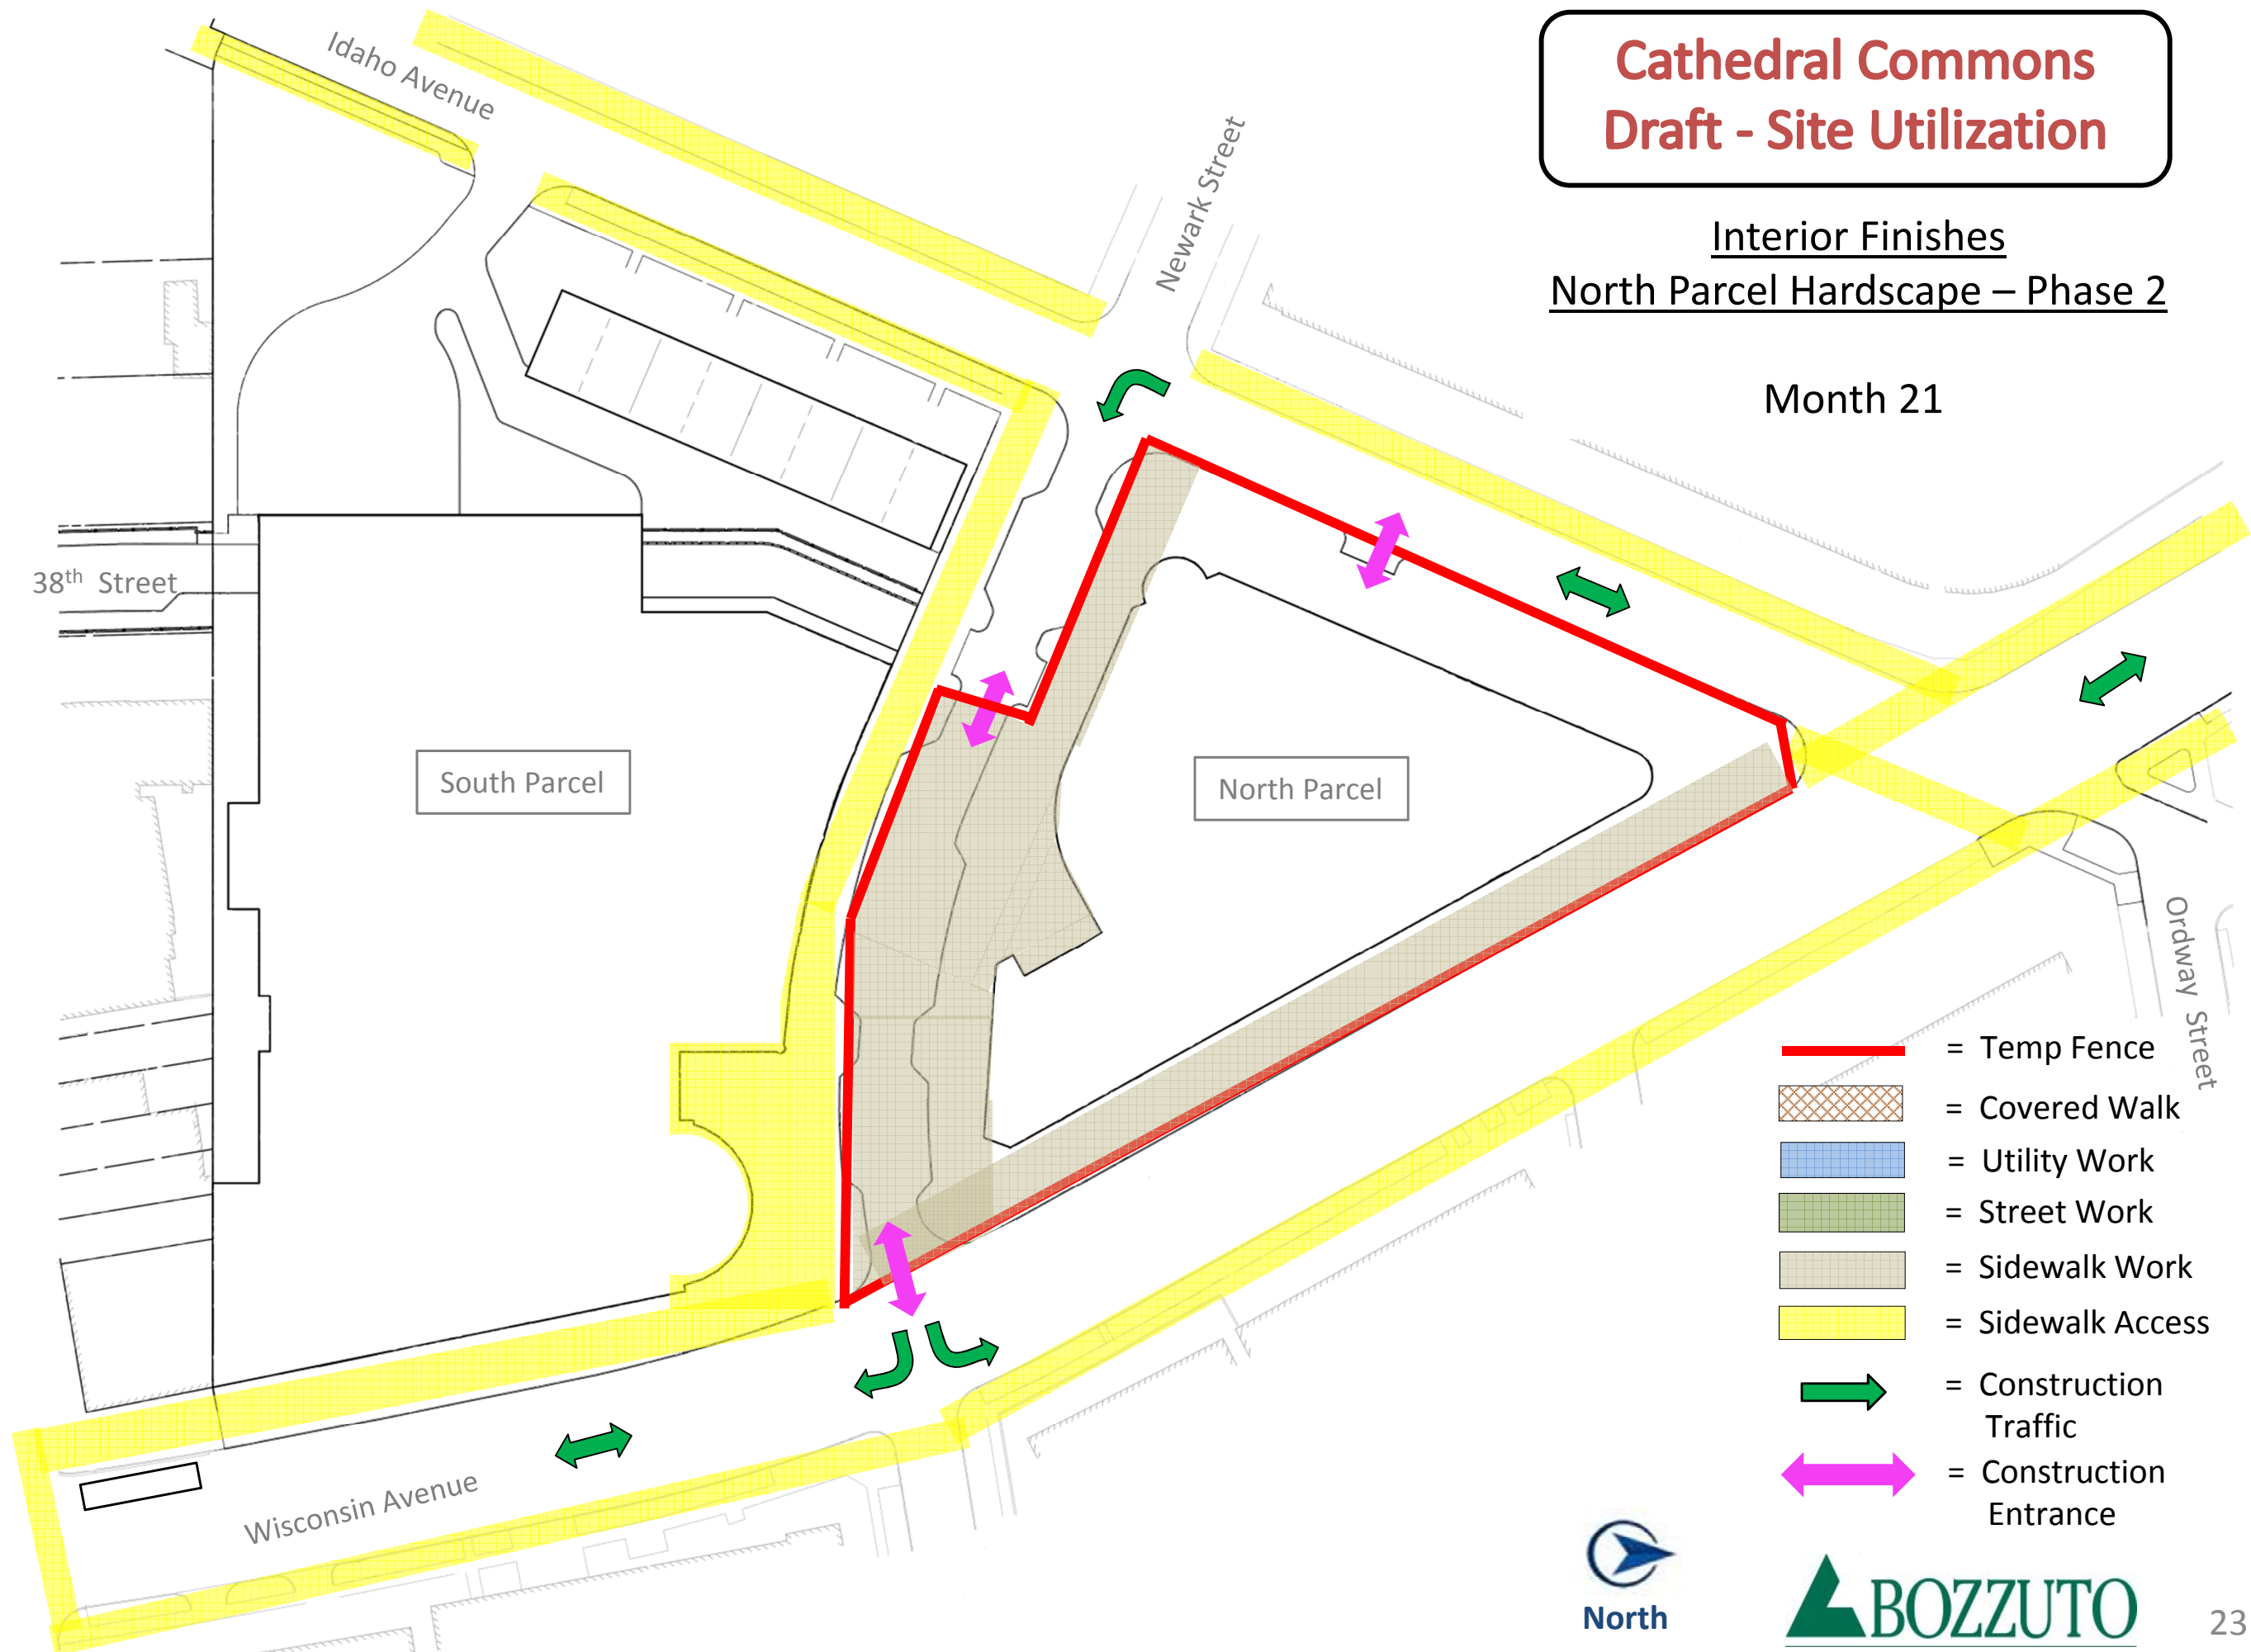




# Cathedral Commons Draft - Site Utilization

Interior Finishes  
North Parcel Hardscape – Phase 3

Month 21

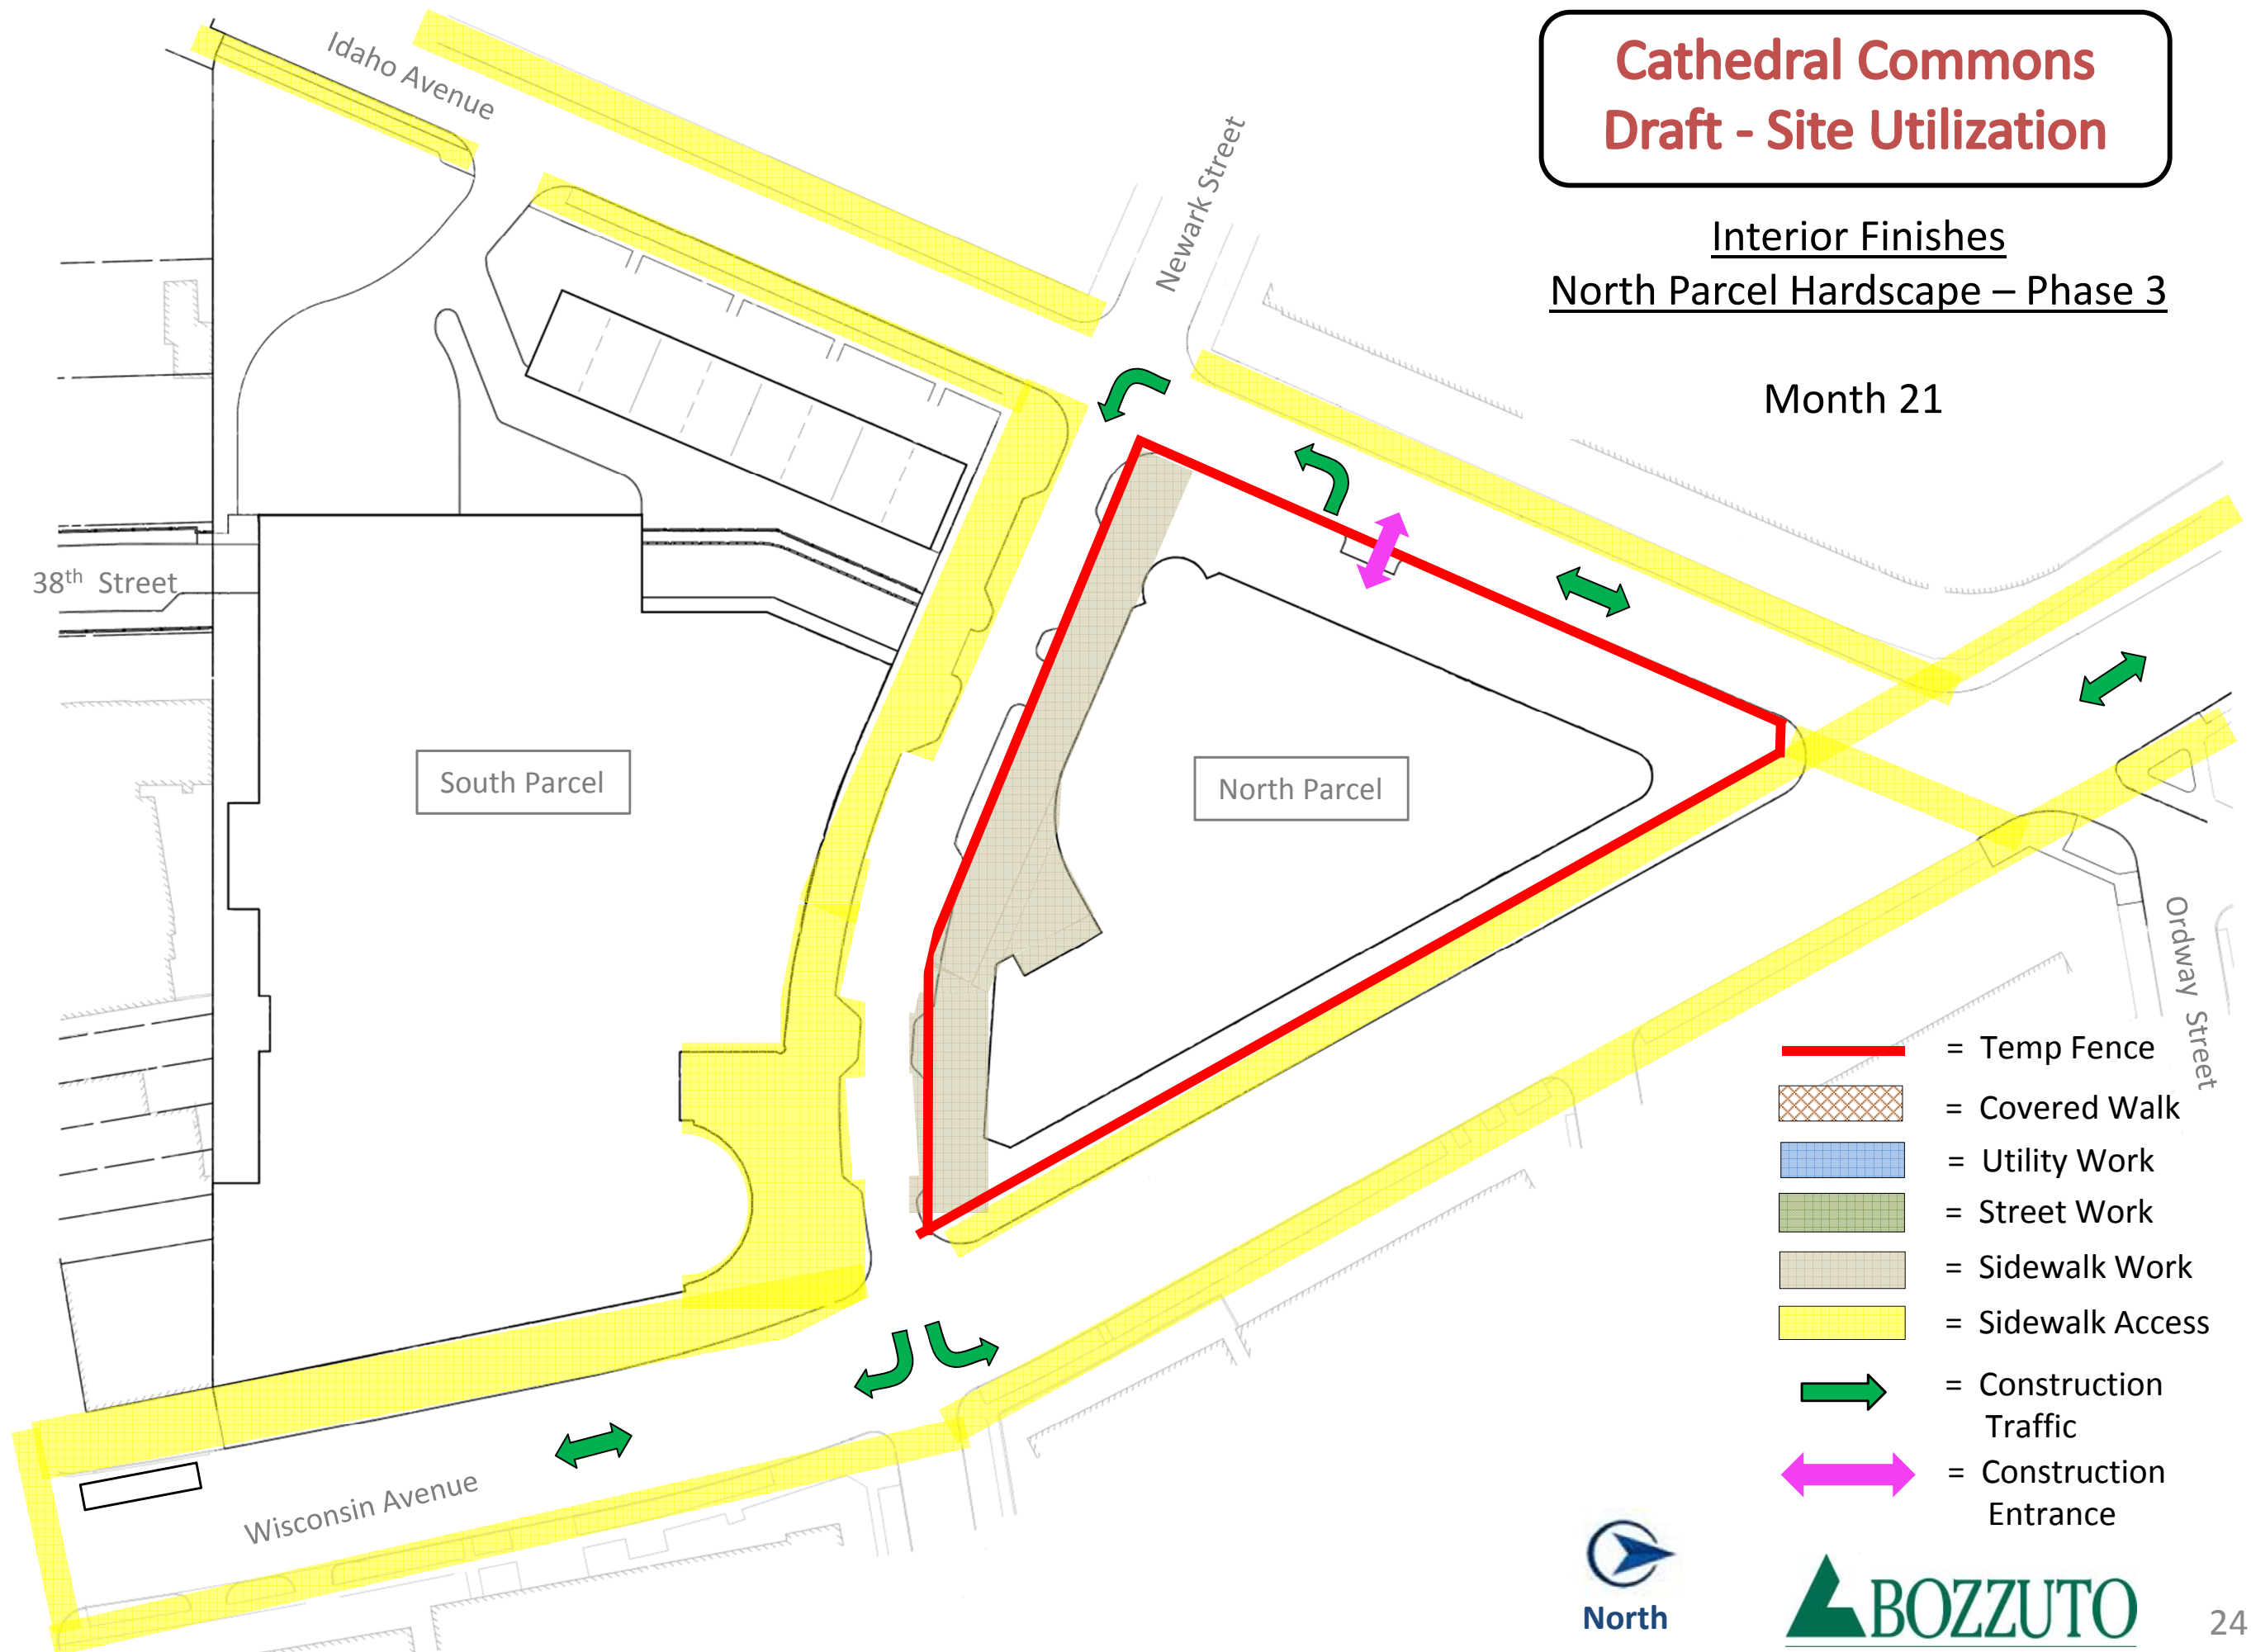

# Cathedral Commons Draft - Site Utilization

Substantially Complete

Month 23

